




o/c

RG04044753IN ITR:827104044753
RL DAHEJ SO (392130)
Counter No:2,26/06/2021,10:52
To:C P C BOARD ,VADODRA
PIN:390023, Subhanpura SO
From:BEIL INFRASTRUCTURE LTD,DAHEJ
Wt:1340gms
Amt:355.00(Cash)
(Track on www.indiapost.gov.in)
(Dial 1800266888) (Clear Postage, Star Rate)



RG04044749IN ITR:827104044749
RL DAHEJ SO (392130)
Counter No:2,26/06/2021,10:52
To:THE DIRECTOR ,BHOVAL
PIN:462016, R.S.Nagar S.O
From:BEIL INFRASTRUCTURE LTD,DAHEJ
Wt:1380gms
Amt:362.00(Cash)

Ref.: BEIL/DHJ/2021-22/15

To,
The Director
Ministry of Environment, Forest & Climate Change
Western Region Office,
Kendriya Paryavaran Bhavan,
Link Road No.3, E-5 Ravishankar Nagar
Bhopal-462016

Sub.: Half yearly compliance report of two EC's for Common Treatment, Storage, Disposal facility (TSDF) & Multi Effect Evaporator (MEE) and Installation of two incinerators & capacity enhancement of existing landfill. period Oct'20 to Mar'21.

- Ref.:**
1. Environmental Clearance No. SEIAA/GUJ/EC/7(d)/227/2013 dated 22nd July,2013 for setting up of common hazardous waste Treatment, Storage, Disposal facility (TSDF) and Multi Effect Evaporator (MEE)
 2. Environmental Clearance No. IA/GJ/MIS/55789/2016 dated 11th June, 2018 for Installation of two incinerators and capacity enhancement of Existing Landfill Facility

Dear Sir,

BEIL is operating a TSDF facility consisting of a secured land fill Facility and Multi Effect Evaporator (MEE) followed by spray dryer located at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist.Bharuch,Gujarat.

We are submitting here with the half yearly Compliance status report of both the above referred Environment Clearances for period October 2020 to March 2021. With this, we would also like to inform that EC no. IA/GJ/MIS/55789/2016 dated 11th June, 2018 for Installation of two incinerators and capacity enhancement of existing Landfill has not been implemented till date. However, planning stage is complete, and we have received CTE No 164667 on 24.12.2019.

BEIL has received and disposed land fillable Hazardous waste: During 1st October 2020 to 31st March 2021 is 137512.724 MT. Cumulative quantity disposed in landfill from the beginning (up to 31.03.2021) is 583331.347 MT.

Handwritten signature
22-6-2021
Post Box
Gujarat Pollution Control Board
BHARUCH

1.Compliance Status of Environmental clearance for setting up of a common hazardous waste treatment, storage, disposal facility (TSDF) and Multi Effect Evaporation (MEE) plant at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch by M/s BEIL Infrastructure Limited for Period Oct'20 to Mar'21.

EC File No.: SEIAA/GUJ/EC/7(d)/ 227/2013 dated 22nd July 2013

Sr. No	EC Conditions Details	Status
1.	The proposal is for Environmental Clearance for M/s, Bharuch Enviro Infrastructure Limited (BEIL) for setting up of a common hazardous waste Treatment, Storage, Disposal Facility (TSDF) and Multiple Effect Evaporation (MEE) Plant at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch. M/s, BEIL Infrastructure Ltd. (BEIL) proposes to set up TSDF (14 Lac MT) and MEE Plant (3*200KL/day) at Plot No. D-43, Dahej Industrial Estate, Dist. Bharuch. The proposal falls under project / activity no. 7(d) in the Schedule of the EIA Notification, 2006.	Complied We have started landfill activity from 29.04.2015. The solid waste receipt is streamlined for cell-1 (Capacity-1,28,000 MT), cell - 2 & 5 (Capacity - 2, 39, 640 MT, In operation), cell – 3 (Capacity – 1,32,769), Cell – 4 (Capacity – 1,35,705). Total 583331.347 MT of Landfillable Hazardous waste is received and disposed till March 2021. MEE Plant of Capacity 200 KLD has been installed and commissioned in May 2017.We have received CCA-Amendment No: - AWH-89413 dated 16.12.17.
2	The proposed project falls under category 7(d) of the schedule of the EIA Notification, 2006. As the proposed project is situated in the industrial area, which is not notified, it falls in Category B as per the schedule of the EIA Notification-2006.	Noted
3	The project activity is covered in 7(d) and is of 'B' Category, Since, the proposed project is located in the industrial area, which is not notified, public consultation is required as per paragraph 7(i) (III) (i) (b) of the Environment Impact Assessment Notification-2006. Public hearing of the project was conducted by the GPCB on 05/04/2013 at 11:30 Hrs. At P.J. Chheda JantaVidyalay, Dahej, Tal. Vagra, Dist. Bharuch	Noted
4	The SEAC, Gujarat had recommended to the SEIAA, Gujarat, to grant the Environment Clearance to this project for the above-	Noted

	<p>mentioned project. The proposal was considered by SEIAA, Gujarat in its meeting held on 22/07/2013 at Gandhinagar. Since the public consultation is required for the project, the SEIAA hereby accords Environmental Clearance to above project under the provisions of EIA Notification dated 14th September 2008 subject to the compliance of the following conditions.</p>	
--	---	--

SPECIFIC CONDITIONS:

Sr. No.	Description	Status
1.	<p>Ground water table at the project site shall be ascertained through the GWRDC before initiating construction of secured landfill site. The depth of the secured land fill site shall be decided based on the ground water level at the site and bottom of the secured landfill site shall be kept at least 2 m above the ground water table.</p>	<p>Complied.</p> <p>Ground water table at the project site has been ascertained through the GWRDC before initiating construction of secured landfill site. The depth of the secured land fill site has been decided based on the ground water level at the site and bottom of the secured landfill site, which is 7.5 (> 2 m) meter above the ground water table.</p> <p>Report of GWRDC is attached as ANNEXURE 1.</p>
2	<p>Construction of the secured landfill site shall be undertaken meticulously keeping in view the existing natural drainage pattern of the site to ensure that the natural drainage is not affected. All construction designs/drawings relating to the proposed landfill site must have approvals of reputed institutes like NPC/IIT</p>	<p>Complied.</p> <p>Construction of the secured landfill site has been undertaken meticulously keeping in view the existing natural drainage pattern of the site ensuring that the natural drainage is not affected. All Construction design/ drawings relating to the proposed landfill site are approved from IIT, Delhi. Drawings approved by IIT; Delhi are attached as ANNEXURE 2.</p>
3	<p>The proponent shall ensure that design and construction of secured landfill site is as per the guidelines of CPCB with proper leachate collection arrangement.</p>	<p>Complied.</p> <p>We have ensured that design and construction of secured landfill site is as per guidelines of CPCB with proper leachate collection arrangement. Summary of the CPCB guidelines compliance has attached as ANNEXURE 4.</p>
4	<p>The proponent shall ensure that the transportation of the Hazardous wastes to the TSDF conforms to the</p>	<p>Complied.</p> <p>We have ensured that the transportation of the</p>

	norms laid down in the Hazardous Wastes (Management, Handling, and Transboundary Movement) Rules 2008	hazardous wastes to the TSDF confirms to the norms laid down in the hazardous and other waste (Management and Trans boundary Movement) rules 2016 and its subsequent amendments i.e. licensed and trained drivers, close and hydraulic dumpers, GPS enabled dumpers etc. Total Approved 170 dedicated vehicles equipped with GPS system are being used for Transportation of Hazardous waste from member Industries to TSDF.
5	Project proponent shall ensure that wastes with organic content >5% of degradable organic matters are not disposed into the landfill. How-ever required arrangement for collection, treatment and disposal of gases from the secured landfill if any shall be provided.	Complied. We are carrying out finger-print analysis of every truck load of waste received at site. We ensure that waste with organic content >5% of degradable organic matters are not disposed into landfill. Comprehensive analysis is being carried out at the time of enrolling members. If organic content is high, the waste is sent for incineration at BEIL Ankleshwar site. Only inorganic-waste or waste meeting acceptance criteria, is sent to landfill. Required arrangements for collection, treatment, and disposal of gases from the landfill is provided. Typical reports of finger-print analysis of solid waste are attached as ANNEXURE 5 .
6	The TSDF & MEE shall only handle the waste generated from the member units.	Complied. The waste generated from members of BEIL is only accepted who have valid CC&A obtained from GPCB. At present we are having 805 members for Landfill at BEIL. In support of this we are submitting returns to GPCB.
7	The project Proponent shall set up necessary facility for onsite testing of wastes to decide the requirement of treatment if any before disposal.	Complied. We have set up a Laboratory with all the required facilities for onsite testing of wastes to decide the requirement of treatment (Stabilization/Neutralization/Solidification) if any before disposal.
8	Project Proponent shall carryout periodical ground water/soil monitoring to and around the site to check the contamination including TCLP test for heavy metals	Complied. Company is carrying out internally and through third party regular monitoring of Ground water (twice in a month – Internally and monthly by External party). soil monitoring is carried out

annually through third Party in and around the site. In soil monitoring heavy metals are checked by TCLP test & its results are also attached. All the parameters are well within the limit. The monitoring results of ground water & soil conducted by third party are attached as **ANNEXURE 6.**

Summary Table: Ground Water (Oct'20 to Mar'21)

Sr . No.	Parameter	Unit	Average of Up-stream borewell	Average of down-stream	Average of outside premises
1	Colour	Co-Pt	12.42	10.27	4.96
2	pH	-	7.53	7.45	7.76
3	Conductivity	mmhos/cm	54.86	51.64	0.74
4	Turbidity	NTU	1.33	1.14	0.35
5	TSS	mg/lit	9	7.17	ND
6	TDS	mg/lit	35813	33965	506.39
7	TOC	mg/lit	12.67	10.5	ND
8	COD	mg/lit	79.83	70.33	ND
9	Chloride	mg/lit	17025.67	16121	148.5

Summary Table: Soil Analysis (Oct'20 to Mar'21)

Sr No	Parameters	pH	Conductivity (umh o/cm)	TDS (%)	TOC (%)
1	Nr EB-1	8.63	2176	1.18	0.84
2	Opp Salt Farm	8.54	4451	1.95	0.78
3	Nr EB-2	8.7	1879	1.10	0.45
4	Opp. Khetan Ind	8.27	3180	1.54	0.49
5	Nr ADM	8.34	1746	1.05	0.56
6	Behind Tegros	8.91	2840	1.25	0.93

Sr No	Parameters	Lead (mg/l)	Copper (mg/l)	Mercury (mg/l)	Nickel (mg/l)
1	Nr EB-1	0.36	0.43	ND	0.89
2	Opp. Salt Farm	0.48	0.40	ND	0.77
3	Nr EB-2	ND	0.37	ND	0.52
4	Opp. Khetan Ind	0.24	0.32	ND	0.59
5	Nr ADM	ND	0.24	ND	0.63
6	Behind Tegros	ND	0.39	ND	0.72

9 The thirds party assessment on functioning of the TSDF and MEE shall be carried out through a reputed institute like NPC/IIT or any academic / research institute of similar reputation once in a year and mitigation measures as may be suggested by such institute shall be implemented in consultation with the Gujarat Pollution Control Board

Complied.
 We have constructed Cell#1, Cell# 2 & Cell# 5, Cell#3, Cell# 4 under IIT, Delhi's guidance. A third-party assessment on functioning of the TSDF & MEE is carried out by a GPCB appointed reputed academic Institute (Schedule -1 Auditors) every year. The recommendations and their compliance are submitted to GPCB every six months. Also, Expert from IIT, Delhi regularly visit the site and give us their report. These reports are submitted to GPCB.
 Auditor's recommendation & compliance submitted

		to GPCB and Latest report of IIT Inspection submitted to GPCB, are enclosed as ANNEXURE 3 .																																
A.1	Water:																																	
10	Fresh water requirement shall not exceed 350 KL/day and it shall be met only through water supply from the GIDC Metering of water shall be done and its records shall be maintained. No ground water shall be tapped for the project requirements in any case.	<p>Complied.</p> <p>Fresh water requirement is not exceeding 350 KLD and it is met through water supply from GIDC, records are maintained. No ground water is being tapped for the project requirement in any case.</p> <p>During Oct'20 to Mar'21, Average water consumption is @ 101.2 KLD. Summary of the same as below.</p> <table border="1"> <thead> <tr> <th>Sr. No</th> <th>Month</th> <th>Water Consumption (KL/ month)</th> <th>Average (KLD)</th> </tr> </thead> <tbody> <tr> <td>1</td> <td>Oct'20</td> <td>3412</td> <td>110.06</td> </tr> <tr> <td>2</td> <td>Nov'20</td> <td>3023</td> <td>100.77</td> </tr> <tr> <td>3</td> <td>Dec'20</td> <td>2334</td> <td>75.29</td> </tr> <tr> <td>4</td> <td>Jan'21</td> <td>2533</td> <td>81.71</td> </tr> <tr> <td>5</td> <td>Feb'21</td> <td>3085</td> <td>110.18</td> </tr> <tr> <td>6</td> <td>Mar'21</td> <td>4014</td> <td>129.48</td> </tr> <tr> <td></td> <td>Average</td> <td>3066.8</td> <td>101.2</td> </tr> </tbody> </table>	Sr. No	Month	Water Consumption (KL/ month)	Average (KLD)	1	Oct'20	3412	110.06	2	Nov'20	3023	100.77	3	Dec'20	2334	75.29	4	Jan'21	2533	81.71	5	Feb'21	3085	110.18	6	Mar'21	4014	129.48		Average	3066.8	101.2
Sr. No	Month	Water Consumption (KL/ month)	Average (KLD)																															
1	Oct'20	3412	110.06																															
2	Nov'20	3023	100.77																															
3	Dec'20	2334	75.29																															
4	Jan'21	2533	81.71																															
5	Feb'21	3085	110.18																															
6	Mar'21	4014	129.48																															
	Average	3066.8	101.2																															
11	A leachate collection system shall be provided to collect the leachates at a collection point. Leachate shall be pumped from leachate wells and shall be treated in in-house MEE. However, in the initial two – three year the leachate shall be sent to BEIL Ankleshwar for treatment with MEE.	<p>Complied.</p> <p>Leachate collection system is provided to collect the leachates at collection-points.</p> <p>There is planning to construct total 7 no. of leachate collection wells, from which 4 collection wells have been constructed for the cell 1, cell2 and cell5, cell3, cell4 and monsoon shed.</p> <p>In-house MEE was put up on 12.12.17 and thereafter leachate is treated in in-house MEE.</p> <p>During Oct'20 to Mar'21, Average Leachate treated in MEE, is @ 12.4 KLD. Summary of the same as below.</p>																																

		Sr. No	Month	Leachate generation (KL/ month)	Average (KLD)
		1	Oct'20	319.3	10.3
		2	Nov'20	303.6	10.1
		3	Dec'20	372.2	12.
		4	Jan'21	340.5	10.9
		5	Feb'21	298.6	10.6
		6	Mar'21	643.8	20.7
			Average	379.67	12.4
12	BEIL shall explore the possibilities for reuse of condensate water generated from MEE plant for landfill construction gardening and domestic purpose within the BEIL	Complied. Condensate water generated from MEE plant is being treated in the Effluent treatment plant having RO as tertiary treatment, then it is utilized for green belt development.			
13	Domestic wastewater and condensate water from the MEE shall be disposed-off as per the norms to be laid down by the GPCB	Complied. Soak pit & septic tank are provided to dispose domestic wastewater. Condensate water generated from MEE plant is being treated in the Effluent treatment plant and then it is used for green belt development.			
14	Enough care shall be taken to prevent any leakages/accidental spillages during conveyance of the effluent from the member units to the MEE	Complied. Enough care is being taken to prevent leakages/accidental spillages during conveyance of the effluent from the member units to the MEE. Transporters are registered to BEIL, dedicated vehicles with GPS enabled system, with trained drivers are transporting the effluent from the member units to the MEE.			
15	Separate electricity meter shall be provided at the MEE. A Proper operation logbook of the MEE containing records of quantities and qualities of leachate from secured landfill site and effluent received from the member units, energy consumption etc. Shall be maintained and furnished to the GPCB from time to time.	Complied. Separate electricity meter is provided at the MEE. A proper operation logbook of the MEE containing records of the quantities and qualities of leachate from secured landfill site and effluent received from the member units, energy consumption etc., are being maintained. These data are regularly submitted to GPCB in monthly patrak, protocols, environment audit reports and others from time to time.			

16	Storage Tank of adequate capacity shall be provided to hold effluent for at least 48 hours in the case of either maintenance of the MEE or disturbances in MEE operations.	Complied. Storage tanks of 450 KLD are provided to hold effluent in case of MEE maintenance.																								
17	In case of power failure standby DG set/s having power generation capacity equivalent to the requirement of power to run the MEE shall be installed, so that the MEE can be operated even in case of power failure	Complied. According to our requirement we have installed DG set of capacity 600 KVA.																								
A.2 AIR:																										
18	Natural gas to the tune of 440 Nm ³ /day shall be used as a fuel in Boiler (5 T/Hr) and a stack of 30 m height shall be provided to Boiler	Complied. A stack of 30 m height is provided to Boiler & FO is used as fuel in boiler. (6 T/Hr.)																								
19	HSD to the tune of 3KL/Month shall be used as a fuel in D.G. Set [600 KVA] and a stack of 9.3m height shall be provided to D.G. Set	Complied. HSD consumption is less than 3 KL/Month in DG Set (600 KVA) and a stack of 11 m height is provided to the DG set.																								
20	The Flue gas emission from Boiler and D.G. Set shall conform to the standards prescribed by GPCB. At no time emission levels shall go beyond the stipulated standards	Complied. We are monitoring DG set and boiler on monthly basis. The flue gas emission from DG set and boiler confirms to the standards prescribed by GPCB. At no time emission levels are going beyond the stipulated standards. Reports are attached as ANNEXURE 7 . Summary Table: DG Stack Analysis (Oct'20 to Mar'21)																								
<table border="1"> <thead> <tr> <th>Sr. No</th> <th>Parameter</th> <th>Min.</th> <th>Max.</th> <th>Avg.</th> <th>Permissible Limit</th> </tr> </thead> <tbody> <tr> <td>1</td> <td>SPM (Mg/Nm)</td> <td>69.79</td> <td>78.95</td> <td>75.14</td> <td>150</td> </tr> <tr> <td>2</td> <td>Sox (ppm)</td> <td>10.64</td> <td>15.87</td> <td>12.84</td> <td>100</td> </tr> <tr> <td>3</td> <td>Nox (ppm)</td> <td>17.87</td> <td>21.53</td> <td>19.96</td> <td>50</td> </tr> </tbody> </table>			Sr. No	Parameter	Min.	Max.	Avg.	Permissible Limit	1	SPM (Mg/Nm)	69.79	78.95	75.14	150	2	Sox (ppm)	10.64	15.87	12.84	100	3	Nox (ppm)	17.87	21.53	19.96	50
Sr. No	Parameter	Min.	Max.	Avg.	Permissible Limit																					
1	SPM (Mg/Nm)	69.79	78.95	75.14	150																					
2	Sox (ppm)	10.64	15.87	12.84	100																					
3	Nox (ppm)	17.87	21.53	19.96	50																					

Summary Table: Boiler Stack Analysis (Oct'20 to Mar'21)

Sr. No	Parameter	Min.	Max.	Avg.	Permissible Limit
1	SPM (Mg/Nm)	74.74	88.64	81.20	150
2	Sox (ppm)	19.19	22.99	21.04	100
3	Nox (ppm)	15.73	18.28	16.78	50

21	<p>Project proponent shall carryout periodical air quality monitoring in and around the site including VOC, HC. Locations of ambient air quality monitoring stations shall be fixed in consultation with the GPCB</p>	<p>Complied.</p> <p>Third party monitoring of ambient air quality including VOC and HC is carried out monthly. In-house ambient air quality monitoring is carried out. Third party monitoring reports are attached as Annexure 8.</p> <p>Table: Ambient Air (Oct'20 to Mar'21)</p> <table border="1" data-bbox="778 667 1453 1653"> <thead> <tr> <th>Sr. No</th> <th>Parameter</th> <th>Min.</th> <th>Max.</th> <th>Avg.</th> <th>Permissible Limit</th> </tr> </thead> <tbody> <tr> <td>1.</td> <td>SO₂ ($\mu\text{g}/\text{m}^3$)</td> <td>10.6</td> <td>17.4</td> <td>12.95</td> <td>80</td> </tr> <tr> <td>2.</td> <td>NO_x ($\mu\text{g}/\text{m}^3$)</td> <td>23.4</td> <td>33.9</td> <td>27.7</td> <td>80</td> </tr> <tr> <td>3.</td> <td>HCl ($\mu\text{g}/\text{m}^3$)</td> <td>ND</td> <td>ND</td> <td>ND</td> <td>200</td> </tr> <tr> <td>4.</td> <td>H₂S ($\mu\text{g}/\text{m}^3$)</td> <td>ND</td> <td>ND</td> <td>ND</td> <td>500</td> </tr> <tr> <td>5.</td> <td>CO (mg/m^3)</td> <td>0.74</td> <td>1.16</td> <td>0.95</td> <td>2</td> </tr> <tr> <td>6.</td> <td>HC ($\mu\text{g}/\text{m}^3$)</td> <td>ND</td> <td>ND</td> <td>ND</td> <td>160</td> </tr> <tr> <td>7.</td> <td>VOC (Benzene) ($\mu\text{g}/\text{m}^3$)</td> <td>ND</td> <td>ND</td> <td>ND</td> <td>5</td> </tr> <tr> <td>8.</td> <td>PM_{2.5} ($\mu\text{g}/\text{m}^3$)</td> <td>26.92</td> <td>42.6</td> <td>33.44</td> <td>60</td> </tr> <tr> <td>9.</td> <td>PM₁₀ ($\mu\text{g}/\text{m}^3$)</td> <td>67.82</td> <td>84.4</td> <td>77.42</td> <td>100</td> </tr> </tbody> </table>	Sr. No	Parameter	Min.	Max.	Avg.	Permissible Limit	1.	SO ₂ ($\mu\text{g}/\text{m}^3$)	10.6	17.4	12.95	80	2.	NO _x ($\mu\text{g}/\text{m}^3$)	23.4	33.9	27.7	80	3.	HCl ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	200	4.	H ₂ S ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	500	5.	CO (mg/m^3)	0.74	1.16	0.95	2	6.	HC ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	160	7.	VOC (Benzene) ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	5	8.	PM _{2.5} ($\mu\text{g}/\text{m}^3$)	26.92	42.6	33.44	60	9.	PM ₁₀ ($\mu\text{g}/\text{m}^3$)	67.82	84.4	77.42	100
Sr. No	Parameter	Min.	Max.	Avg.	Permissible Limit																																																									
1.	SO ₂ ($\mu\text{g}/\text{m}^3$)	10.6	17.4	12.95	80																																																									
2.	NO _x ($\mu\text{g}/\text{m}^3$)	23.4	33.9	27.7	80																																																									
3.	HCl ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	200																																																									
4.	H ₂ S ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	500																																																									
5.	CO (mg/m^3)	0.74	1.16	0.95	2																																																									
6.	HC ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	160																																																									
7.	VOC (Benzene) ($\mu\text{g}/\text{m}^3$)	ND	ND	ND	5																																																									
8.	PM _{2.5} ($\mu\text{g}/\text{m}^3$)	26.92	42.6	33.44	60																																																									
9.	PM ₁₀ ($\mu\text{g}/\text{m}^3$)	67.82	84.4	77.42	100																																																									
22	<p>All transporting routes within the premises shall have roads to minimize fugitive emission</p>	<p>Complied.</p> <p>All transporting routes within the premises are having cement roads to minimize fugitive emission. Proper housekeeping is being carried out in the plant on daily basis, truck tire washing facilities is provided.</p>																																																												

A.3 SOLID / HAZARDOUS WASTES:		
23	The proponent shall ensure that the TSDF fulfils all the provisions of Hazardous Wastes (Management, Handling and Transboundary Movement) Rules 2008 and the design and the construction of secured landfill site is as per the guidelines of CPCB with proper leachate collection arrangement.	Complied. We are fulfilling all the provisions of Hazardous and Other Wastes (Management and Tran's boundary Movement), Rules 2016 and its subsequent amendments. The design and the construction of secured landfill site is as per the guidelines of CPCB with proper leachate collection arrangement. Drawings are approved by IIT, Delhi and they are carrying out inspections. IIT certificate is attached as ANNEXURE 2 . Summary of CPCB guidelines are attached as ANNEXURE 4 .
24	Temporary hazardous waste storage area of about 4000MT capacity having impervious bottom and roof cover shall be provided as proposed.	Complied. Temporary Hazardous waste storage area of capacity 20000 MT having impervious bottom and roof cover has been provided.
25	The project proponent shall not store the hazardous wastes more than the quantity that has been permitted by the CPCB/ Gujarat State Pollution Control Board.	Complied. We are not storing hazardous waste (landfill waste) except during monsoon.
26	The main operational site shall be kept covered by tarpaulin with separate rain-water collection system during monsoon period.	Complied. We are already following the same practice. We keep main operation site covered by tarpaulin with separate storm water collection system during monsoon period. We have submitted Monsoon Planning to the Regional Office, GPCB on 06.06.2020 Same is attached as ANNEXURE 9 .
27	Salt from MEE and discarded bags shall be disposed in the secured landfill site	Complied. Salt from the MEE are being disposed in the secured landfill. During this period (Oct'20 to Mar'21) total 3084.34 MT of MEE salt has been disposed in landfill. As of now, no discarded bags are generated from MEE.
28	BEIL shall explore possibilities with respect to reduction and reuse of hazardous waste generated by member units and received at the	Complied. We ensure to explore possibilities with respect to reduce and reuse of hazardous waste generated by

	project site.	<p>member units and received at the project site. We have received authorization for decontamination of drums vide letter no. GPCB/HAZ-BRCH/B-CCA-143(I)/ID-40137/375053 dated 07.11.2016 to reuse and recycle discarded used drums.</p> <p>Summary of drum receipt and decontamination is as below. (Oct'20 to Mar'21):</p> <table border="1" data-bbox="783 573 1457 958"> <thead> <tr> <th>Month</th> <th>DRUM RECEIPT</th> <th>DRUM DECONTAMINATED</th> </tr> </thead> <tbody> <tr> <td>Oct 2020</td> <td>3285</td> <td>2830</td> </tr> <tr> <td>Nov 2020</td> <td>4588</td> <td>4490</td> </tr> <tr> <td>Dec 2020</td> <td>3281</td> <td>3756</td> </tr> <tr> <td>Jan 2021</td> <td>2369</td> <td>1924</td> </tr> <tr> <td>Feb 2021</td> <td>3631</td> <td>2979</td> </tr> <tr> <td>Mar 2021</td> <td>2755</td> <td>3985</td> </tr> </tbody> </table>	Month	DRUM RECEIPT	DRUM DECONTAMINATED	Oct 2020	3285	2830	Nov 2020	4588	4490	Dec 2020	3281	3756	Jan 2021	2369	1924	Feb 2021	3631	2979	Mar 2021	2755	3985
Month	DRUM RECEIPT	DRUM DECONTAMINATED																					
Oct 2020	3285	2830																					
Nov 2020	4588	4490																					
Dec 2020	3281	3756																					
Jan 2021	2369	1924																					
Feb 2021	3631	2979																					
Mar 2021	2755	3985																					
29	Used oil shall be sold only to the registered recyclers.	<p>Complied.</p> <p>Right now, very less amount of used oil is being generated. We ensure to sell used oil only to registered recyclers.</p>																					
A.4 SAFETY:																							
30	All necessary precautionary measures shall be taken to avoid any kind of accident during storage and handling of hazardous wastes.	<p>Complied.</p> <p>We are taking all necessary precautionary measures to avoid any kind of accident during storage and handling of hazardous waste. Fire hydrants (storage capacity 250 KL), fire extinguishers are provided. Adequate PPEs are being provided to all the workers and employees, work permits are issued before starting any work and being closed after completing the work, on site emergency plan is also there which is updated on yearly basis. We are carrying out mock drills regularly.</p> <p>Please refer Annexure 10</p> <ul style="list-style-type: none"> A) Ack copy of Onsite Emergency plan submitted to DISH B) Onsite Emergency Plan C) Ack copy of Mock Drill Report submitted to DISH 																					
31	Handling And storage of wastes shall be done in such a manner that	Complied.																					

	minimal human exposure occurs.	We ensure to handle and store waste in such a manner to minimize human exposure. The Hazardous waste stabilization and disposal to landfill is carried out with the help of the excavator and other machineries. MEE waste is also directly emptied to tanks from where it is carried through the pipelines.
32	All transportation of hazardous materials shall be as per motor vehicle Act & Rules	Complied. We have ensured that the transportation of the hazardous wastes to the TSDF confirms to the norms laid down in the hazardous and other wastes (management and handling) rules 2016 i.e. licensed and trained drivers, close and hydraulic dumpers, GPS enabled dumpers etc. Total Approved 170 dedicated vehicles equipped with GPS system are being used for Transportation of Hazardous waste from member Industries to TSDF.
33	Hazardous materials storage shall be at an isolated designated location, bund/dyke walls shall be provided for storage tanks for hazardous Chemicals.	Complied. Storage sheds at isolated designated location with impervious floor & roof is provided with dyke wall. Storage tanks of adequate quantity are provided with dyke wall.
34	Personal Protective Equipment shall be provided to workers and its usage shall be ensured and supervised.	Complied. Personal Protective Equipment are provided to workers and its usage are being ensured and supervised.
35	First Aid Box and required Antidotes for the chemicals used in laboratory shall be made readily available in adequate quantity at all the times	Complied. First Aid Box (4 First aid box, at gate, at admin building, at lab and at plant control room) and required Antidotes for the chemicals used in laboratory are made readily available in adequate quantity at all the times.
36	Training shall be given to all workers on safety and health aspect of handling hazardous wastes.	Complied. ➤ A training calendar is prepared in advance to inform everyone regarding the training dates. ➤ We try to ensure that all relevant employees are covered and maintain a record of personnel covered in each training.

		<p>Please refer Annexure 19:</p> <p>A) Training calendar for 2020-21 & 2021-22 B) Training attendance sheets 2020 (Oct'20-Mar'21)</p>
37	Occupational health surveillance of the workers shall be carried out on a regular basis and records shall be maintained as per the Factories Act and Rules. Pre-employment and periodical medical examination for all workers shall be undertaken as per statutory requirement.	<p>Complied.</p> <p>Pre-employment checkup are being carried out. BCA test of the workers are being done on every two month and full medical checkup is being done once in a year. FMO is visiting regularly to the site.</p>
38	Project proponent shall prepare and implement an On-Site Emergency Management Plan and Disaster Management Plan (DMP) for the project as per the guidelines from Directorate of industrial Safety and Health. Adequate firefighting facilities shall be installed to handle the fire.	<p>Complied.</p> <p>We've prepared and Implemented Onsite Emergency Plan and Disaster Management Plan. On-site emergency plan & disaster management plan is attached as ANNEXURE 10.</p> <p>Fire hydrants (Existing storage capacity 250 KL), fire extinguishers are provided, and Pre-employment checkup are being carried out. BCA test of the workers are being done on every two month and full medical checkup is being done once in a year.</p>
A.5 NOISE:		
39	The overall noise level in and around the premises shall be kept within the standards by providing noise control measures including engineering controls like acoustic insulation hoods, silencers, enclosures etc. On all sources of noise generation. The ambient noise level shall conform to the standards prescribed under The Environment (Protection Act 1986 & Rules)	<p>Complied.</p> <p>We ensure to keep noise level in and around the premises within the standard limit by providing noise control measures according to its requirement.</p> <p>We are monitoring noise level monthly by third party and once in a month internally at all locations, which are well within the limit.</p> <p>Reports are attached as ANNEXURE 11.</p>

		Summary Table: Noise (Day Time) (Oct'20 to Mar'21)					
		Sr. No	Place	Min	Max.	Avg.	Permissible Limit (dB)
		1	Near Main Gate (dB)	61.8	66.4	64	75
		2	Behind ADM Building (dB)	57.2	62.3	59	75
		3	Near EB 1 Borewell (dB)	60.6	64.6	63	75
		4	Nr. Monsoon Shed	51.4	59.2	56	75
		5	B/H Landfill cell 4	68.2	73.6	70	75
		6	Nr. EB2 Borewell	60.4	66	64	75
A.6 GREEN BELT AND OTHER PLANTATION:							
40	Project proponent shall develop green belt all along the periphery of the TSDF as per the CPCB guidelines with plant species that are significant and used for pollution abatement. Drip irrigation system shall be used for the green belt for optimum utilization of the water resources.	<p>Complied.</p> <p>➤ We have developed 53,622 sq. mt. area along the 15 mt periphery as green belt and other forms of greenery as per CPCB guidelines. We assure that tree plantation is always going to be an on-going process.</p> <p>➤ Drip Irrigation system has been installed.</p> <p>Please refer Annexure 20:</p> <p>A) Layout showing plantation along the periphery. B) Photographs of plantation along the periphery. C) Photographs of Drip Irrigation at site.</p>					
41	BEIL shall also tie up with local agencies like gram panchayat,	<p>Complied.</p> <p>➤ In consultation with the gram panchayat, an</p>					

	<p>schools, social forestry office etc. For plantation at suitable open places in GIDC estate and nearby villages and shall submit an action plan of plantation for next five year to the GPCB</p>	<p>action plan of plantation for the next five years has been prepared. As per the action plan, BEIL will provide plants and tree guards for the locations mentioned by the gram panchayat.</p> <ul style="list-style-type: none"> ➤ As per the action plan, we have planted 100 trees near Bhutnath temple, 20 trees at GEB Dahej, 50 trees near Badyadev temple in the year 2018 & 2019. ➤ We have also planted around 200 trees at Compost site in Dahej Village. ➤ BEIL has also done tree plantation in the following villages: <ul style="list-style-type: none"> 1800 nos near Kadodara 2800 in Vav village 2800 nos paniyadara 2800 nos Padariya ➤ We have also distributed tree guards at Gauseva trust Suva, Gram Panchayat at Nandarkha villages, Bhutnath charitable trust, Dahej Gram Panchayat, Kadodara Gram Panchayat. <p>Please refer Annexure 21:</p> <ul style="list-style-type: none"> A) Action plan for Tree Plantation B) Tree Plantation at GEB office Dahej C) Acknowledgement letters from villages for plantation already done by BEIL/UPL D) Tree Guard Distribution to Nandarkha village Gram Panchayat. E) Tree Guard Distribution to Kadodara village Gram Panchayat. F) Photos of tree plantation at Compost site Dahej.
--	--	--

OTHER CONDITIONS:

Sr. No.	Description	Status
42	Project Proponent shall obtain necessary Authorization/ Consents from the Gujarat Pollution Control Board	Complied. We have received CCA renewal 109249 dated 14.09.2020 and it is valid up to 17.04.2025.
43	A separate Environment Management Cell equipped with full-fledged testing laboratory facilities shall be set up to carry out the environment Management and Monitoring Functions	Complied. A full-fledged, well qualified and experienced staff is appointed in the environment cell. The details are as given below:

		<p>Environment Cell at Site:</p> <ol style="list-style-type: none"> 1. Mr. Manoj Patel: General Manager – Project (BE Civil) 2. Ms. Rakshita Vyas: Manager – Environment (M.Sc. Env. Science) 3. Mr. Shahrukh Saiyed: Environment Engineer (B.E. Environmental Science and Technology) <p>Corporate Environment Cell:</p> <ol style="list-style-type: none"> 1. Mr. B.D. Dalwadi - CEO - (BE – Chemical) 2. Dr. P N Parameswaran: Advisor – Environment (PhD Environment)
44	In the event of de-functioning of MEE receipt of effluent from member units shall be immediately stopped and they shall be intimated about the same. Effluent from the member units shall not be received until the desired efficiency of MEE has been achieved.	<p>Complied.</p> <p>As and when the situation arises, we ensure to stop taking effluent from member units immediately and will start again only when desired efficiency of MEE will be achieved.</p>
45	Adequate spares for waste and effluent collection, handling and transfer shall always be maintained.	<p>Complied.</p> <p>Adequate spares for waste and effluent collection, handling and transfer are always maintained.</p>
46	BEIL shall comply with all the provisions of CPCB guidelines for TSDF as may be applicable from time to time	<p>Complied.</p> <p>We have complied all the provisions of CPCB guidelines for TSDF as applicable from time to time and in future also we shall comply.</p> <p>Summary of the guidelines Compliance is attached as ANNEXURE 4.</p>
47	BEIL shall maintain accurate records of their member units in respect of quantity of each product manufactured quantities and qualities of waste & effluent generated booked & supplied to the TSDF & MEE on day to day basis and shall submit the complied records to the GPCB on monthly basis	<p>Complied.</p> <p>We are submitting monthly report to GPCB office.</p>
48	BEIL shall ensure that each & every member unit renews the agreement/ membership on before expiring of said agreement/membership	<p>Complied.</p> <p>We ensure that each & every member</p>

	and shall inform the GPCB about any unit not renewing the agreement/membership within stipulated period BEIL shall immediately inform the Gujarat Pollution Control Board termination/ suspension of membership of any member unit.	unit renews the agreement/ membership on before expiring of said agreement/membership and will inform the GPCB about any unit not renewing the agreement/membership within stipulated period. We ensure to immediately inform the Gujarat Pollution Control Board termination/ suspension of membership of any member unit.
49	BEIL shall instruct and make sure that each member unit provides effluent storage tank and hazardous waste storage area having adequate retention time.	<p>Complied.</p> <p>As per our protocol, before giving membership, industries have to submit some details to BEIL in the prescribed membership form. One of the details asked for, is storage capacities of liquid and solid waste. We do not accept incomplete membership forms. Samples of our membership form and member's documents were shown at the time of visit from RO-MOEF, Bhopal. GPCB mentions a condition in every industry's CCA, that the industry needs to provide effluent storage tanks and hazardous waste storage area having adequate retention time.</p> <p>Annexure – 18</p> <p>A) Membership form – Landfill. B) List of members with their consent details & hazardous storage details C) Hazardous waste storage details of Bharat Rasayan, Diaichi, Fermenta Biotech, Insecticides Ltd.</p>
50	BEIL shall not allow any new member or enhance waste / effluent quantity of existing members unless & until they have prior requisite permissions from competent authorities.	<p>Complied.</p> <p>BEIL does not give membership without verifying the member's consent. We also have CCA copies of members. Samples of CCA copies of members were shown at the time of visit.</p>

		<p>Annexure – 18</p> <p>B) List of members with their consent details.</p>
51	Pucca flooring/ impervious layer shall be provided in the work area, chemical storage area and chemical handling area to minimize soil contamination	<p>Complied.</p> <p>We have provided Pucca flooring/ impervious layer in the work area, chemical storage area and chemical handling area to minimize soil contamination.</p>
52	Good Housekeeping shall be maintained within the premises. All pipes valves and drains shall be leak proof Leakages from the pipes, pumps shall be minimal and if occurs shall be arrested promptly. Floor washing shall be admitted into the effluent collection system for subsequent treatment and disposal through MEE	<p>Complied.</p> <ul style="list-style-type: none"> ➤ We ensure the housekeeping is good, and no major dusting is observed. We have also implemented 5S system, which is specially designed for good housekeeping practices. ➤ To ensure least leakages from pumps/motors/lines, preventive maintenance of the same is carried out on regular basis. ➤ Leakages from equipment & floor washing effluent is being collected in tank/pit & treated in MEE. <p>Please refer Annexure 22:</p> <p>A) 5S Certificate of BEIL</p>
53	During effluent transfer, spillages shall be avoided, and garland drain be constructed to avoid mixing of accidental spillages with storm water.	<p>Complied.</p> <ul style="list-style-type: none"> ➤ In case of spillage during transfer of effluent, the spilled effluent gets collected in the garland drain which has a collection pit at its end. From this collection pit, the effluent is transferred back to the feed tank for treatment in MEE. There is a separate effluent collection drain in the plant and is not connected to storm water drain. Similarly, there is a separate effluent collection drain/garland drain in all the plants and the spilled effluent is collected and transferred to MEE. Pictures depicting the same are attached. ➤ The main landfill site is kept covered during monsoon and no waste is added in this site during the period and hence there are no chances of contaminated run-off from landfill. Further, an IIT

		<p>approved leachate collection system is developed and there is a garland drain around the leachate tank. The leachate from here is pumped to the storage tank which is provided with dyke wall. Therefore, no chances of any type of contamination from anywhere. Pictures & IIT approved leachate collection system layout attached.</p> <p>➤ The outlet of storm water drain is equipped with a gate system and the water in the channel is checked daily. If at all, the water in the storm water channel is found contaminated then we pump it to MEE for treatment. Therefore, there are no chances of contaminated water going out of the premises.</p> <p>Please refer Annexure 23:</p> <p>A) Picture of plant showing separate garland drain & storm water channel.</p> <p>B) Picture showing garland drain, effluent collection chamber of drain and plant area.</p> <p>C) Leachate tank with dyke wall.</p> <p>D) Gate at the storm water channel outlet.</p> <p>E) Landfill Monsoon Covering Photographs.</p> <p>F) IIT Approved Leachate Collection System.</p>
54	Necessary measures shall be taken to prevent contamination of storm water from wastes/effluent handled at site. The storm water drains shall be kept separate and shall remain dry throughout the year except monsoon.	<p>Complied.</p> <p>Necessary measures have been taken to prevent contamination of storm water from waste/effluent handled at site. Separate storm water drain is provided.</p>
55	BEIL shall intimate the GPCB about occurrence of any accident, act or event resulting in discharge of poisonous, noxious, or polluting mater or the likelihood of the same into a stream or land or well.	<p>Complied.</p> <p>Till date there has been no such incidence. We ensure to intimate GPCB about occurrence of any accident, act or event resulting in discharge of poisonous, noxious, or polluting mater or the likelihood of the same into a stream</p>

		or land or well.												
56	The funds earmarked for environment protection measures should be maintained in a separate account and there should be no diversion of these funds for any other purpose. A year-wise expenditure on environmental safeguards should be reported.	<p>Complied.</p> <p>A separate account is maintained for environment protection and the cumulative amount is Rs 490,91,000 till March 2021. These funds are not diverted for any other purpose. A year wise expenditure on environmental safeguards is mentioned in the below table: -</p> <table border="1"> <thead> <tr> <th>Sr. No.</th> <th>Year</th> <th>Expense</th> </tr> </thead> <tbody> <tr> <td>1</td> <td>2018 – 2019</td> <td>13,40,242</td> </tr> <tr> <td>2</td> <td>2019 – 2020</td> <td>30,90,150</td> </tr> <tr> <td>3</td> <td>2020 – 2021</td> <td>1,70,76,593</td> </tr> </tbody> </table>	Sr. No.	Year	Expense	1	2018 – 2019	13,40,242	2	2019 – 2020	30,90,150	3	2020 – 2021	1,70,76,593
Sr. No.	Year	Expense												
1	2018 – 2019	13,40,242												
2	2019 – 2020	30,90,150												
3	2020 – 2021	1,70,76,593												
57	All the issues raised in the public hearing shall be comprehensively addressed/ compiled with in a time bound manner.	<p>Complied</p> <p>All the issues raised in public hearing were addressed/complied on time.</p> <p>Please refer Annexure 24: Compliance Report of Public Hearing.</p>												
58	BEIL shall assign specific budget for socio-economic upliftment of the surrounding villages and shall undertake eco-developmental measures including community welfare program most useful in the project area for the overall improvements of the environment in consultation with the District Development Officer/District Collector.	<p>Complied.</p> <ul style="list-style-type: none"> ➤ We have donated Rs. 15000 to Bhutnath Charitable Trust and we are also providing monthly Stipend to Local villagers (Mr. Rajendra Parmar & Mr. Dinesh Ahir). ➤ Apart from that we have tied up with local Gram panchayat to develop a garden, costing Rs. 3.2 Lacs. ➤ We are also extending supporting hand when and where asked and required. ➤ We have also built a solid waste management site in Dahej village and the kitchen waste is collected from Dahej village and converted to fertilizer which is also distributed in the village and we have recruited 2 persons for the compost site also. ➤ We have also distributed dustbins at Dahej village under Swatch Bharat mission. ➤ Further, a total budget of Rs. 40 lakhs for the next 5 years have been 												

		<p>allocated for socio economic upliftment to improve the overall environment. We shall be using this amount on various activities like providing sanitation, solid waste management, rainwater harvesting, etc. The tentative break-up of Rs. 40 lakhs for the 5 years from 2018-19 are as under:</p> <table border="1" data-bbox="959 521 1442 786"> <thead> <tr> <th>Year</th> <th>Rs. (Lakhs)</th> <th>Expenditure (Lakhs)</th> </tr> </thead> <tbody> <tr> <td>18-19</td> <td>10</td> <td>4.68</td> </tr> <tr> <td>19-20</td> <td>10</td> <td>24.91</td> </tr> <tr> <td>20-21</td> <td>10</td> <td>8.35</td> </tr> <tr> <td>21-22</td> <td>5</td> <td>-</td> </tr> <tr> <td>22-23</td> <td>5</td> <td>-</td> </tr> </tbody> </table> <p>➤ A letter with our intention to contribute the above amount towards the socio-economic upliftment projects in co-ordination with District Collector/District Development Officer is submitted to the respective offices. Inward copy attached.</p> <p>Please refer Annexure 25:</p> <p>A) Inward copy of Letter submitted to DC/DDO offices B) Photos of Compost Site built by BEIL in Dahej village as a Solid waste management program.</p>	Year	Rs. (Lakhs)	Expenditure (Lakhs)	18-19	10	4.68	19-20	10	24.91	20-21	10	8.35	21-22	5	-	22-23	5	-
Year	Rs. (Lakhs)	Expenditure (Lakhs)																		
18-19	10	4.68																		
19-20	10	24.91																		
20-21	10	8.35																		
21-22	5	-																		
22-23	5	-																		
59	BEIL shall comply with all the recommendations as well as the environmental protection measures and risk mitigation measures/ safeguard proposed in the REIA report, Risk Assessment Report & Disaster Management Plan of the project.	Complied. We have complied with all the recommendations as well as the environmental protection measures and risk mitigation measures/ safeguard proposed in the REIA report & Risk Assessment Report of the project. EMP Compliance is attached as ANNEXURE 16.																		
60	In the event of a change in project profile or change in the implementation agency a fresh reference shall be made to the SEIAA/SEAC	Complied. We have received EC on date 19 th December 2018 for Installation of Incinerators and Capacity enhancement																		

		of Landfill Facility.
61	BEIL shall thrive to obtain the ISO 14001 and OSHAS 18001 Certification	Complied. We've got ISO 14001:2015 & OHSAS 18001:2007 certificate and valid up to 24.06.2022 and 11.03.2021 respectively. Copy of Certificate is attached as ANNEXURE 12.
62	The project manager shall extend full support to the officer of MOEF/GPCB during inspection of the project for monitoring purpose by furnishing full details and action plan including action reports in respect of mitigation measures and other environmental protection activities	Complied.
63	A six-monthly monitoring report shall need to be submitted by the project proponents to the Regional Office of the MOEF and SEIAA regarding the implementation of the stipulated condition in hard and soft copies to the regulatory authority concerned on 1 st June and 1 st December of each calendar year	Complied. We have submitted six monthly report to the Regional Office of the MOEF and SEIAA regarding the implementation of the stipulated condition in hard and soft copies to the regulatory authority. Acknowledgement copy of the last submitted copy is attached as ANNEXURE 13.
64	The project proponents shall inform the Regional Office of MOEF at Bhopal as well as the SEIAA, the date of financial closure and final approval of the project by the concern authorities and the date of start of land development work.	Complied We had informed the GPCB, Regional Office of MOEF and SEIAA about the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project vide letter No BEIL/DAHEJ/2015 dated 30.07.2014. Same is attached as ANNEXURE 14.
65	BEIL shall also comply with any additional condition that may be imposed by the SEAC or the SEIAA or any other competent authority for the purpose of the environmental protection and management.	Complied. We are complying with conditions imposed by the SEAC or the SEIAA and in the future too shall abide by it. EC Compliance is submitted half yearly to the concern authorities (MOEF, CPCB, GPCB). All the conditions stipulated in the CCA are also complied.

66	No further expansion or modification in the plant likely to cause environmental impacts shall be carried out without obtaining proper Environmental Clearance from the concerned authority.	Complied. We have received EC Dated 20.12.2018. For installation of 2 nos. of incinerators and capacity enhancement of existing landfill.												
67	The project authority shall earmark adequate funds to implement the condition stipulated by SEIAA as well as GPCB along with the implementation schedule for all the conditions stipulated herein. The funds so provided shall not be diverted for any other purpose.	Complied. We have earmarked adequate funds to implement the conditions stipulated by SEIAA as well as GPCB along with the implementation schedule for all the conditions stipulated herein. A separate account is maintained for environment protection and the cumulative amount is Rs 490.91 lacs till March 2021. <table border="1" data-bbox="922 913 1455 1128"> <thead> <tr> <th>Sr. No.</th> <th>Year</th> <th>Expense</th> </tr> </thead> <tbody> <tr> <td>1</td> <td>2018 – 2019</td> <td>13,40,242</td> </tr> <tr> <td>2</td> <td>2019 – 2020</td> <td>30,90,150</td> </tr> <tr> <td>3</td> <td>2020 – 2021</td> <td>1,70,76,593</td> </tr> </tbody> </table>	Sr. No.	Year	Expense	1	2018 – 2019	13,40,242	2	2019 – 2020	30,90,150	3	2020 – 2021	1,70,76,593
Sr. No.	Year	Expense												
1	2018 – 2019	13,40,242												
2	2019 – 2020	30,90,150												
3	2020 – 2021	1,70,76,593												
68	The applicant shall inform the public that the project has been accorded environmental clearance by the SEIAA and that the copies of the clearance letter are available with GPCB and may also be seen at the Website of SEIAA/GPCB. This shall be advertised within seven day from the date of clearance letter, in at least two local newspapers that are widely circulated in the region. One of which shall be in Gujarati language and the other in English. A copy each of the same shall be forwarded to the concerned Regional Office of the authority.	Complied. BEIL had received EC at site on 23rd Aug'13 and we had given advertisement in two local newspapers, namely, Times of India and Divya Bhaskar on 24th Aug'13 itself. Annexure 15: A) EC copy. B) Newspaper advertisements dated 24 th August'13.												
69	The project authorities shall also adhere to the stipulations made by the Gujarat Pollution Control Board.	Complied. All the conditions stipulated in the CC&A are complied.												
70	The project authorities shall inform the GPCB Regional Office of MOEF and SEIAA about the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project.	Complied. We had informed the GPCB, Regional Office of MOEF and SEIAA about the date of financial closure and final												

		<p>approval of the project by the concerned authorities and the date of start of the project vide letter No BEIL/DAHEJ/2015 dated 30.07.2014.</p> <p>Same is attached as ANNEXURE 14.</p>
71	The SEIAA may revoke or suspend the clearance, if implementation of any of the above conditions is not found satisfactory.	Noted
72	The company in a time bound manner shall implement these conditions. The SEIAA reserves the right to stipulate additional condition, if the same is found necessary. The above conditions will be enforced, inter-alia under the provisions of the Water (Prevention & Control of Pollution) Act 1974, Air (Prevention & Control of Pollution) Act 1981. The environment (Protection) Act 1986. Hazardous Wastes (Management, Handling and Transboundary Movement) Rules 2008 and the public Liability Insurance Act 1991 along with their amendments and rules.	<p>Complied</p> <p>We are complying with conditions imposed by the SEAC or the SEIAA. EC Compliance is submitted half yearly to the concern authorities (MOEF, CPCB, GPCB). All the conditions stipulated in the CCA are also complied. We are having Public Liability Act Policy No. 1806012721P100990596 which is valid up to 30.04.2022. PLI Policy is attached as Annexure 17.</p>
73	This environmental clearance is valid for five years from the date of issue.	<p>Complied</p> <p>We have received EC vide letter no. SEIAA/GUJ/EC/7(d)/227/2013 dated 13.07.2013. We have got CCA renewal order no. AWH – 109249 issued on 14.09.2020.</p>
74	Any appeal against this environmental clearance shall be with the National Green Tribunal, if preferred within a period of 30 day as prescribed under Section 16 of the National Green Tribunal Act 2010	N. A

2. Compliance Status of Environmental clearance for Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility at existing Common Hazardous Waste Treatment Storage and Disposal Facilities (TSDF) at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch by M/s BEIL Infrastructure Limited for Period Apr' 20 to Sep'20.

This EC is for installation of Two Incinerators and capacity enhancement of Existing Landfill. This EC is not yet implemented we have only received CTE from GPCB dated 24.12.2019 We shall comply with the conditions once the EC is implemented. However, the compliance status as of now is as under.

Sr No.	EC Condition Details	Status																								
1	The proposal is for grant of environmental clearance to the project 'Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility' at existing Common Hazardous Waste Treatment, Storage and Disposal Facilities (TSDF) at plot number D-43, Dahej Industrial Estate, Taluka Vagra, District Bharuch by M/s BEIL Infrastructure Limited	Noted We have obtained CTE from GPCB. An Incinerator plant is under implementation.																								
2	The proposed project is Category "A" "Common hazardous waste treatment, storage and disposal facilities (TSDFs) listed under activity 7 (d) as per EIA Notification dated 14 th September 2006 as it is proposed to upgrade the facility integrated facilities having incineration & landfill.	Noted																								
3	Due to growth of chemical Industries in the Dahej industrial area, generation of hazardous waste Landfillable & incinerable waste has been increasing many folds. The existing secured landfill is likely to get exhausted much before planed period at the current rate of waste generation & disposal. Therefore, it is proposed to enhance the capacity of SLF from 14 lakhs MT to 19 lakhs MT and addition of two Incinerators. All the other facilities such as infrastructure, laboratory is already available at the existing site.	Noted																								
4	<p>Details of existing and proposed facilities are as under:</p> <table border="1" data-bbox="188 1417 1018 2020"> <thead> <tr> <th data-bbox="188 1417 464 1458">Particulars</th> <th data-bbox="464 1417 743 1458">Existing</th> <th data-bbox="743 1417 1018 1458">Proposed</th> </tr> </thead> <tbody> <tr> <td data-bbox="188 1458 464 1498">Land area</td> <td data-bbox="464 1458 743 1498">2,85,343.76 m2</td> <td data-bbox="743 1458 1018 1498">Nil</td> </tr> <tr> <td data-bbox="188 1498 464 1574">Secured landfill capacity</td> <td data-bbox="464 1498 743 1574">14 LMT</td> <td data-bbox="743 1498 1018 1574">19LMT</td> </tr> <tr> <td data-bbox="188 1574 464 1650">Incinerator</td> <td data-bbox="464 1574 743 1650">Nil</td> <td data-bbox="743 1574 1018 1650">2 Nos. 12 Million Kcal/hr</td> </tr> <tr> <td data-bbox="188 1650 464 1727">Water consumption</td> <td data-bbox="464 1650 743 1727">466 KLD</td> <td data-bbox="743 1650 1018 1727">900 KLD</td> </tr> <tr> <td data-bbox="188 1727 464 1767">Power</td> <td data-bbox="464 1727 743 1767">475 KVA</td> <td data-bbox="743 1727 1018 1767">1920 KVA</td> </tr> <tr> <td data-bbox="188 1767 464 1874">D.G.</td> <td data-bbox="464 1767 743 1874">1 no 600 KVA</td> <td data-bbox="743 1767 1018 1874">2 nos. (600 KVA + 900 KVA) capacity</td> </tr> <tr> <td data-bbox="188 1874 464 2020">Employment</td> <td data-bbox="464 1874 743 2020">Employee-23 Worker – 84</td> <td data-bbox="743 1874 1018 2020">Construction phase 150 workman Operation phase: 60 workmen</td> </tr> </tbody> </table>	Particulars	Existing	Proposed	Land area	2,85,343.76 m2	Nil	Secured landfill capacity	14 LMT	19LMT	Incinerator	Nil	2 Nos. 12 Million Kcal/hr	Water consumption	466 KLD	900 KLD	Power	475 KVA	1920 KVA	D.G.	1 no 600 KVA	2 nos. (600 KVA + 900 KVA) capacity	Employment	Employee-23 Worker – 84	Construction phase 150 workman Operation phase: 60 workmen	Noted
Particulars	Existing	Proposed																								
Land area	2,85,343.76 m2	Nil																								
Secured landfill capacity	14 LMT	19LMT																								
Incinerator	Nil	2 Nos. 12 Million Kcal/hr																								
Water consumption	466 KLD	900 KLD																								
Power	475 KVA	1920 KVA																								
D.G.	1 no 600 KVA	2 nos. (600 KVA + 900 KVA) capacity																								
Employment	Employee-23 Worker – 84	Construction phase 150 workman Operation phase: 60 workmen																								

5	Water Consumption for the proposed project is 900 KLD and will be met from GIDC water supply	Shall be complied
6	Leachate/effluent from landfill will be treated in Multiple Effect Evaporator (MEE) plant. The wastewater from incinerator shall be used for quenching. Municipal spoil waste generated from the project shall be disposed as per MSW Rules, 2016.	Noted Shall be complied
7	Hazardous solid waste generated as the residue from MEE after treatment of leachate and residue ash generated from incineration of hazardous waste shall be disposed in the landfill. Transportation of hazardous solid waste is done as per guidelines of CPCB. The TSDF have approved transporter authorization with dedicated vehicle (hydraulics) for transportation of wastes.	Noted Shall be complied We are transporting the MEE salt as per the guidelines of CPCB and Incinerator ash will be transported in the same way.
8	The proposed project shall be an important endeavor to mitigate the degradation of environment in the region.	Noted
9	TOR for the proposed project was approved by MOEF & CC on dated 26 th October 2016 vide Letter no F.No. -10-43/2016-1A-III.	Noted
10	Public Hearing was exempted vide amendment in TOR issued vide letter dated 14 th May 2018, as Dahej Industrial Estate of GIDC is a part of Development of Petroleum, Chemical and Petro-chemical Investment Region (PCPIR) Dahej, Dist. Bharuch. The PCPIR has already obtained Environmental Clearance on 17 th September 2017 vide letter 21-49/2010/-1AIII for the entire industrialized region. The Public hearing for the same was also conducted on 30 th July 2014.	Noted
11	Investment/Cost of the project is approx. Rs. 64 Crore	Noted
12	Benefits of the project: There will be a positive environmental impact by collecting and disposing the hazardous waste in the scientific manner that will reduce the future health hazard. It is expected that additional people will get employment and hence job opportunities for the local people as well as migrants from nearby areas would increase.	Noted
13	Employment potential: About 150 persons (construction phase) & 60 persons (operational phase).	Noted
14	The project/activity is covered under category 'A' of item 7(d) Common hazardous waste Treatment, Storage and Disposal Facilities (TSDFs) of the Schedule to the EIA Notification, 2006 and its subsequent amendments, and requires appraisal at Central Level.	Noted
15	The EAC, in its 35 th meeting held on 29-31 October 2018, deliberated on the proposal including certified compliance report letter No. 18-A-96/2013(Parya)/943 dated 28.08.2017 (inspection done on 06.06.2017) issued by the MOEF & CC's Regional Office (Western Region), Bhopal. The EAC, on being satisfied with the submissions of the project proponent,	Noted

	recommended the project for grant of environmental clearance to the project. As per recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the project `Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility at existing Common Hazardous Waste Treatment, Storage and Disposal Facilities (TSDF) at plot number D-43, Dahej Industrial Estate, Taluka Vagra, District Bharuch by M/s Bharuch Enviro Infrastructure Limited, under the provisions of the EIA Notification, 2006 and amendments/circulars issued thereon, and subject to the specific and general conditions as under: -	
A.1	SPECIFIC CONDITIONS	
1	Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.	Noted Shall be complied We have obtained CTE on 24.12.2019, CTE application no. 164667
2	The Project proponent should ensure that the TSDF fulfils all the provisions of Hazardous and other Wastes (Management and Transboundary Movement) Rules, 2016.	Noted Shall be complied
3	Ground water abstraction shall be as prescribed by the CGWA. A clearance/permission of the CGWA shall be obtained in this regard.	Noted Shall be complied
4	It shall be ensured that all the trees and other plantation are of the non-edible varieties and do not in any way encourage the incorporation of toxic materials in the food chain.	Noted & Complied We are ensuring that trees and other plantation are of non-edible varieties.
5	The TSDF should only handle the waste generated from the member units.	Complied The waste generated from members units is only accepted.
6	As proposed, air pollution control device viz. gas quencher; treatment with mixture of hydrated lime and activated powder for adsorption of partial acidity and VOCs (if any); bag-filter/ESP for removal of particulate matter; ventury scrubber followed by packed bed scrubber with caustic circulation to neutralize the acidic vapours in flue gas; and demister column for arresting water carry over will be provided to the incinerator. Online pollutant monitoring shall be provided as per CPCB guidelines for monitoring particulate matter, SO ₂ , Nox and CO from the incinerator stack. The periodical monitoring of Dioxins and Furans in the Stack emissions shall be carried out.	Noted Shall be complied
7	Analysis of Dioxins and Furans shall be done through CSIR — National Institute for Interdisciplinary Science and Technology (NIIST), Thiruvananthapuram or equivalent NABL Accredited laboratory.	Noted Shall be complied
8	The project proponents shall adhere to all conditions as prescribed in the Protocol for ‘Performance Evaluation and Monitoring of the Common Hazardous Waste Treatment, Storage and Disposal Facilities’ published by the CPCB in May	Noted

	2010.	
9	Incinerator shall be designed as per CPCB guidelines. Energy shall be recovered from incinerator.	Noted
10	Sufficient number of Piezometer wells shall be installed in and around the project site to monitor the ground water quality in consultation with the State Pollution Control Board / CPCB. Trend analysis of ground water quality shall be carried out each season and information shall be submitted to the SPCB and the Regional Office of MOEF & CC.	Noted Shall be complied
11	Ambient air quality monitoring shall be carried out in and around the landfill site at up wind and downwind locations.	Complied We are regularly monitoring the ambient air quality around the landfill at up-wind and down-wind directions. Results attached as Annexure – 8.
12	The depth of the land fill site shall be decided based on the ground water table at the site and may be such as permitted by the Pollution Control Board.	Noted & Complied Ground water table at the project site has been ascertained through the GWRDC before initiating construction of secured landfill site. The depth of the secured land fill site has been decided based on the ground water level at the site and bottom of the secured landfill site, which is 7.5 (> 2 m) meter above the ground water table.
13	Environmental Monitoring Programme shall be implemented as per EIA report and guidelines prescribed by CPCB for hazardous waste facilities. Periodical ground water/soil monitoring to check the contamination in and around the site shall be carried out.	Noted
14	The Company shall ensure proper handling of all spillages by introducing spill control procedures for various chemicals.	Noted
15	On-line real time continuous monitoring facilities shall be provided as per the CPCB or State Board Directions.	Noted Shall be complied
16	No non-hazardous wastes, as defined under the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016, shall be handled in the premises.	Complied We are carrying out Internal Analysis and only hazardous waste is handled at site.
17	Gas generated in the Landfill should be properly collected, monitored and flared.	Noted
18	Project Proponent shall develop green belt with native plant species that are significant and used for the pollution abatement. At least 10 m thick greenbelt shall be developed in the periphery of hazardous waste facility.	Noted We have planted trees and it is always an ongoing activity.
19	Project should ensure that the site is properly cordoned off from general movement and no unauthorized person or goods permitted to enter the premises. Necessary security provision should be made as a condition in the Authorization under the	Complied We have ensured that the project is properly cordoned off from general movement and no

	Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 to prevent unwanted access.	unauthorized person or goods permitted to enter the premises.
20	Pre-medical check-up to be carried out on workers at the time of employment and regular medical record to be maintained.	Complied We are carrying out Pre-medical check-up of employees at the time of employment and maintaining record for the same.
21	Emergency plan shall be drawn in consultation with SPCB/CPCB and implemented in order to minimize the hazards to human health or environment from fires, explosion or any unplanned sudden or non-sudden release of hazardous waste or hazardous waste constituents to air, soil or surface water.	Noted
22	Rain-water runoff from the landfill area and other hazardous waste management area shall be collected and treated in the effluent treatment plant.	Complied Any contaminated run-off is treated in the in-house MEE plant.
23	The Project proponent shall not store the Hazardous Wastes more than the quantity that has been permitted by the CPCB/SPCB.	Noted & Complied
24	As per the Ministry's Office Memorandum F.No. 22-65/2017-IA.III dated 1 st May 2018, and as proposed, a fund of Rs. 0.40 Crore @ 1% of project Cost, shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as sanitation, solid waste management and rainwater harvesting etc. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.	Noted & Complied We have constructed a Compost Site as a solid waste management program at the nearby Dahej village. The cost of the project is Rs 21.46 Lakhs (construction cost) whereas monthly payment of approximately 45,000 for kitchen waste collection from Dahej village is also paid by BEIL. BEIL have also recruited two persons for segregation work at compost site. Photos attached as Annexure – 25.
B	GENERAL CONDITIONS	
1	A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control Board. The EC letter shall also be displayed at the Regional Office, District Industries Centre and Collector's Office/ Tehsildar's office for 30 days.	We have submitted a copy of environment clearance to the GPCB Bharuch, Member Secretary GPCB Gandhinagar and Collector Office Bharuch.
2	The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.	Noted.
3	Officials from the Regional Office of MOEF &CC, Bhopal who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities, and documents/data by the project proponents during their	Noted

	inspection. A complete set of all the documents submitted to MOEF & CC shall be forwarded to the APCCF, Regional Office of MOEF & CC, Bhopal.	
4	In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.	Noted
5	The Ministry reserves the right to add additional safeguard measures subsequently, if found necessary, and to take action including revoking of the environment clearance under the provisions of the Environmental (Protection) Act, 1986, to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.	Noted
6	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.	Noted
7	These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.	Noted
8	The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at http://www.envfor.nic.in . The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the Regional Office of this Ministry at Bhopal.	Complied. BEIL had received EC on 19 th Dec 2018 and we had given adv in three newspapers namely, Divya Bhaskar, Sandesh and Times of India on 21 st Dec'18. Annexure 27: A) EC copy. B) Newspaper advertisements dated 21 st December'18
9	Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.	Not Applicable
10	A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parisad /Municipal Corporation, Urban Local Body and the Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.	Complied We have sent the clearance letter to the nearby panchayat's, municipal corporation, and local NGO. Letter is attached as Annexure – 26.
11	The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MOEF & CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM2.5, PM10, SO2, NOx (ambient	Noted

	levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.	
12	The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the respective Regional Offices of MOEF& CC by email.	Complied Every year we are submitting the Environmental Statement to the GPCB Regional Office Bharuch and to GPCB Gandhinagar.

ANNEXURE 1

GUJARAT WATER RESOURCES DEVELOPMENT CORPORATION LTD., GANDHINAGAR.



OFFICE OF THE GEOHYDROLOGIST
GROUND WATER DIVISION NO.1,
REGIONAL DATA PROCESSING CENTRE,
VASANA BARRAGE CAMPUS, VASANA,
AHMEDABAD - 380 007.
TEL.NO. 079-26604027 FAX NO. 079-26609803
Email : ghdy1@gmail.com

No.GWDn.1/PB/Deposit/Gen/ 637 /2012
Date: 27/04/12


To,
The Dy.General Manager
Bharuch Enviro. Infrastructures Ltd.,
Plot No.9701-16, GIDC Estate, P.B.No.82,
ANKLESHWAR - 393 002.

Sub:- Geohydrological survey at Bharuch Enviro. Infrastructures Limited,
Dahej, Plot No.43, Dahej-1 Campus.
Ref:- Your's office letter dated 31/01/12.

Dear Sir,

With reference to above subject find herewith Geohydrological
Investigation Report at Dahej, Taluka-Vagara, District-Bharuch under deposit
work.

D.A.: As above.


GEOHYDROLOGIST
G.W.DIV.NO.1,
AHMEDABAD.

Copy submitted to:

➤ The Superintending Engineer, GWMI Circle, Gandhinagar for information
please.DA: A/a.

Copy to:

➤ The Geologist, G.W.Sub.Dn.No.2, Vadodara In reference to your letter
No.GWDn.1/PB/Deposit work/143/12, dated 20/04/12.

== Save Water ==

B. S. I. S.
05 MAY 2012
Inward No. 260
Time 11:30 AM

BRIEF REPORT ON
GEOHYDROLOGICAL CONDITIONS AROUND BEIL, DAHEJ
GIDC AREA, TALUKA VAGRA DISTRICT BIHARUCH

(April -2012)

GEOHYDROLOGIST
REGIONAL DATA CENTRE
VASNA BARRAGE
VASNA
AHMEDABAD

A BRIEF REPORT ON GEOHYDROLOGICAL CONDITIONS AROUND DAHEJ GIDC AREA, TALUKA VAGRA DISTRICT BHARUCH

AIM OF STUDY

Bharuch Enviro Infrastructure Ltd. has asked for Geohydrological Condition in & around Village Dahej GIDC area to study the ground water flow direction, details of aquifers and level of 1st, 2nd & 3rd aquifers based on sub-surface geology of the area in their proposed Landfill site at Dahej GIDC as per letter No. GWDn. I/ PB/Deposit work/ 293/ 2012, Dated : 28/02/2012.

INTRODUCTION

Geohydrological investigation was carried out at Village Dahej-GIDC area and based on these investigation details of existing ground water structures such as Tube Well, Bore Well & Open Well and on long term seasonal water level fluctuations of the area, were studied and based on these data this report has been prepared.

LOCATION AND EXTENT

GIDC Area is situated at Village Dahej in the South Western part of Vagra Taluka. The study area covering GIDC lies between 72^o 32' 50" to 72^o 37' 40" East longitude and 21^o 40' 41" to 21^o 44' 59" North latitude covered under Survey of India Topo sheet No. 46 C/10. The total geographical area of the Village Dahej is 30.02 Sq.Kms. The Dahej Village is connected by State Highway Bharuch-Dahej broad gauge railway line Sammi-Dahej. (Plate-1)

PHYSIOGRAPHY

The topography of the area is mainly plain with general slope towards Northwest and West direction.

DRAINAGE

The drainage of the area is controlled mainly by Gulf of Cambay.

CLIMATE

The area having tropical climate with summer season from mid March to mid June with maximum temperature up to 42^o, Winter season from November to February with minimum temperature up to 12^o and Monsoon season from mid June to October. The long term average rainfall of the taluka is 674 mm for the period 1963 to 2010 and short term average rainfall is 883 mm from 2002 to 2010.

GEOLOGY

Geologically the area comprises of alluvial formations of Recent to Sub Recent age. The geological succession in stratigraphical order is mentioned below.

ERA	PERIOD	AGE	LITHOLOGY
Cenozoic	Quaternary	Sub-Recent to Recent	Alluvium consisting of Sand & Clay Beds
	Tertiary	Lower Miocene	Clay

The alluvium deposit of Sub-Recent to Recent age is observed in the area. It consists of alternate bands of Yellowish brown clay and fine to coarse grained sand. The Tertiary formation consists of clay underlies the alluvium.

As the area is under the influence of sea water intrusion no efforts has been made by local farmers or existing industries for ground water exploration. GWRDC has drilled one piezometer at Village Dahej under Hydrology Project and drilled one more piezometer at Village Atali under Narmada Canal Command Area. However to know aquifer deposition in the BEL area it is necessary to construct exploratory bore well.

GEOHYDROLOGY:

The main hydrological unit in the area is alluvium formation. The alluvium formation mainly comprises of alternate bands of sand & clay. The sand formation consists of medium to fine grained and works as aquifer. The ground water in area is highly saline so no efforts have been done to extract ground water.

Two Piezometers are constructed by GWRDC under different projects in this area. At Atali piezometer, the depth to water level varies from 2.60 mts to 6.60mts, which has the depth of 12.00 Mts. At Dahej Piezometer having depth of 38.38 Mts, depth of water level ranges from 7.65 to 9.96 mts(Statement no 1) for year 2007-2011. BEL has drilled two nos of shallow bore well with a depth of 25.00 Mts. each. Water level observed in BEL bore well is 8.50 Mts to 7.90 Mts.

GROUNDWATER FLOW:

The general observation reveals that the flow of the groundwater generally controlled by topography of the area. As no efforts has been made to extract ground

water due to high salinity it is assumed that ground water generally follow the topography of the area and at Dahej village the topography is slopping towards Northwest and West direction so ground water flow should be towards Northwest and West direction.

GROUNDWATER SEASONAL FLUCTUATIONS:

To study the groundwater seasonal fluctuation in the area, the statement showing water level fluctuation of the existing monitoring station from the year 2007 to 2011 is studied. (Table No.I) The minimum water level ranges from 2.60 Mts. observed at village Atali of Vagra Taluka to 9.90 mts. at village Daheji of Vagra Taluka. The average seasonal fluctuation observed is 1.62 Mts to 2.39 Mts in the area.

GROUND WATER QUALITY:

To study the ground water quality water samples are collected from existing bore well constructed by BEL in their premises which indicate TDS 5110 ppm. the higher values of TDS is observed at BEL Bore well with a depth of 25.00 Mts which indicates that aquifer is saline with respect to TDS value. At Village Atali the TDS value ranges from 250 ppm to 570 ppm while at Village Dahej TDS value range from 3470 ppm to 4030 ppm. It is observed that higher values of TDS are observed at higher depth.

CONCLUSIONS:

- (1) Ground water level in the area ranges from 2.60 Mts to 9.90 Mts. bgl in the study area.
- (2) Ground water level fluctuation ranges from 1.62 Mts to 2.39 Mts.
- (3) From existing data of Piezometer constructed in study area it is presumed that first aquifer starts from 7.00 Mts to 12.00 Mts, second aquifer from 28.00 Mts to 37.00 Mts, whereas no information available for third aquifer as no structure is observed with higher depth.

RECOMMENDATIONS:

Based on existing bore well data and geohydrological investigation carried out in area, there are two aquifers at different depths. To know the exact depth of different aquifer in the study area, it is recommend to drill exploratory bore well with a depth of 60.00 Mts, or until the third aquifer is encountered in South East portion of the study area. (Plate-II) The bore well should be electro logged at pilot stage.

The specification of exploratory bore well is mentioned below.

Sr.No.	Bore No.	Bore Detail	Diameter in mm	Depth in Mts.
1	E-1	Exploratory	200 mm	60.00

Depending on the litho log of exploratory bore well, it is recommended to drill 3 nos. of piezometer nests with varying depth from 20.00 Mts to 60.00 Mts, tapping different aquifers.

The distance between the three different piezometer should be kept at least 15.00 Mts.

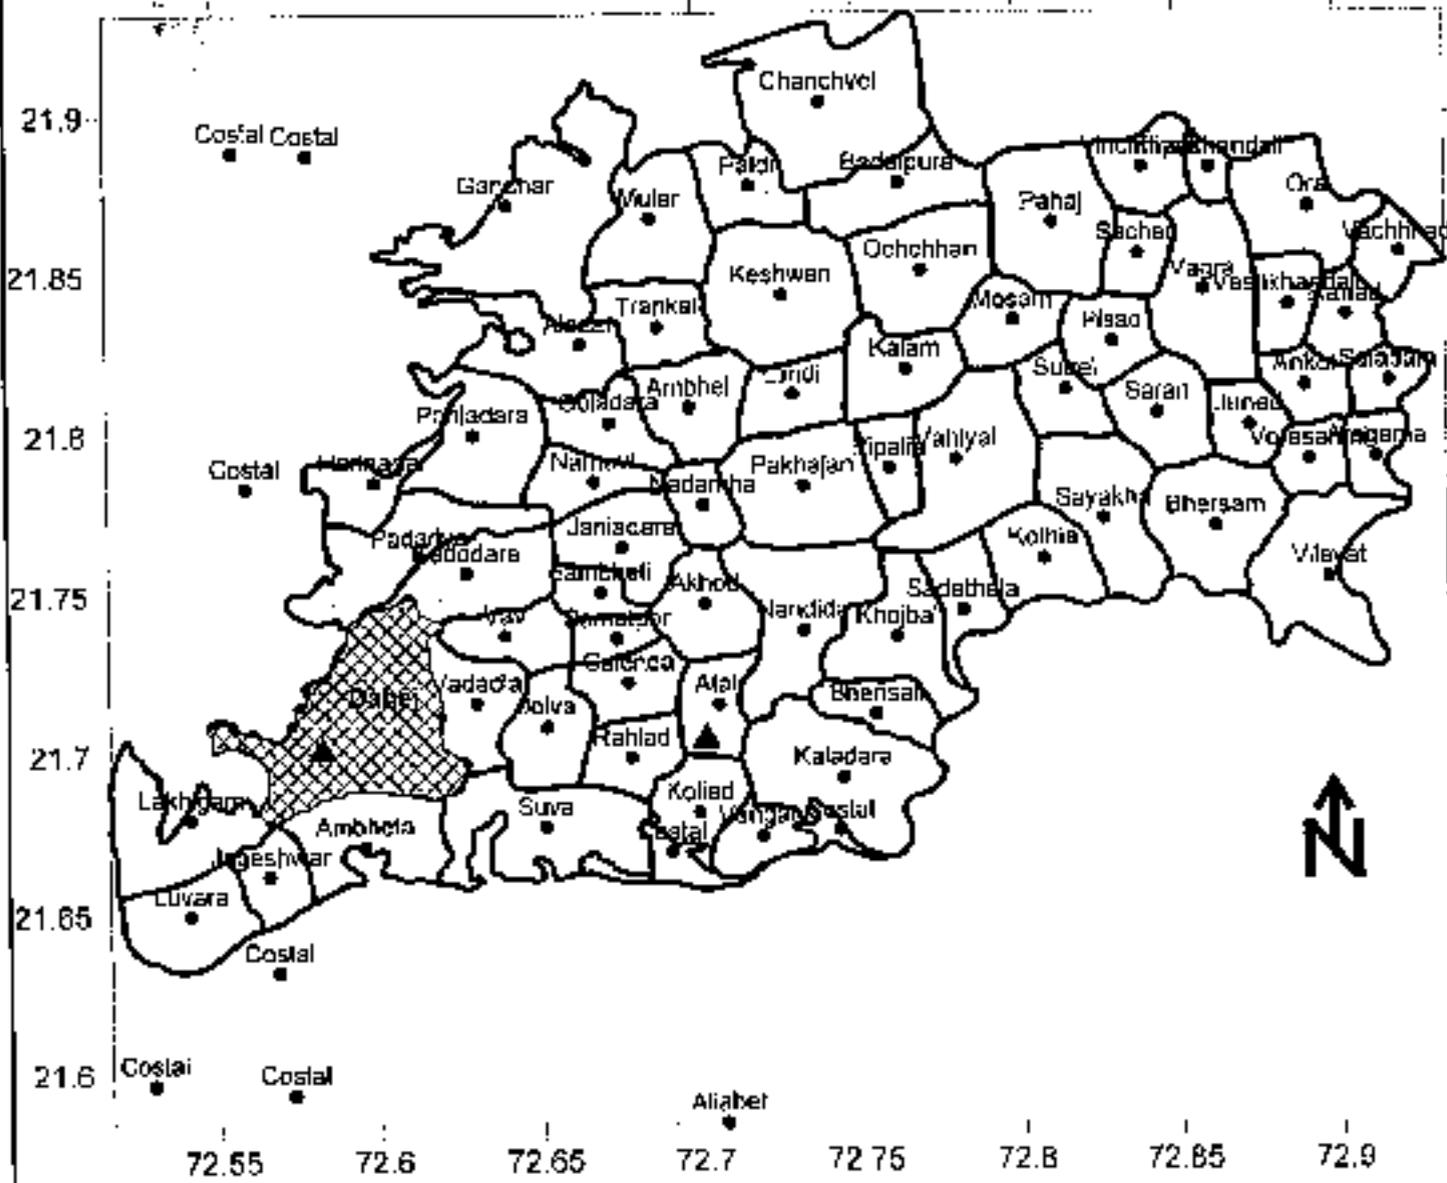
The details of set of bores comprising one piezometer nest to be drilled are mentioned below.

Sr.No.	Bore No.	Bore Detail	Diameter in mm	Depth in Mts.
1	P-1	First aquifer piezometer	150 mm	20.00
2	P-2	Second aquifer piezometer	150 mm	45.00
3	P-3	Third aquifer piezometer	150 mm	60.00

STATEMENT SHOWING WATER LEVEL AND QUALITY OF PIEZOMETERS DRILLED FOR LAST FIVE YEARS

Month/Year	VILLAGE ATAU			VILLAGE DAHEI		
	Water Level	Rise /fall	TDS in PPM	Water Level	Rise /fall	TDS in PPM
May-07	5.41		****	9.00		4010
Oct-07	3.14	2.30	430	7.80	1.20	3830
May-08	5.10		****	9.23		3730
Oct-08	3.30	1.80	440	8.46	0.77	3860
May-09	4.98		380	9.16		4030
Oct-09	3.84	1.14	370	8.64	0.52	3760
May-10	5.70		570	9.50		3960
Oct-10	2.60	3.10	440	6.15	3.35	3920
May-11	6.60		490	9.90		3470
Oct-11	3.00	3.60	290	7.05	2.25	3690
Average		2.39			1.62	

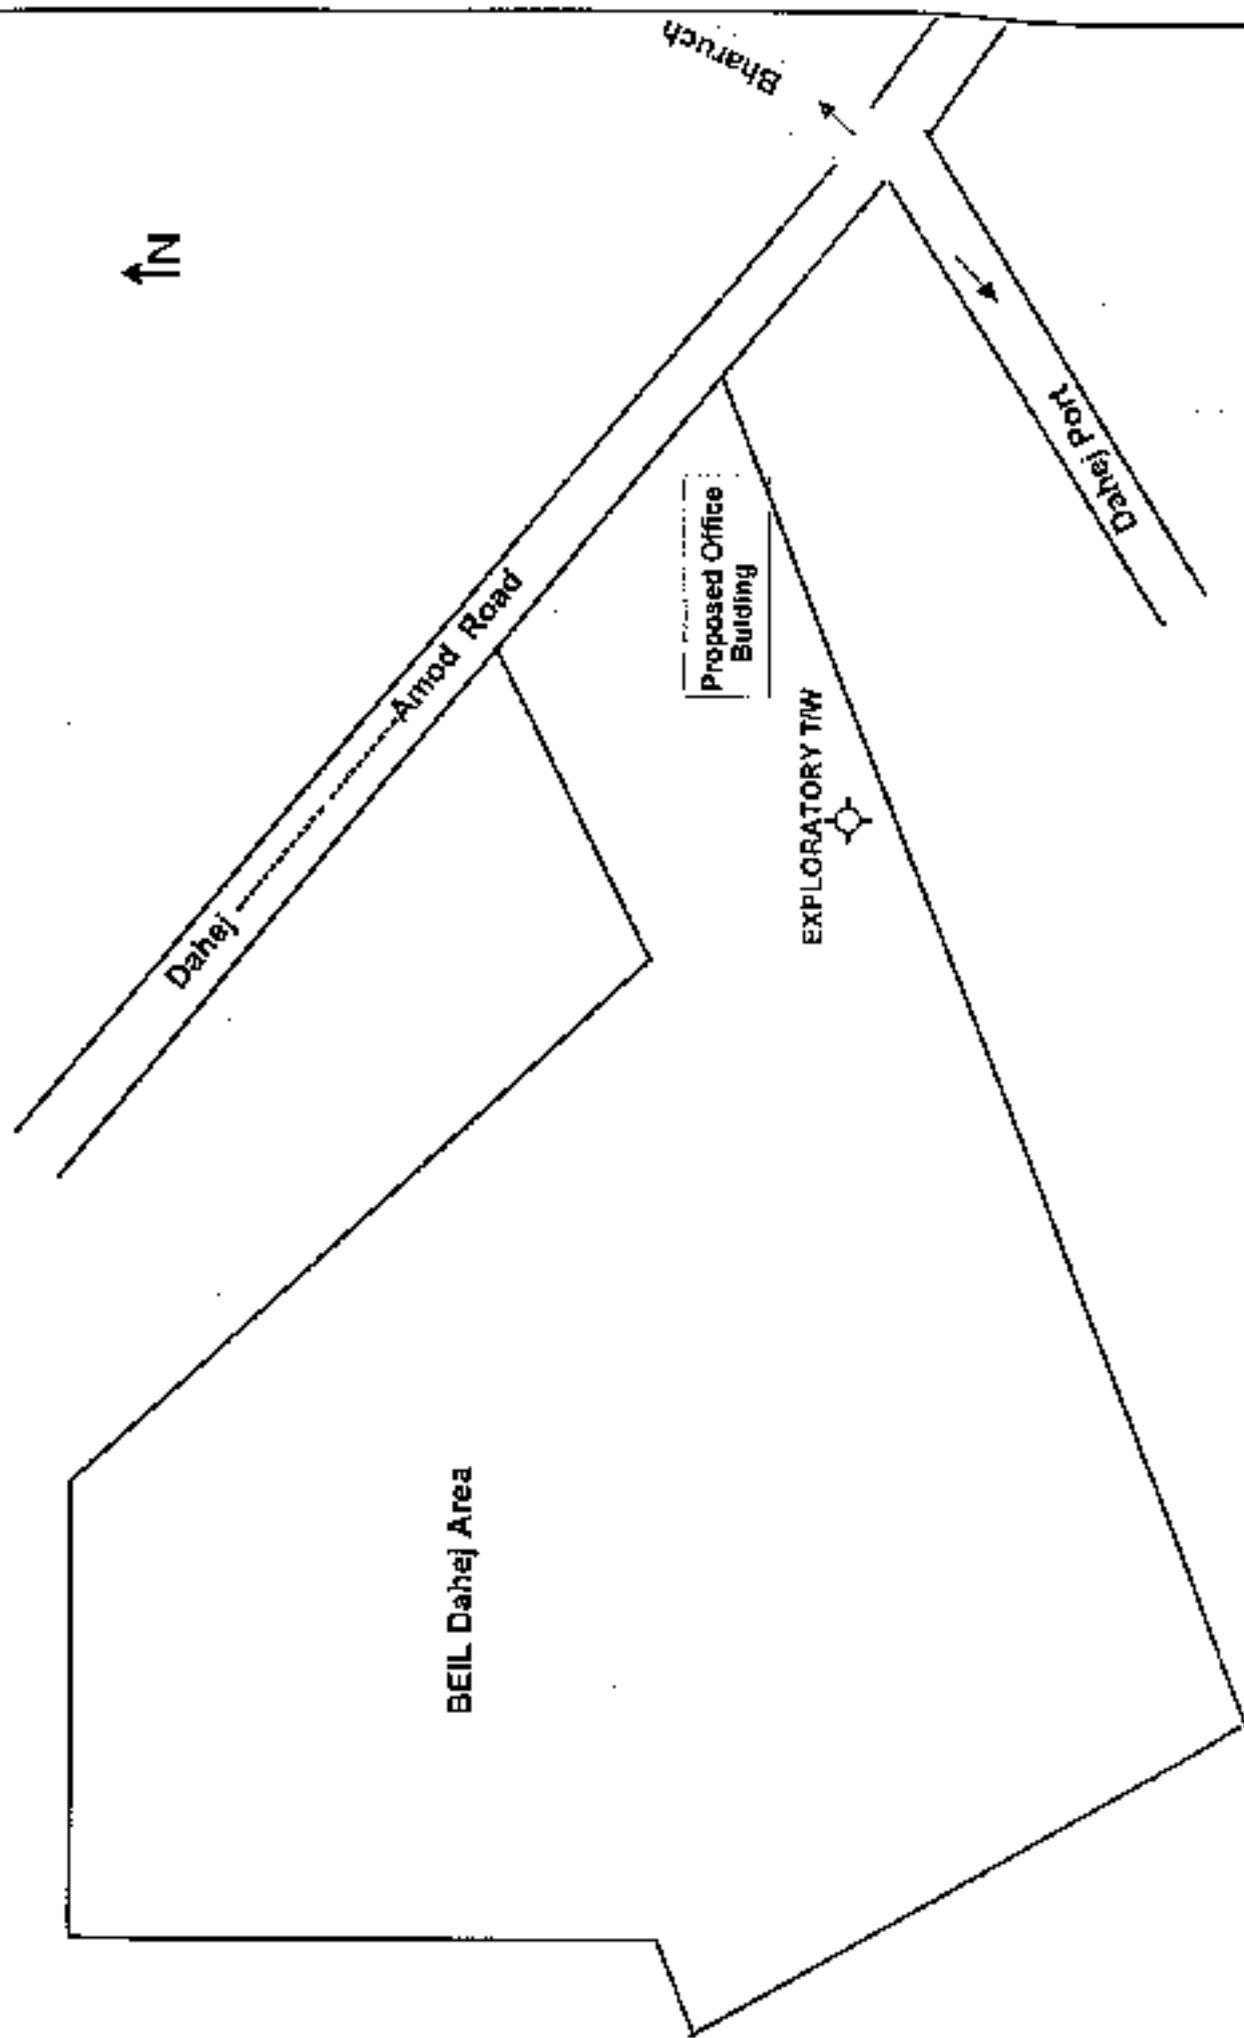
LOCATION PLAN OF VILLAGE DAHEJ TALUKA VAGRA DIST. BHARUCH



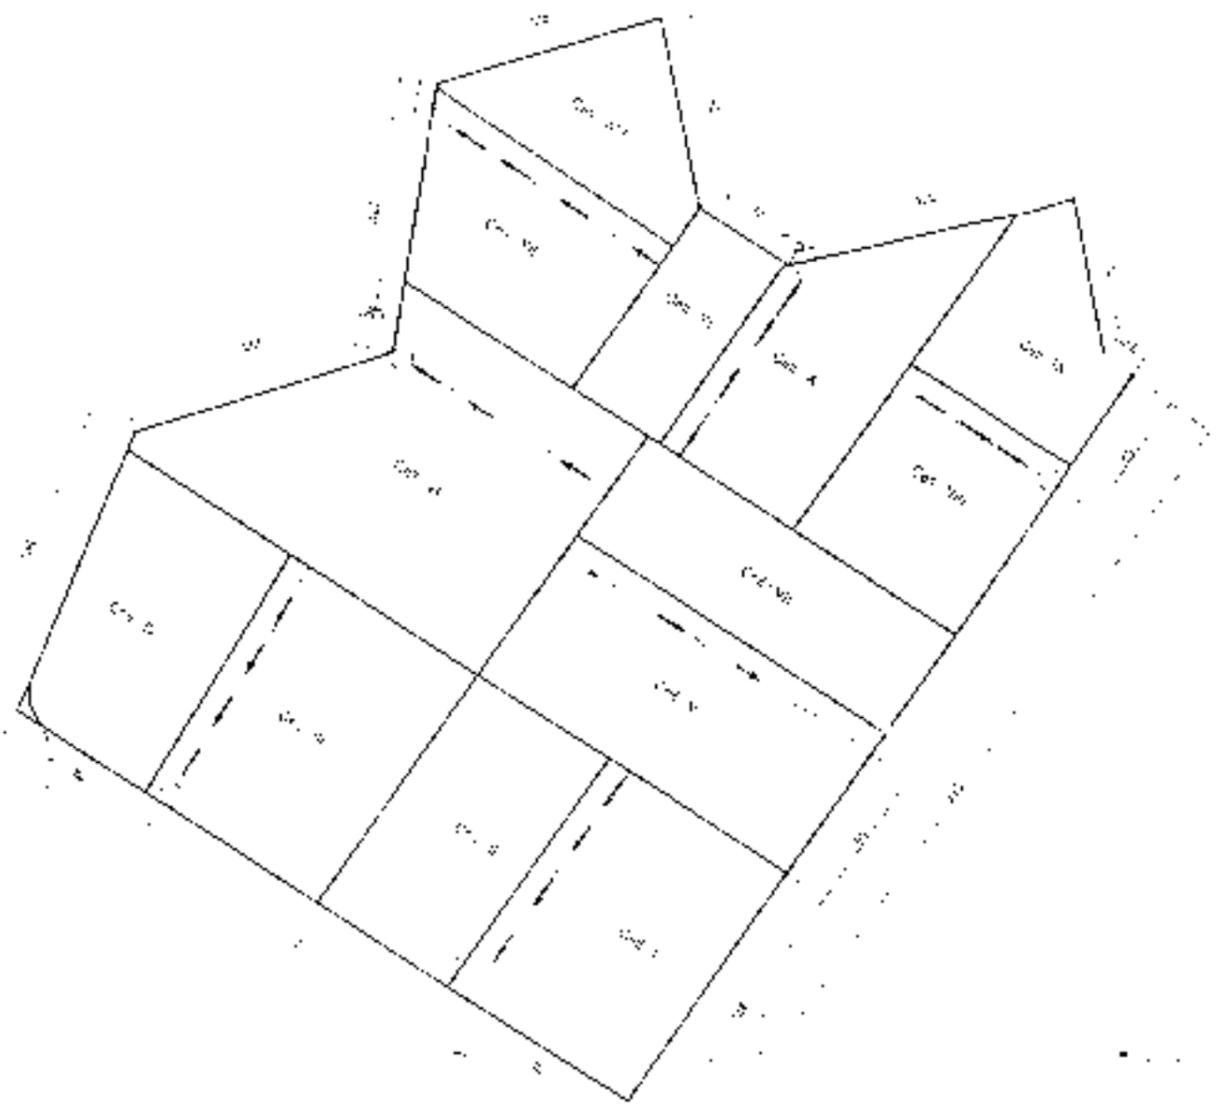
INDEX

-  VILLAGE DAHEJ
-  MONITORING PIEZOMETER

LOCATION PLAN FOR PROPOSED EXPLORATORY TUBE WELL AT BEIL SITE DAHEJ - TALUKA - VAGRA DIST. - BHARUCH



ANNEXURE 2



PLAN OF YEARLY PHASES OF LANDFILL

PLAN OF YEARLY PHASES OF LANDFILL

CONSTRUCTION OF SECURED LANDFILL FACILITY



BHARUCH ENVIRO INFRASTRUCTURE LIMITED



BHARUCH ENVIRO INFRASTRUCTURE LIMITED



INDIAN INSTITUTE OF TECHNOLOGY,
NEW DELHI

[Signature]
21/10
Dr. Manoj Datta
Professor
Civil Engineering Department
Indian Institute of Technology Delhi
Hauz Khas, New Delhi - 110016

[Signature]

FIG. NO. REV. DATE

SCALE
N.P.S.

PLAN OF LANDFILL

CONSTRUCTION OF SECURED LANDFILL FACILITY



BHARUCH ENVIRO INFRASTRUCTURE LIMITED




BHARUCH ENVIRO INFRASTRUCTURE LIMITED



INDIAN INSTITUTE OF TECHNOLOGY
NEW DELHI

[Handwritten signature]

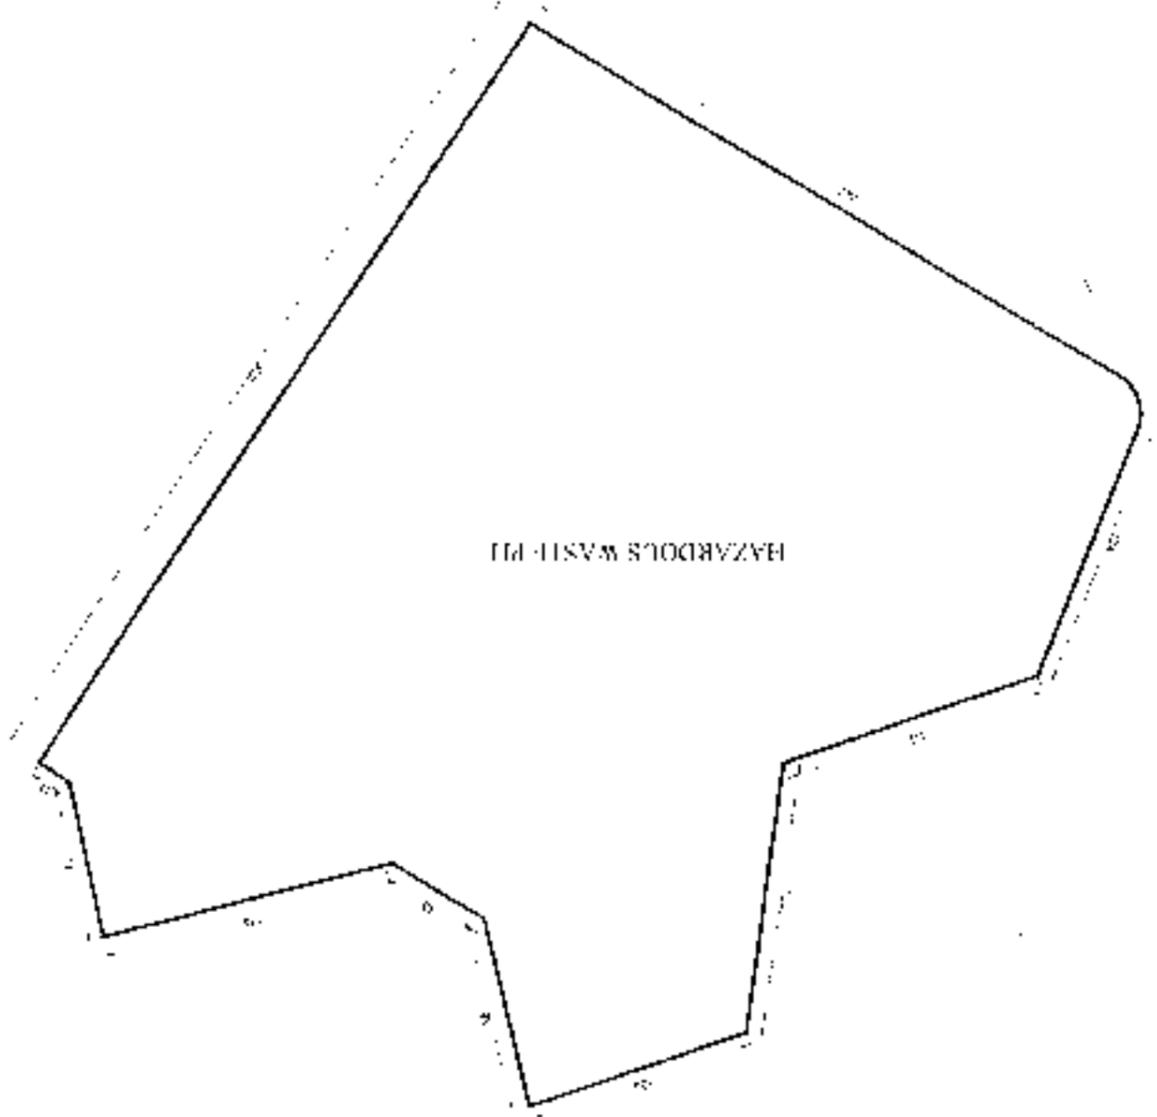
Dr. Manoj Kumar
Professor
Civil Engineering Department
Indian Institute of Technology
New Delhi - 110016



DRG NO. R/A DATE

SCALE
N.T.S.

PLAN OF LANDFILL





INDIAN INSTITUTE OF TECHNOLOGY, DELHI

Department of Civil Engineering

Hauz Khas, New Delhi – 110 016

Dr. Manoj Datta
Professor & Head

Phone: 26591163/26591241 (O)

Fax: 26581117/26882037

Email: mndatta@civil.iitd.ac.in

20/03/2015

IITD/CE/MD/2015/BEIL/Dah

To,
Mr. Ashok Panwani
Bharuch Enviro Infrastructure Limited
Dahaj
Gujarat

Dear Sir,

Kindly refer to the visit of undersigned on 11th March 2015 at your Dahaj site regarding the Cell I of Landfill of Bharuch Enviro Infrastructure Limited.

It is certified that the Cell I of Landfill is satisfactory for receiving hazardous waste in all respect as per CPCB guideline and drawings approved by IIT, Delhi.

Yours sincerely,

(Dr. Manoj Datta)



INDIAN INSTITUTE OF TECHNOLOGY, DELHI

Department of Civil Engineering

Hauz Khas, New Delhi – 110 016

Dr. Manoj Datta
Professor & Head

Phone: 26591183/26591241 (O)

Fax: 26581117/26862037

Email: mdatta@civil.iitd.ac.in

IITD/CE/MD/2016

4th March 2016

Sub: Technical Review of Secured Landfill of BEIL at Dahej for Hazardous Waste

Overview

The Secured (Hazardous Waste) Landfill Facility of Bharuch Enviro Infrastructure Limited at Dahej was assessed for compliance with HW Landfill Guidelines (HWLG) published by CPCB. The assessment was based on review of design documents, review of drawings, site visit on 16th Feb 2016, inspection of active phase (under construction) and review of records and associated documents.

Review Report

- Landfill Design:** The methodology of design, construction and operation is satisfactory.
- Landfill Layout:** Plan and layout depicts phased operation.
- Landfill Section:** Landfill side slopes, liner and cover provisions are as per design.
- Phased Operation:** Landfill is operated in yearly phases.
- Leachate Quantity:** Generation of leachate is minimized by keeping exposed active area small.
- Liner System:** Liner System is as per HW landfill guidelines. All essential components (including HDPE geomembrane and barrier soil layer) meet minimum requirements as specified.
- Leachate Collection and Removal:** Leachate collection layer, drainage slopes, collection sump, leachate well and other components all comply with HW guidelines
- Leachate Management:** Multiple effect evaporator (offsite).
- Gaseous Emissions Management:** Gas collection layer and passive venting provided in design.
- Final Cover System:** Gas collection layer, barrier layer, HDPE geomembrane, drainage layer, top soil and vegetation grass / rubble + vegetation meet HW guidelines.
- Surface Water Drainage System:** Berms, drainage channels and surface water drain provided adequately
- Slope Stability:** Adequate safety against slippage along interfaces of different layers.

Site Infrastructure: Fencing, office, road, laboratory, drainage system, weighbridge, waste inspection, temporary storage, waste stabilization facilities as per standards

Environmental Monitoring System: Ground water wells installed.

Site Development: Planned in phases.

Record Keeping: Satisfactory.

Waste Inspection: Adequate facilities.

Phase Development and operation: Yearly

Phase Closure: HW cover to be provided on completion of each phase.

Landfill Closure: Progressive closure and joining of cover system with completion of progressive phases.

Vegetative Cover: Local vegetation or grass / rubble with local vegetation

Post Closure Maintenance System: Provision of post-closure funds.

Conclusions

Cells 2 and 5 are observed to be designed in accordance with Hazardous Waste Landfill Guidelines of CPCB and drawings approved vide IIT Delhi consulting project and are ready to receive the waste.



(Dr. Manoj Datta)



INDIAN INSTITUTE OF TECHNOLOGY, DELHI

Department of Civil Engineering

Hauz Khas, New Delhi – 110 016

Dr. Manoj Datta
Professor

Phone: 26591183/26591241 (O)

Fax: 26581117/26862037

Email: mdatta@civil.iitd.ac.in

IITD/CE/MD/2019

7th June 2019

Mr. Manoj Patel,
Bharuch Enviro Infrastructure Limited
Plot No. D-43
Dahej-Amod Road
GIDC Estate, Ta-Vagra
Dahej – 392130, Dist.: Bharuch (Gujarat)

Sub: Technical Review of Closure of Cell 5, Construction of new Cells-3 & 4 and Monsoon Storage Shed (second part) at Secured Landfill of BEIL, at Dahej for Hazardous Waste

Overview

The Secured (Hazardous Waste) Landfill Facility of Bharuch Enviro Infrastructure Limited at Dahej was assessed for compliance with HW Landfill Guidelines (HWLG) published by CPCB for construction of new Cells 3 and 4. The assessment was based on review of design documents, review of drawings, site visit on 1st May 2019, inspection of construction work as well as review of records and associated documents. Closure activities on Cell 5 were reviewed. Base liner system of monsoon storage shed (second part) was also reviewed.

Review Report

Const. of Cells-3&4	(a) Construction of Cells 3&4 completed; inspected during site visit. (b) All components installed as per design. (c) Side slopes as per design. (d) Geosynthetic materials and soil layers as per specifications. (e) Thickness of components adequate. (f) Drainage layers as per design. (g) Separation and filtration layers as per design.
Monsoon Storage Shed	(a) Second part of monsoon storage shed inspected visually. (b) Base liner system is as per design and construction completed.
Closure of Cell 5	(a) Work underway; operations inspected during site visit
Landfill Design:	Design, construction and operating methodology is satisfactory.
Landfill Layout:	Layout meets requirements of phased operation.
Landfill Section:	Landfill side slopes, liner and cover provisions are as per design.
Phased Operation:	Operation is in yearly phases.

Leachate Quantity:	Minimized by temporary covering during monsoons. All leachate pumped out and treated.
Liner System:	In accordance with HW landfill guidelines. All essential components (including HDPE geomembrane and barrier soil layer) meet minimum requirements as per guidelines.
Leachate Collection and Removal:	Leachate collection layer, drainage slopes, collection sump, well and other components all comply with HW guidelines.
Leachate Management:	Spray Drier and MEE
Gaseous Emissions:	Gas collection layer and passive venting.
Final Cover System:	Gas collection layer, barrier layer, HDPE geomembrane, drainage layer, top soil and vegetation / rubble + vegetation meet HW guidelines/equivalence.
Surface Water Drainage:	Berms, drainage channels and surface water drain provided adequately.
Slope Stability:	Slope inclination as per design.
Site Infrastructure:	Boundary wall, road, laboratory, drainage system, weighbridge, waste inspection, temporary storage, waste stabilization facilities as per standards.
Environmental Monitoring:	Ground water wells for monitoring.
Site Development:	Well planned.
Record Keeping:	Satisfactory.
Waste Inspection:	Adequate facilities.
Phase Development and Operation:	Yearly.
Phase Closure:	HW cover system provided on completion of each phase (or part thereof).
Landfill Closure:	Progressive closure and joining of cover system with completion of each phase.
Vegetative Cover:	Local vegetation or grass / rubble with vegetation.
Post Closure Maintenance System:	Provision of funds for maintenance after closure

Conclusions

Construction drawings and photographs were reviewed during site visit and various components of the liner system were visually inspected and found satisfactory. It is observed that construction work of liner and leachate collection system of new cells 3 & 4 had been completed in all respects as per CPCB Guidelines and drawings approved by IIT Delhi. Closure of Cell-5 is underway and operations are satisfactory. Base liner system of monsoon storage shed (second part) has been completed.

Cells 3 & 4 are now ready to receive the waste. Base liner system of monsoon storage shed (second part) is also ready to receive waste.



(Dr. Manoj Datta)

ANNEXURE 3



Ref.: BEIL/DHU/2021-22/14

12th June 2021

The Member Secretary,
Gujarat Pollution Control Board,
Paryavaran Bhavan,
Sector -10/A
Gandhinagar- 382010

Sub: Compliance to observations and recommendations of Environmental Audit for the Half year
(April 2020 to September 2020)

Dear Sir,

We have submitted half yearly Environment Audit Report for April 2020 to September 2020 to H.O.
GPCB Gandhinagar along with fees on 16.03.2021. The audit was carried out by Parul Institute.

We would like to bring your kind attention that we are complying to various observations and
recommendations of the auditor.

The compliance of observation and recommendations of the Auditor are enclosed.

We hope that above is in the order.

Thanking You,

Yours faithfully,
For, BEIL Infrastructure Limited

Authorized Signatory

Encl: a/a

CC:
Regional office
Gujarat Pollution Control Board
Bharuch

17/6/2021
Post Received
Gujarat Pollution Control Board
BHARUCH

CIN NO. U45300GJ1997PLC032896

Works Office : Plot No. D-43, Dahej Amod Road, GIDC Estate, Dahej, T. Vagra - 392 130, Dist. Bharuch (Gujarat)
Phone : (02641) 291129, E-mail : mistryrg@beil.co.in
Regd. Office : Plot No. 9701-16, GIDC Estate, Post Box No. 82, Ankleshwar 393 002, Dist. : Bharuch (Gujarat)
Phones (02646) 253135, 225228 Fax : (02642) 222849 E-mail : dalwad@beil.co.in



BHARUCH ENVIRO INFRASTRUCTURE LTD.

(Unit - Dahej)

CIN-U45300GJ1997PLC032696

Date: 20/5/2016
PCB ID NO: 40137

To,
The Member Secretary
Gujarat Pollution Control Board
Paryavaran Bhavan
Gandhinagar

Sub: Submission of Inspection Report and Testing Reports for Construction of Cell:2 & 5 at Plot No:43, GIDC, Dahej.

Dear Sir,

In connection with above subject and telephonic instruction from your office to expedite submission of third party reports.

Please find submitted herewith inspection report of the agency appointed by BEIL (IIT, New Delhi) covering third party certificate, testing reports, photographs, approved drawing, methodology for construction, methodology adopted for construction, summary of test report required by CPCB and executed by BEIL.

Kindly note that we have submitted status report to office of R.O, Bharuch by email on dated 1/1/2016 and 22/1/2016. (Copy Enclosed).

In view of above you are humbly requested to consider this reports as part of compliance of CPCB guideline for construction Cell: 2 & 5.

Request you to process our application and give us CC & A for Cell: 2 & 5 at the earliest.

Thanking you,

Yours faithfully,
For Bharuch Enviro Infrastructure Limited

B.D. Dalwadi
Chief Executive Office

Encl: As Above

c.c: The Regional Office - GPCB, Bharuch

Post Received
Gujarat Pollution Control Board
BHARUCH
21/5/16

Works Office : Plot No. D-43, Dahej, Amod Road, GIDC Estate, Dahej, Ta-Vagra - 392130, Dist. : Bharuch (Gujarat)
Phones : (02644) 291129 • Email : bhupendra.mahia@uniphos.com
Head Office : Plot No. 9701-16, GIDC Estate, Post Box No. 62, Ankleshwar - 393 002, Dist. : Bharuch (Gujarat)
Phones : (02646) 253135, 225228 • Fax : (02643) 222849 • E-mail : panjwani@uniphos.com
Regd. Office : Plot No. 117-118, GIDC Estate, Ankleshwar - 393 002, Dist. : Bharuch (Gujarat)

ANNEXURE 4

Annexure 00

Compliance of CPCB Criteria for Hazardous waste landfill

Sr. No.	Conditions	Status
1.	<p>Location Criteria:</p> <ul style="list-style-type: none"> - Lake or Pond : 200 Mtrs - River : 100 Mtrs - Flood plain : 100 years - Highway : 500 Mtrs - Habitation : 500 Mtrs - Public Parks : 500 Mtrs - Critical habitat Area : No landfill - Wet Lands: No landfill - Airport : No Landfill - Water Supply: 500 Mtrs - Coastal Regulation Zone : No landfill - Ground Water table level: < 2 meters below the base 	<p>Complied</p> <p>Landfill is located in Vagra Taluka fulfilling all the criteria mentioned in the guidelines. Nearest railway station is at about 50 Km, Bharuch. Nearest village is at about 3.76 KM, Dahej. Nearest airport is at about 75 Km, Vadodara. The project site is located about 43.7 km away from National Highway No. 8, 0.44 km and 33.87 km away from State Highway No 6 and 37. The CRZ area is about 7.0 Km away from the project site.</p>
2.	<p>Planning And Design criteria:</p> <p>1. Essential Components:</p> <ul style="list-style-type: none"> - Liner System at base and sides of landfill - A leachate collection and treatment facility - Gas collection and treatment facility - Final cover system at top - Surface water drainage system - Environmental monitoring system - Closure and post closure plan 	<p>Complied</p> <p>Appropriate base and side liners has been provided according to the criteria. Leachate collection wells (Total 4 wells for the cell 1, cell2 & cell5, cell3, cell4 & Monsoon cell) has been provided for collecting leachate which further treated in MEE followed by Spray dryer. At present only cell 1 & cell 5 are partially capped, Surface water drainage system is provided.</p>
	<p>2. Phased Operation:</p> <ul style="list-style-type: none"> - During the monsoon months the waste may stockpiled in a temporary holding area (covered with roof). During this period and the landfill may be kept capped with final cover/ intermediate cover and landfill operations suspended to reduce infiltration of rainwater into the landfill. 	<p>Complied.</p> <p>Landfill site operation is being suspended during the 4 months of monsoon. We have constructed monsoon landfill cell of capacity 20000 MT having impervious bottom and roof cover has been provided. Landfill which is in operation is covered</p>

		with tarpaulin during these periods.
	<p>3. Liner system:</p> <ul style="list-style-type: none"> - Leachate control within a landfill involves the following steps: (a) prevention of migration of leachate from landfill sides and landfill base to the subsoil by suitable liner system; and (b) drainage of leachate collected at the base of a landfill to the side of the landfill and removal of the leachate from within the landfill. 	<p>Complied</p> <p>A proper base and side liners has been provided according to the criteria. Drainage system is also provided to avoid infiltration of surface water.</p>
	<p>4. Leachate Management:</p> <ul style="list-style-type: none"> - Offsite Treatment - Onsite Treatment - Recirculation 	<p>Complied</p> <p>Leachate collection wells (Total 4 wells for the cell 1, cell2, cell5, cell3, cell4 & Monsoon cell) has been provided and collected leachate is treated onsite in MEE. Leachate is recirculated accelerating process of landfill stabilization.</p>
	<p>5. Gaseous Emission Management:</p> <ul style="list-style-type: none"> - Controlled passive venting - Controlled collection and treatment 	<p>Complied</p> <p>At present only Cell 1 & Cell 5 are partially capped.</p>
	<p>6. Final Cover System</p>	<p>Complied</p> <p>At present Cell-1 & Cell 5 are only partially capped, while no other cells are closed. Closure of the Cell will be according to the Guidelines.</p>
	<p>7. Site Infrastructure:</p> <ul style="list-style-type: none"> - Site Entrance and Fencing. - Administrative and Site Control Offices - Access Roads - Waste Inspection and Sampling Facility. - Equipment Workshops and Garages. - Signs and Directions - Water Supply - Lighting - Vehicle Cleaning Facility - Fire Fighting Equipment 	<p>Complied</p> <p>All the facilities like site entrance and fencing, administration, site control offices, access roads, waste inspection, sampling facility, water supply, lightings, vehicle cleaning facility, firefighting equipment, signs and directions etc. have been provided.</p>
	<p>8. Environment Monitoring System:</p>	<p>Complied</p> <p>Regular monitoring of leachate quality, air quality, and noise is being carried out. Monitoring of ground water, leachate, VOC generation, ambient air monitoring, noise monitoring has been conducted on regular basis. All the analysis reports are</p>

		attached.
	9. Closure and post closure maintenance plan:	Complied At present only Cell-1 & Cell-5 are only partially capped, while no other cells are closed. Closure of the Cell will be according to the Guidelines.
3.	Waste Acceptance Criteria	Complied On arrival of any waste, it is first analyzed and if it follows GPCB/CPCB waste acceptance criteria then only then it is accepted.
4.	Construction and operational Criteria: <ul style="list-style-type: none"> - Site Development - Phase development - Phase operation - Phase closure - Landfill closure - Post closure vegetative stabilization 	Complied Proper facilities for site development like record keeping for site manual, site reports, vehicle inspection is provided.
5.	Inspection, Monitoring and record keeping criteria: <ul style="list-style-type: none"> - During construction of liners and covers - During operation - During closure and post closure period - Environmental Monitoring System 	Complied Regular inspections of liners, and covers was being conducted during construction phase of landfill. Adequate environmental monitoring system has been provided.
6.	Financial Assurance Criteria	Complied We have prepared detailed financial estimates for construction, operation, and closure and post closure activity of the landfill.
7.	Contingency Plan for Emergency	Complied We are having onsite emergency plan, which is updated on yearly basis and submitted to GPCB, RO.

ANNEXURE 5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
1	2ef1bddb0c			24-MAR-21 10:18:50	30-Mar-2021 16.18	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	19500.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	2.6	NO	16.18	ODOURLESS	PASS	7.5
2	856a7eed90			28-MAR-21 08:34:16	30-Mar-2021 11.34	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	18330.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	3.5	NO	32.76	ODOURLESS	NOT PASS	7.5
3	99e6add18b			29-MAR-21 11:23:30	30-Mar-2021 14.27	ETP SLUDGE (34.3)	SOLID	GYP SUM SLUDGE	19100.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	9.4	NO	34.28	ODOURLESS	PASS	7.5
4	203d3a8476			29-MAR-21 23:10:50	30-Mar-2021 09.28	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	1050.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
5	549a48c802			30-MAR-21 01:33:02	30-Mar-2021 09.24	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	1810.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
6	402ef91550			30-MAR-21 03:00:25	30-Mar-2021 09.25	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	720.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
7	62bba1e871			30-MAR-21 05:50:46	30-Mar-2021 09.27	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	1810.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
8	d6e98909c8			30-MAR-21 09:50:10	30-Mar-2021 14.01	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	18310.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	17.8	NO	44.32	ODOURLESS	NOT PASS	7.5
9	647f28b707			30-MAR-21 09:56:18	30-Mar-2021 14.03	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	20330.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	17.08	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
10	9a7f027dbe			30-MAR-21 10:33:32	30-Mar-2021 16.36	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	17380.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	2.0	NO	21.38	ODOURLESS	PASS	7.5
11	64194f2b17			30-MAR-21 10:47:50	30-Mar-2021 14.23	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	17460.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	20.2	NO	52.67	ODOURLESS	PASS	7.5
12	244d3c6450			30-MAR-21 10:49:58	30-Mar-2021 16.45	PROCESS RESIDUE WASTE (29.1)	SOLID	MAP SALT	2130.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
13	768535e861			30-MAR-21 11:10:56	31-Mar-2021 10.00	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	690.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
14	32e37d02a1			30-MAR-21 11:41:51	30-Mar-2021 14.24	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	16010.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	18.2	NO	47.35	ODOURLESS	NOT PASS	7.5
15	e3ebed348a			30-MAR-21 12:09:07	30-Mar-2021 14.26	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	14380.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	16.4	NO	39.19	ODOURLESS	PASS	7.5
16	ce4f2d906c			30-MAR-21 12:38:25	30-Mar-2021 16.46	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	1710.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
17	e939506fd1			30-MAR-21 14:11:50	30-Mar-2021 16.58	ETP SLUDGE (34.3)	SOLID	LANDFILL WASTE	15650.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	12.24	ODOURLESS	PASS	7.5
18	404b6bb489			30-MAR-21 14:14:34	30-Mar-2021 20.01	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	9410.000	8.65	COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	23.57	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
19	9b466b4c3b			30-MAR-21 14:24:15	30-Mar-2021 17.00	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	16370.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	2.0	NO	20.86	ODOURLESS	PASS	7.5
20	91ef89b395			30-MAR-21 14:55:42	30-Mar-2021 16.48	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	4090.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
21	e23689f8e6			30-MAR-21 14:58:02	30-Mar-2021 17.03	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	17770.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	17.2	NO	41.52	ODOURLESS	PASS	7.5
22	23cc7af4e8			30-MAR-21 14:59:43	30-Mar-2021 17.01	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	17820.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	4.2	NO	31.06	ODOURLESS	PASS	7.5
23	32f9d64f54			30-MAR-21 15:19:55	30-Mar-2021 16.54	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	3120.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
24	cae49c816a			30-MAR-21 15:22:20	30-Mar-2021 16.57	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	3210.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
25	ed4678d702			30-MAR-21 15:29:11	30-Mar-2021 17.08	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	16620.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	18.2	NO	40.56	ODOURLESS	PASS	7.5
26	f19110f23a			30-MAR-21 15:31:38	30-Mar-2021 17.04	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	17360.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	19.4	NO	47.82	ODOURLESS	PASS	7.5
27	3a2e1c21d9			30-MAR-21 15:43:26	30-Mar-2021 17.11	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	16510.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	1.0	NO	18.15	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
28	139de6e88a			30-MAR-21 15:54:18	30-Mar-2021 17.13	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	17650.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	23.0	NO	49.09	ODOURLESS	PASS	7.5
29	a7c43af350			30-MAR-21 15:59:16	30-Mar-2021 17.10	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	16300.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	1.8	NO	21.67	ODOURLESS	PASS	7.5
30	af182df869			30-MAR-21 16:32:38	30-Mar-2021 17.25	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	13630.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	1.2	NO	20.45	ODOURLESS	PASS	7.5
31	b0d7134650			30-MAR-21 16:34:51	30-Mar-2021 17.30	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	18620.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	16.2	NO	40.32	ODOURLESS	PASS	7.5
32	a7e9e605eb			30-MAR-21 17:55:56	30-Mar-2021 20.03	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	1120.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
33	c7981b336e			31-MAR-21 07:27:36	31-Mar-2021 11.52	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	16940.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	17.8	NO	51.18	ODOURLESS	PASS	7.5
34	4255ec75b7			31-MAR-21 07:30:01	31-Mar-2021 11.49	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	12880.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	13.6	NO	67.13	ODOURLESS	NOT PASS	7.5
35	cad4cc71a7			31-MAR-21 07:33:37	31-Mar-2021 11.50	INSULATION WASTE (31.1)	NON RECYCLE WASTE	INSULATION WASTE	2230.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
36	fb46453622			31-MAR-21 07:36:16	31-Mar-2021 11.53	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	BRINE SLUDGE	18210.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	19.0	NO	54.88	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
37	305f229b0b			31-MAR-21 07:40:46	31-Mar-2021 12.02	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	21380.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	13.79	ODOURLESS	PASS	7.5
38	19599f5e81			31-MAR-21 07:46:56	31-Mar-2021 12.10	RESIDUE/SLUDGES AND FILTER CAKES (16.2)	SOLID	FILTER CAKES	6500.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	15.6	NO	48.91	ODOURLESS	NOT PASS	7.5
39	343b5d9d81			31-MAR-21 08:15:57	31-Mar-2021 12.17	ETP SLUDGE (34.3)	SOLID	CHEMICAL SLUDGE	6840.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	7.37	ODOURLESS	PASS	7.5
40	1b51af2733			31-MAR-21 08:18:21	31-Mar-2021 12.11	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	19540.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	29.6	NO	57.48	ODOURLESS	PASS	7.5
41	1c39acf47e			31-MAR-21 08:21:20	31-Mar-2021 12.12	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	17040.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	5.8	NO	32.06	ODOURLESS	PASS	7.5
42	de7c61d35f			31-MAR-21 08:24:13	31-Mar-2021 12.19	INSULATION WASTE (31.1)	NON RECYCLE WASTE	INSULATION WASTE	1870.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
43	c7a6b8d343			31-MAR-21 08:29:36	31-Mar-2021 12.18	INSULATION WASTE (31.1)	NON RECYCLE WASTE	INSULATION WASTE	1570.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE		NO		ODOURLESS	PASS	
44	6b464339c9			31-MAR-21 08:41:07	31-Mar-2021 12.15	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	14000.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	12.75	ODOURLESS	PASS	7.5
45	2f19d4a142			31-MAR-21 08:44:49	31-Mar-2021 12.14	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	17190.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	23.2	NO	49.28	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
46	867e755ef2			31-MAR-21 08:50:28	31-Mar-2021 12.21	ETP SLUDGE (34.3)	SOLID	CHEMICAL SLUDGE	7380.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	11.96	ODOURLESS	PASS	7.5
47	ee16908b7b			31-MAR-21 09:27:02	31-Mar-2021 12.30	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	21410.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	14.84	ODOURLESS	PASS	7.5
48	2430531e04			31-MAR-21 09:29:43	31-Mar-2021 12.29	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	21220.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	13.49	ODOURLESS	PASS	7.5
49	c31fbdefbf			31-MAR-21 09:31:48	31-Mar-2021 12.33	ETP SLUDGE (34.3)	SOLID	LANDFILL WASTE	15560.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	6.5	NO	34.56	ODOURLESS	PASS	7.5
50	9313d5ea5e			31-MAR-21 09:34:30	31-Mar-2021 12.27	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	21400.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	12.18	ODOURLESS	PASS	7.5
51	8e045bb300			31-MAR-21 09:36:56	31-Mar-2021 12.24	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	21540.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	11.75	ODOURLESS	PASS	7.5
52	36855ea049			31-MAR-21 09:39:44	31-Mar-2021 12.22	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	20390.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	13.79	ODOURLESS	PASS	7.5
53	44c0dbd629			31-MAR-21 09:42:16	31-Mar-2021 12.35	PROCESS RESIDUE WASTE (29.1)	SOLID	MEE SALT	18960.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	5.2	NO	31.04	ODOURLESS	PASS	7.5
54	b1301529ce			31-MAR-21 09:44:49	31-Mar-2021 12.37	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	19160.000		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	17.28	ODOURLESS	PASS	7.5

Receipt Date From: 30-MAR-2021

FINGERPRINT ANALYSIS REPORT - LANDFILL

Receipt Date To: 31-MAR-2021

Sr No	ID	MANIFEST	CUSTOMER	Inward Date	Analysis Date	Waste Type / Category No	Physical State	Product Code	Quantity (KG)	*ANNEALING LOSS	COMPARISON WITH STD	COMPATIBILITY TEST	FLAMMABILITY TEST	LRT TEST	METAL STABILIZATION REQUIRED	MOISTURE CONTENT	ODOR	PFLT TEST	PH
55	11bf21f646			31-MAR-21 09:47:17	31-Mar-2021 12.50	ETP SLUDGE (34.3)	SOLID	ETP WASTE	14995.0 00		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	8.8	NO	39.18	ODOURLESS	PASS	7.5
56	fdaf8c295c			31-MAR-21 09:51:32	31-Mar-2021 12.43	ETP SLUDGE (34.3)	SOLID	ETP WASTE	15460.0 00		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	7.8	NO	37.47	ODOURLESS	PASS	7.5
57	80f7143745			31-MAR-21 09:58:22	31-Mar-2021 14.05	ETP SLUDGE (34.3)	SOLID	LANDFILL WASTE	23410.0 00	7.42	COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	2.06	ODOURLESS	PASS	7.5
58	4b4162b872			31-MAR-21 10:04:58	31-Mar-2021 12.41	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	17390.0 00		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	17.8	NO	56.70	ODOURLESS	PASS	7.5
59	ebe967fa7a			31-MAR-21 11:00:54	31-Mar-2021 12.40	ETP SLUDGE (34.3)	SOLID	ETP SLUDGE	19140.0 00		COMPARABLE	COMPATIBLE	NON-FLAMMABLE	0.0	NO	8.19	ODOURLESS	PASS	7.5

ANNEXURE 6

**TEST REPORT**

QF/7.8/37-WT

Page: 1 of 2

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0054**Issue Date : **13/10/2020**Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**Sampling Location : **EB 1 Up stream**

Description of Sample : **Ground Water sample** Quantity/No. of Samples : **05 Lit./One**
Date of Sampling : **03/10/2020** Sampling Procedure : **IS:3025**
Sampling by : **Pollucon Laboratories Pvt. Ltd.** Protocol (purpose) : **QC/Env. Monitoring**
Sample Receipt Date : **05/10/2020** Lab ID. : **BLD/2010/02**
Packing/ Seal : **Sealed** Test Parameters : **As per table**
Date of Starting of Test : **05/10/2020** Date of Completion of Test : **13/10/2020**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.38	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	14.5	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	56.4	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.86	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	8.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	381.46	IS 3025 (Part-16) 2017
7	TOC	mg/L	18	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	86	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4204	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	360	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	2.1	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	19324	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3524	IS 3025 (Part 24) 2019
14	Nitrate	mg/L	6.06	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.45	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Macky Suraliwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Page: 2 of 2

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0054**Issue Date : **13/10/2020**Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**Sampling Location : **EB 1 Up stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.14	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	350	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	798	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	12242	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	356	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	6.3	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni:0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L,O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognized by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- CPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Page: 1 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0055 Issue Date : 13/10/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : EB 2 Down Stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 03/10/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 05/10/2020	Lab ID. : BLD/2010/03
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 05/10/2020	Date of Completion of Test : 13/10/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.46	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	11.6	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	54.6	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.68	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	7.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	35796	IS 3025 (Part-16) 2017
7	TOC	mg/L	14	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	63	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4119	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	356	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.35	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	16830	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3430	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	5.24	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.27	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...


Macky Suraliwala
Sr., Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Page: 2 of 2

Customer's Name and Address :


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0055 Issue Date : 13/10/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : EB 2 Down Stream

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.14	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	330	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	782	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	11408	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	312	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	6.1	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.03, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- PSSAI Approved Lab
- Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07018605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0064
	Issue Date : 15/11/2020
	Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020

Sampling Location : EB 1 Up stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 07/11/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 08/11/2020	Lab ID. : BLD/2011/02
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 08/11/2020	Date of Completion of Test : 15/11/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1.	pH	--	7.56	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	57.14	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.59	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	11	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	37142	IS 3025 (Part-16) 2017
7	TOC	mg/L	14	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	70	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4352	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	448	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	3.2	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	17686	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3624	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	5.62	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.51	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Macky Surajiwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0064 Issue Date : 15/11/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : EB 1 Up stream

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.14	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	360	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method)
28	Magnesium as Mg	mg/L	828	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	11104	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	360	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	8.4	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni:0.02 mg/L, Manganese as Mn:0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Surafwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCB approved schedule II auditors
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp.Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle,Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0065 Issue Date : 15/11/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---


Sampling Location : EB 2 Down Stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 07/11/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 08/11/2020	Lab ID. : BLD/2011/03
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 08/11/2020	Date of Completion of Test : 15/11/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.48	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	52.80	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.22	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	8.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	35868	IS 3025 (Part-16) 2017
7	TOC	mg/L	12	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	68	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	3510	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	446	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.38	IS 3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	17286	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3490	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	4.40	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.38	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Page: 2 of 2

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0065**Issue Date : **15/11/2020**Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**Sampling Location : **EB 2 Down Stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.10	APHA (23 rd Edition 2017) 4500 F D SPAND5 Method
27	Calcium as Ca	mg/L	280	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method)
28	Magnesium as Mg	mg/L	792	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	10498	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	340	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	7.3	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni:0.02 mg/L, Manganese as Mn:0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Surajiwala
Sr. Scientist


Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCII approved schedule II auditor
- ISO 14001
- CHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp.Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle,Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Page: 1 of 2

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0071**Issue Date : **26/12/2020**Customer's Ref. : **W.O. No. 8520210015
Dated:14.04.2020**Sampling Location : **EB 1 Up stream**

Description of Sample : **Ground Water sample** Quantity/No. of Samples : **05 Lit./One**
 Date of Sampling : **18/12/2020** Sampling Procedure : **IS:3025**
 Sampling by : **Pollucon Laboratories Pvt. Ltd.** Protocol (purpose) : **QC/Env. Monitoring**
 Sample Receipt Date : **19/12/2020** Lab ID. : **BLD/2012/02**
 Packing/ Seal : **Sealed** Test Parameters : **As per table**
 Date of Starting of Test : **19/12/2020** Date of Completion of Test : **26/12/2020**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.75	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	51.86	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.12	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	7.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	33812	IS 3025 (Part-16) 2017
7	TOC	mg/L	10	APHA (23 rd Edition 2017) 3510 B
8	COD	mg/L	80	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	3980	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	476	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	0.82	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	15549	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	4014	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	3.94	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
20	Nickel as Ni	mg/L	Not Detected	IS 3025 (Part-48) 2019
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
24	Iron as Fe	mg/L	0.42	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackey
Mackey Surahwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab

● Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986

● GPCB approved schedule II auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.B/37-WT

Customer's Name and Address :

Page: 2 of 2


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0071 Issue Date : 26/12/2020 Customer's Ref. : W.O. No. 8520210015 Dated:14.04.2020
--	---

Sampling Location : EB 1 Up stream

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.45	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	290	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	574	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	12236	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	310	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	5.0	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Nickel as Ni:0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc: 0.05 mg/L, O&G : 2.0 mg/L, Manganese as Mn:0.03 mg/L, Pesticides : 0.1 µg/L.


Macky Surahwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp.Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle,Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com



TEST REPORT

QF/7.B/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0072A
	Issue Date : 26/12/2020
	Customer's Ref. : W.O. No. 8520210015 Dated:14.04.2020

Sampling Location : **EB 2 Down Stream**

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 18/12/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 19/12/2020	Lab ID. : BLD/2012/03
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 19/12/2020	Date of Completion of Test : 26/12/2020

RESULT TABLE

Sr. No.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.62	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	48.6	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.78	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	5.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	32344	IS 3025 (Part-16) 2017
7	TOC	mg/L	8.0	APHA (23 rd Edition 2017) 3510 B
8	COD	mg/L	72	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	2905	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	454	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	0.62	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	15125	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3872	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	3.42	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CY E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.33	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackay Suralfwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognized by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCB approved schedule II auditor
- ISO 14001
- ORSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp.Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle,Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0072A Issue Date : 26/12/2020 Customer's Ref. : W.O. No. 8520310015 Dated:14.04.2020
--	--

Sampling Location : **EB 2 Down Stream**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.20	APHA (23 rd Edition 2017) 4500 F D SPANDE Method
27	Calcium as Ca	mg/L	276	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	540	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	11250	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	295	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	4.5	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Nickel as Ni: 0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Manganese as Mn: 0.03 mg/L, Pesticides : 0.1 µg/L.


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986
- GPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QP/18/11-PC

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No : PL/BLD 0003
	Issue Date : 13/01/2021
	Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020


Sampling Location :	EB ± Up stream
---------------------	-----------------------


Description of Sample :	Ground Water sample	Quantity/No. of Samples :	05 Lit./One
Date of Sampling :	04/01/2021	Sampling Procedure :	IS:3025
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) :	QC/Env. Monitoring
Sample Receipt Date :	05/01/2021	Lab ID :	BLD/2101/03
Packing/ Seal :	Scaled	Test Parameters :	As per table
Date of Starting of Test :	05/01/2021	Date of Completion of Test :	13/01/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.33	IS 3025 (Part - 1) 2019 Electrode Method
2	Colour	Co-pt	15	IS 3025 (Part - 1) 2019
3	Conductivity	mmhos/cm	55.17	IS 3025 (Part - 1) 2019
4	Turbidity	NTU	0.86	APHA (21 st Edition 2017) 2101 B
5	Total Suspended Solids	mg/L	8.0	IS 3025 (Part - 1) 2019
6	Total Dissolved Solids	mg/L	35840	IS 3025 (Part - 1) 2019
7	TOC	mg/L	0.0	APHA (21 st Edition 2017) 5310 B
8	COD	mg/L	74	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4738	IS 1045 (Part - 2) 2019 APHA Method
10	Total Alkalinity	mg/l	312	IS 3025 (Part - 2) 2019
11	Total Kjeldahl Nitrogen	mg/L	0.94	IS 3025 (Part - 2) 1988 (Revised) 1 (Revised) 2019
12	Chlorides as Cl	mg/l	17537	IS 3025 (Part - 3) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	4200	IS 3025 (Part 3) 2019
14	Nitrate	mg/L	3.12	APHA (23 rd Edition 2017) 4500 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/l	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/l	Not Detected	IS 3025 (Part-4) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 B : Cadmeric Nitride
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.38	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/l	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned over leaf

**TEST REPORT**

QI/7 3137-A/1

Customer's Name and Address :

Page 2 of 2


**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISTT: BHARUCH**

Test Report No. : **PL/BLD 0003**
Issue Date : **13/01/2021**
Customer's Ref. : **W.O.No.R520210015**
Dated:14-04-2020

Sampling Location : **EB 1 Up stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.74	APHA (23) Edition 2017, TME TDS-9025 Method
27	Calcium as Ca	mg/L	312	IS 3025 (Part - 43) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	829	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/l	11036	APHA (23) Edition 2017, TME T
30	Potassium as K	mg/L	329	APHA (23) Edition 2017, TME TDS-9025 Method
31	BOD	mg/L	7.58	IS 3025 (Part - 44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-41) 2019 Inducto-oxidation Method
33	D&G	mg/L	Not Detected	APHA (23) Edition 2017, TME T
34	Pesticides	µg/L	Not Detected	USEPA 808.1-905 USEPA 821.2-1997 USEPA 812.2-2003

Artesian Head Lead as Pb : 0.095 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.03 mg/L, Total Chloride as Cl : 0.05 mg/L, Phosphate as P : 0.01 mg/L, Sulphate as So₄ : 1 mg/L, Nitrate as N : 0.02 mg/L, Manganese as Mn : 0.01 mg/L, Ammonical Nitrogen : 0.2 mg/L, Sulphide as S₂ : 0.01 mg/L, Total Hardness as CaCO₃ : 2.2 mg/L, Free Chlor : 0.1 µg/L.


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

Q-7/8/1/W

Customer's Name and Address

Page: 1 of 2

M/s. BELL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL - VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0004
	Issue Date : 13/01/2021
	Customer's Ref : W.O.No.8520210015 Dated: 14.04.2020


Sampling Location : EB 2 Down Stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 04/01/2021	Sampling Procedure : 15:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 05/01/2021	Lab ID. : BLD/2101/04
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 05/01/2021	Date of Completion of Test : 13/01/2021


RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.12	IS 3025 (Part - 1): 2011 Extreme & Minor
2	Colour	Co-pt	15	IS 3025 (Part - 1): 2011
3	Conductivity	µmhos/cm	51.86	IS 3025 (Part - 1): 2011
4	Turbidity	NTU	0.72	APHA (21 st Edition 2017) 2111 B
5	Total Suspended Solids	mg/L	6.0	IS 3025 (Part - 1): 2011
6	Total Dissolved Solids	mg/L	33.46	IS 3025 (Part - 1): 2011
7	TOC	mg/L	7.0	APHA (23 rd Edition 2017) 8100 B
8	COD	mg/L	62	APHA (23 rd Edition 2017) 5210 B Open Reflux Method
9	Total Hardness	mg/L	4060	IS 3025 (Part - 2): 2011 EDTA Method
10	Total Alkalinity	mg/l	288	IS 3025 (Part - 2): 2011
11	Total Kjeldahl Nitrogen	mg/L	0.76	IS 3025 (Part-3), 1990 Clause 3.5 (Revised 2009)
12	Chlorides as Cl	mg/L	16849	IS 3025 (Part - 3): 2011 Argentometric Method
13	Sulphates as SO ₄	mg/L	4.00	IS 3025 (Part-3): 2011
14	Nitrate	mg/L	2.94	APHA (23 rd Edition 2017) 4500 F
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-3): 2011
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 3500 CN C Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.29	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...



Macky Suraliwala
Sr. Scientist



Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QNT/8/21/W11

Page: 2 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH

Test Report No. : **PL/BLD 0004**Issue Date : **13/01/2021**Customer's Ref. : **W.O.No B520210015
Dated:14/04/2020**Sampling Location : **EB 2 Down Stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.16	APHA (231) Edition 2017; 4.401.01 (2005) Method
27	Calcium as Ca	mg/l	798	IS 3025 (Part - 4) 2015 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	792	IS 3025 (Part - 4) 2015 EDTA Titrimetric
29	Sodium as Na	mg/L	10586	APHA (231) Edition 2017; 811.01 B
30	Potassium as K	mg/L	314	APHA (231) Edition 2017; 8110.01 A Potassium Phthalate
31	BOD	mg/L	5.8	IS 3025 (Part - 4) 2015
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part - 4) 2015 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (231) Edition 2017; 8020 B
34	Pesticides	ug/L	Not Detected	ISPPA 906:1999; USEPA 8757:1999; USEPA 832:2000

Detection Limit as per 0.005 mg/L, Cadmium as per 0.001 mg/L, Copper as per 0.02 mg/L, Total Chlorine as per 0.25 mg/L, Mercury as per 0.02 mg/L, Arsenic as per 0.01 mg/L, Nickel as per 0.02 mg/L, Manganese as per 0.02 mg/L, Ammonical Nitrogen as per 0.2 mg/L, Iron as per 0.05 mg/L, Zinc as per 0.05 mg/L, Phosphate as per 0.02 mg/L.

Macky Surahwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf

**TEST REPORT**

QC/17.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0013A Issue Date : 09/03/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	--

Sampling Location : EB 1 Up stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 10/02/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 11/02/2021	Lab ID. : BLD/2102/04
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 11/02/2021	Date of Completion of Test : 20/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.61	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	15	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	57.23	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.39	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	8.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	36486	IS 3025 (Part 16) 2017
7	TOC	mg/L	14	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	87	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4016	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	458	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.76	IS : 3025 (Part-34) : 1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	16036	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3812	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	3.72	APHA (23 rd Edition 2017) 4510 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN F Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.48	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackey
Mackey Suralkwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7 & 07-WT

Customer's Name and Address :

Page: 2 of 2

M/S. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0013A Issue Date : 09/03/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	--

Sampling Location : **EB 1 Up stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.32	APHA (23 rd Edition 2017) 4500 F D SPANOS Method
27	Calcium as Ca	mg/L	310	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	778	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	12138	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	312	APHA (23 rd Edition 2017) 3500 K By Flame Photometer
31	BOD	mg/L	12.6	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 521.2 1995/ USCPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.05 mg/L, Mercury as Hg : 0.001 mg/L, Arsenic as As : 0.1 mg/L, Nickel as Ni : 0.02 mg/L, Manganese as Mn : 0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN : 0.01 mg/L, Zinc : 0.05 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L

Mackey
Mackey Suralwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QI/7.8/37-W7

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0014 Issue Date : 09/03/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	--

Sampling Location : **EB 2 Down Stream**

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 10/02/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 11/02/2021	Lab ID. : BLD/2102/05
Parking/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 11/02/2021	Date of Completion of Test : 20/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.58	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	53.14	IS 3025 (Part - 4) 2019
4	Turbidity	NTU	1.28	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	7.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	34286	IS 3025 (Part-16) 2017
7	TOC	mg/L	12	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	75	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	3824	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	436	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.47	IS 3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	15426	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3672	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	2.76	APHA (23 rd Edition 2017) 4113 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.39	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mack
Macky Surajiwala
Sr. Scientist

Dr. Ajin Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.B/37-WT

Customer's Name and Address :

Page: 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0014 Issue Date : 09/03/2021 Customer's Ref : W.O.No.8320210015 Dated:14.04.2020
--	--

Sampling Location : **EB 2 Down Stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.13	APHA (23 rd Edition 2017) 4500 F D SPANNS Method
27	Calcium as Ca	mg/L	290	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	811	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	11184	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	302	APHA (23 rd Edition 2017) 3500 K B Flame Photometer
31	BOD	mg/L	8.6	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508.1-995/ USEPA 525.2-1995/ USEPA 532.2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Manganese as Mn: 0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L

Mack
Mackey Surajiwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QE/7.8/37-WF

Page 1 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0020 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location : EB 1 Up stream

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 20/03/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 21/03/2021	Lab ID. : BLD/2103/02
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 21/03/2021	Date of Completion of Test : 02/04/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.52	IS 3025 (Part - 11) 2017 Electrode Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	51.40	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.18	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	12.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	33452	IS 3025 (Part-18) 2017
7	TOC	mg/L	1.1	APHA (23 rd Edition 2017) 5310 E
8	COD	mg/L	82	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	4278	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	476	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.16	IS : 3025 (Part-34) 1986 (Clause 2.3 (Reaffirmed 2005)
12	Chlorides as Cl	mg/L	16022	IS 3025 (Part - 37) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3747	IS 3025 (Part-24) 2015
14	Nitrate	mg/L	3.28	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-18) 2017
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CH F Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.52	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continued...

Mackay Suraiwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QH/3/37-01

Page: 2 of 2


Customer's Name and Address :

M/s. BELL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0020 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location : **EB 1 Up stream****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.26	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	324	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	832	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	11124	APHA (23 rd Edition 2017) 2111 B
30	Potassium as K	mg/L	324	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	9.0	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2015 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 E
34	Pesticides	µg/L	Not Detected	USEPA 503 (705) USEPA 571, 1997 USEPA 532 2003

Detection Limit: Lead as Pb: 0.005 mg/L, Calcium as Ca: 0.004 mg/L, Copper as Cu: 0.02 mg/L, Total Chromium: 0.025 mg/L, Mercury as Hg: 0.02 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Manganese as Mn: 0.03 mg/L, Ammonical Nitrogen: 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc: 0.05 mg/L, O&G: 2.0 mg/L, Pesticides: 0.1 µg/L.



Macky Suralfwala
Sr. Scientist



Dr. Arun Sajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page 1 of 2

**M/s. BELL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISTT: BHARUCH**

Test Report No. : **PL/BLD 0021**
Issue Date : **02/04/2021**
Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**


Sampling Location : **EB 2 Down Stream**

Description of Sample : **Ground Water sample** Quantity/No. of Samples : **05 Lit./ One**
Date of Sampling : **20/03/2021** Sampling Procedure : **IS:3025**
Sampling by : **Pollucon Laboratories Pvt. Ltd** Protocol (purpose) : **QC/Env. Monitoring**
Sample Receipt Date : **21/03/2021** Lab ID. : **BLD/2103/03**
Packing/ Seal : **Sealed** Test Parameters : **As per table**
Date of Starting of Test : **21/03/2021** Date of Completion of Test : **02/04/2021**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.99	IS 3025 (Part - 11) 2017 Electronic Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	48.82	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	1.14	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	10.0	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	31750	IS 3025 (Part-16) 2017
7	TOC	mg/L	10	APHA (23 rd Edition 2017) 5200 B
8	COD	mg/L	82	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	3786	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	426	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	1.08	IS 3025 (Part-24) : 1990 Clause 2.3 (Kraffmet 2019)
12	Chlorides as Cl	mg/L	15210	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	3654	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	3.16	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-46) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.26	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...


Macky Suresh
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

TEST REPORT

QF/7.R/37-WT

Customer's Name and Address :

Page: 2 of 2


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0021 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : EB 2 Down Stream

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	1.16	APHA (23 rd Edition 2017) 4500 F-D SPANIOS Method
27	Calcium as Ca	mg/L	253	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	757	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	10877	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	287	APHA (23 rd Edition 2017) 3111 K B Flame Photometer
31	BOD	mg/L	7.7	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 H
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection limits: Lead as Pb : 0.05 mg/L, Cadmium as Cd : 0.04 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.05 mg/L, Mercury as Hg : 0.01 mg/L,
 Arsenic as As : 0.1 mg/L, Nickel as Ni:0.05 mg/L, Manganese as Mn:0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Zinc : 0.16 mg/L,
 O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Surajwala
 Sr. Scientist


Dr. Arun Bajpal
 Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned over-leaf.

**TEST REPORT**

QF/7.0/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. :	PL/BLD 0058
	Issue Date :	13/10/2020
	Customer's Ref. :	W.O.No.8520210015 Dated:14.04.2020

Sampling Location :	Inside Mandir
---------------------	----------------------

Description of Sample :	Ground Water sample	Quantity/No. of Samples :	05 Lit./One
Date of Sampling :	03/10/2020	Sampling Procedure :	IS:3025
Sampling by :	Pollucon Laboratories Pvt.Ltd.	Protocol (purpose) :	QC/Env. Monitoring
Sample Receipt Date :	05/10/2020	Lab ID. :	BLD/2010/06
Packing/ Seal :	Sealed	Test Parameters :	As per table
Date of Starting of Test :	05/10/2020	Date of Completion of Test :	13/10/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	8.12	IS 3025 (Part - 1) 2017 Succimetric Method
2	Colour	Co-pl	3.4	IS 3025 (Part - 1) 2017
3	Conductivity	µmhos/cm	0.48	IS 3025 (Part - 1) 2017
4	Turbidity	NTU	0.32	APHA (23) Edition 2017 2100 J
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 1) 2017
6	Total Dissolved Solids	mg/L	338	IS 3025 (Part - 1) 2017
7	TOC	mg/L	Not Detected	APHA (23) Edition 2017 8310 B
8	COD	mg/L	Not Detected	APHA (23) Edition 2017 8220 B Open Reflux Method
9	Total Hardness	mg/L	109	IS 3025 (Part - 2) 2019 EDTA Method
10	Total Alkalinity	mg/L	116	IS 3025 (Part - 2) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part 3) 2019 Method A.1 (Revised 2002)
12	Chlorides as Cl	mg/L	128	IS 3025 (Part - 2) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	10.4	IS 3025 (Part - 2) 2019
14	Nitrate	mg/L	Not Detected	APHA (23) Edition 2017 8110 J
15	Lead as Pb	mg/l	Not Detected	APHA (23) Edition 2017 8111 J
16	Cadmium as Cd	mg/L	Not Detected	APHA (23) Edition 2017 8111 G
17	Copper as Cu	mg/L	Not Detected	APHA (23) Edition 2017 8111 G
18	Total Chromium	mg/L	Not Detected	APHA (23) Edition 2017 8111 G
19	Mercury as Hg	mg/l	Not Detected	IS 3025 (Part - 2) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23) Edition 2017 8111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23) Edition 2017 8510 CD Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23) Edition 2017 8111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23) Edition 2017 8111 B
24	Iron as Fe	mg/l	0.064	APHA (23) Edition 2017 8111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23) Edition 2017 8111 B

Continues...

Mackay Surajbala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QR/7 5/37-WT

Customer's Name and Address :

Page 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0058 Issue Date : 13/10/2020 Customer's Ref. : W.O.No-8520210015 Dated:14.04.2020
--	---

Sampling Location : **Inside Mandir****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F.D 5940B Method
27	Calcium as Ca	mg/L	52	IS 3025 (Part-43) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	5.96	IS 3025 (Part-46) 2019 EDTA Method
29	Sodium as Na	mg/L	70	APHA (23 rd Edition 2017) 3112 B
30	Potassium as K	mg/L	6.7	APHA (23 rd Edition 2017) 3500 K.B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-31) 2019 Spectrophotometric Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 8021.0
34	Pesticides	µg/l	Not Detected	USEPA 8160 (a)-(b) 1996 EPA 8160 (a)-(b) USEPA 8160 (a)-(b)

Detection Limit Lead as Pb : 0.01 mg/L, Cadmium as Cd : 0.001 mg/L, Copper as Cu : 0.02 mg/L, Chromium as Cr : 0.01 mg/L, Manganese as Mn : 0.01 mg/L, Nickel as Ni : 0.01 mg/L, Arsenic as As : 0.01 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanide as C_N : 0.02 mg/L, Zinc : 0.05 mg/L, BOD : 0.5 mg/L, Pesticides : 0.1 µg/L


Macky Surajiwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- FSSAI Approved Lab
- Recognized by MOEF, New Delhi under Section 12 of Environmental Protection Act 1986
- CITE approved Standard Auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gayatri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016695174, WEB: www.polluconlab.com, E-mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QC/ / A/37 VV

Page: 1 of 7

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0057**Issue Date : **13/10/2020**Customer's Ref. : **W.O.No. B5 20210015
Dated:14.04.2020**Sampling Location : **Near Bus Station**

Description of Sample :	Ground Water sample	Quantity/No. of Samples :	05 Lit./One
Date of Sampling :	03/10/2020	Sampling Procedure :	IS:3025
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) :	QC/Env. Monitoring
Sample Receipt Date :	05/10/2020	Lab ID :	BLD/2010/05
Packing/ Seal :	Sealed	Test Parameters :	As per table
Date of Starting of Test :	05/10/2020	Date of Completion of Test :	13/10/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	8.14	IS 3025 (Part - 11) 2017 Electronic Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	1461	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.34	APHA (23 rd Edition 2017) 2111.3
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 15) 2017
6	Total Dissolved Solids	mg/L	993	IS 3025 (Part 16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 2111.8
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 2120.8 Open Reflux Method
9	Total Hardness	mg/L	268	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	210	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part 34) 1986 Clause 3.1 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	226	IS 3025 (Part - 37) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	27	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 2111.6
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.8
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.9
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.5
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.6
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.9
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition) 2017 4111.01 Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.5
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.4
24	Iron as Fe	mg/L	0.076	APHA (23 rd Edition 2017) 3111.9
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111.8

Mackay Surathwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/18/31-WT

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No : **PL/BLD 0057**Issue Date : **13/10/2020**Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**Sampling Location : **Near Bus Station****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (21 st Edition 2017) 8000 F.D SP60.25 Mg (Doc)
27	Calcium as Ca	mg/L	32	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	43.12	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	110	APHA (21 st Edition 2017) 3111.9
30	Potassium as K	mg/L	9.6	APHA (23 rd Edition 2017) 3500 K.D Flame Photometer
31	BOD	mg/L	Not Detected	IS 3075 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3045 (Part-34), 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (21 st Edition 2017) 5520.6
34	Pesticides	µg/L	Not Detected	USEPA 508.1995/ USEPA 525.2.1995/ USEPA 547.2004

Detection limit (mg/L): Fluorides as F: 0.01 mg/L, Calcium as Ca: 0.01 mg/L, Magnesium as Mg: 0.02 mg/L, Sodium as Na: 0.01 mg/L, Potassium as K: 0.01 mg/L, Ammonical Nitrogen: 0.01 mg/L, O&G: 0.01 mg/L, Pesticides: 0.1 µg/L.


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned over leaf.

**TEST REPORT**

QT.7.8/37-W

Customer's Name and Address

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0056 Issue Date : 13/10/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location : **Near Gram Panchayat**

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 03/10/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 05/10/2020	Lab ID. : BLD/2010/04
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 05/10/2020	Date of Completion of Test : 13/10/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	8.41	IS 3025 (Part - 1) 2017 Isotonic Method
2	Colour	Co-pt	3.8	IS 3025 (Part - 1) 2017
3	Conductivity	mmhos/cm	0.362	IS 3025 (Part - 1) 2017
4	Turbidity	NTU	0.14	APHA (23 rd Edition 2017) 2100 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 1) 2017
6	Total Dissolved Solids	mg/L	253	IS 3025 (Part - 1) 2017
7	TOC	mg/l	Not Detected	APHA (23 rd Edition 2017) 8010 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 8001 A Open Reflux Method
9	Total Hardness	mg/L	61	IS 3025 (Part - 2) 2019 EDTA Method
10	Total Alkalinity	mg/L	132	IS 3025 (Part - 2) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part - 3) 1989 Clause 7.4 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	53	IS 3025 (Part - 4) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	9.6	IS 3025 (Part - 4) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 8100 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 C
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part - 8) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 8101 C1 Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 C
24	Iron as Fe	mg/L	0.056	APHA (23 rd Edition 2017) 8111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 8111 B

Continue...

Macky Surajwala
Sr. Scientist

Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

Q/787/W1

Page: 2 of 2

Customer's Name and Address :

M/s. BELL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0056 Issue Date : 13/10/2020 Customer's Ref. : W.O.No.RS20210015 Dated:14.04.2020
---	---

Sampling Location : **Near Gram Panchayat****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F.D Method
27	Calcium as Ca	mg/L	14.4	IS 3025 (Part - 46) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	6.0	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	19	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	6.2	APHA (23 rd Edition 2017) 3504 & B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (Part - 41) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Resubstantion Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 1920 B
34	Pesticides	µg/L	Not Detected	USEPA 508.1555; USEPA 525.11597; USEPA 532.2000

Detection Limit: Lead as Pb: 0.015 mg/L, Cadmium as Cd: 0.01 mg/L, Copper as Cu: 0.02 mg/L, Chromium: 0.025 mg/L, Mercury as Hg: 0.01 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.05 mg/L, Nitrite as As: 0.1 mg/L, Ammonical Nitrogen: 2 mg/L, Cyanides as CN: 0.02 mg/L, Zinc: 0.05 mg/L, BOD: 0.1 mg/L, Pesticides: 0.1 µg/L.

Macky Surajwala
Sr. Scientist

Dr. Aron Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

TEST REPORT

QF/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO. D-43, GIOC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

 Test Report No. : **PL/BLD 0066**

 Issue Date : **15/11/2020**

 Customer's Ref. : **W.O.No-8520210015
Dated:14.04.2020**

 Sampling Location : **Near Gram Panchayat**

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lt./One
Date of Sampling : 07/11/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 08/11/2020	Lab ID. : BLD/2011/04
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 08/11/2020	Date of Completion of Test : 15/11/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	—	7.41	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.452	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.27	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	312	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	105	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	116	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) -1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	38	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	9.6	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.063	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continues...


Macky Surajwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 2 of 2


**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

Test Report No. : **PL/BLD 0066**
Issue Date : **15/11/2020**
Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**

Sampling Location : **Near Gram Panchayat****RESULT TABLE**

SRL NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 1503 F D SPANDS Method
27	Calcium as Ca	mg/L	24.4	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	10.56	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	34	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	5.8	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 506.1 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg : 0.001 mg/L, Arsenic as As : 0.1 mg/L, Nickel as Ni : 0.02 mg/L, Manganese as Mn : 0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN : 0.001 mg/L, Fluorides as F : 0.5 mg/L, Zinc : 0.20 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.


Macky Syralwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab

● Recognized by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986

● CPCB approved
● Schedule II auditor

● ISO 14001

● (IHSAS 18001)

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantivanth S/M Mill Lane, Near Gayatri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07018605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0068
	Issue Date : 15/11/2020
	Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020

Sampling Location : Inside Mandir
--

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 07/11/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 08/11/2020	Lab ID. : BLD/2011/06
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 08/11/2020	Date of Completion of Test : 15/11/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	—	8.07	IS 3025 (Part - 11) 2017 Electrode Method
2	Colour	Co-pt	6.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.481	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.25	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	332	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B -
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	100	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	110	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS :3025 (Part-34) :1998 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl ⁻	mg/L	98	IS 3025 (Part - 37) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	10.6	IS 3025 (Part-24) 2013
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B -
24	Iron as Fe	mg/L	0.076	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continues...

Mackay Suranwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.B/37-WT

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

Test Report No. : **PL/BLD 0068**
Issue Date : **15/11/2020**
Customer's Ref. : **W.O.No.8520210015**
Date: **14.04.2020**

Sampling Location : **Inside Mandir****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	28	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	7.2	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	65	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	5.8	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 505 (1995)/ USEPA 525.2 (1995)/ USEPA 532 (2000)

Detection Limit: TDS: 0.1 mg/L, COD: 5.0 mg/L, Total Suspended Solids: 2.0 mg/L, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb: 0.005 mg/L, Cadmium as Cd: 0.004 mg/L, Copper as Cu: 0.02 mg/L, Total Chromium: 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Manganese as Mn: 0.03 mg/L, Ammonical Nitrogen: 0.2 mg/L, Cyanides as CN: 0.001 mg/L, Fluorides as F: 0.5 mg/L, Zn: 0.06 mg/L, O&G: 2.0 mg/L, Pesticides: 0.1 µg/L.

Macky Surajwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab

● Recognized by MoEF, New Delhi Under
Sec. 12 of Environmental (Protection) Act-1986● CPCB approved
schedule II auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath S/Mk Min Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2636750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7 8/37-WT

Customer's Name and Address :

Page: 1 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

Test Report No. : **PL/BLD 0067**
Issue Date : **15/11/2020**
Customer's Ref. : **W.O.No.6520210015
Dated:14.04.2020**

Sampling Location : **Near Bus Station**

Description of Sample : **Ground Water sample** Quantity/No. of Samples : **05 Lit./One**
Date of Sampling : **07/11/2020** Sampling Procedure : **IS:3025**
Sampling by : **Pollucon Laboratories Pvt. Ltd.** Protocol (purpose) : **QC/Env. Monitoring**
Sample Receipt Date : **08/11/2020** Lab ID. : **BLD/2011/05**
Packing/ Seal : **Sealed** Test Parameters : **As per table**
Date of Starting of Test : **08/11/2020** Date of Completion of Test : **15/11/2020**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.83	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	1.25	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.30	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	868	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	184	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	199	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part 34) : 1585 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl ⁻	mg/L	326	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	34	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500-CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.083	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continued...

Macky Suraliwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● PSSAI Approved Lab ● Recognized by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986 ● CECB approved schedule II auditor ● ISO 14001 ● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.B/37-WT

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0067**
Issue Date : **15/11/2020**
Customer's Ref. : **W.O.No.8520210015**
Dated:14.04.2020

Sampling Location : **Near Bus Station****RESULT TABLE**

Sr. No.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F-3 SPANOS Method
27	Calcium as Ca	mg/L	48	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	15.36	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	93	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	7.3	APHA (23 rd Edition 2017) 3500 K B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.4 1995/ USEPA 532 2006

Detection Limit: TOC:0.1mg/L, COD:5.0mg/L, Total Suspended Solids: 2.0mg/L, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb: 0.015 mg/L, Calcium as Ca: 0.004 mg/L, Copper as Cu: 0.02 mg/L, Total Chlorine: 0.015 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Manganese as Mn: 0.03 mg/L, Ammonical Nitrogen: 0.2 mg/L, Cyanide as CN: 0.01 mg/L, Fluorides as F: 0.5 mg/L, Zinc: 0.06 mg/L, O&G: 2.0 mg/L, Pesticides: 0.1 µg/L


Macky Suraiwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ISO 9001 Approved Lab

● Recognized by MoEF, New Delhi Under
Sec. 12 of Environmental (Protection) Act-1986● CPCB approved
Schedule II and III

● ISO 14001

● OHSAS 18001

● ISO 45001

"Pollucon House", Plot No. 5 & 6, Opp. Baleji Industrial Society, Old Shantinath SIM Mill Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone: 0261-2635750, 0261-2635781, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7 8/37-WT

Customer's Name and Address .

Page 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0075 Issue Date : 26/12/2020 Customer's Ref. : W.Q. No. B520210015 Dated:14.04.2020
---	---

Sampling Location : Inside Mandir
--

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 19/12/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 19/12/2020	Lab ID. : BLD/2012/06
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 19/12/2020	Date of Completion of Test : 26/12/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.95	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	4.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.44	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.18	APHA (20 th Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/l	320	IS 3025 (Part 16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 2510 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5210 B Open Relius Method
9	Total Hardness	mg/L	89	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	138	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS - 4025 (Part 31) - 1998 Clause 2.3 (Reaffirmed 2000)
12	Chlorides as Cl	mg/L	81	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	14.6	IS 3025 (Part 29) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 4111 A
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 4111 H
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-40) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Columnetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.055	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackey
Mackey Surajiwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF:7 0/37-WT

Page: 2 of 2

Customer's Name and Address :


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0075 Issue Date : 26/12/2020 Customer's Ref. : W.O. No. BS20210015 Dated:14.04.2020
---	---

Sampling Location : Inside Mandir
--

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F B SPANIS Method
27	Calcium as Ca	mg/L	20	IS 3025 (Part - 4): 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	9.36	IS 3025 (Part - 4): 2019 EDTA Method
29	Sodium as Na	mg/L	36	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	4.0	APHA (23 rd Edition 2017) 3500 F D Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508.1955/ USEPA 525.2.1595/ USEPA 531.2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.025 mg/L, Mercury as Hg : 0.003 mg/L, Nickel as Ni : 0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanide as CN : 0.01 mg/L, Zinc : 0.05 mg/L, Urea : 2.0 mg/L, Suspended Solids : 2.0 mg/L, COD : 1.0 mg/L, BOD : 0.1 mg/L, TDS : 0.1 mg/L, Fluorides as F : 0.05 mg/L, Manganese as Mn : 0.1 mg/L, Pesticides : 0.1 µg/L.


Macky Suralwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- ISSAI Approved Lab
- Recognized by MoEF, New Delhi Under Sec. 12 of Environmental Protection Act-1986
- CPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantlnath Silk Mill Lane, Near Gaytri Fashion Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 9281-2635750, 9281-2635751, 9281-2635775, 97016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

CF/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0073A
	Issue Date : 26/12/2020
	Customer's Ref. : W.O. No. 8520210015 Dated:14.04.2020

Sampling Location : **Near Gram Panchayat**

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 18/12/2020	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protokul (purpose) : QC/Env. Monitoring
Sample Receipt Date : 19/12/2020	Lab ID. : BLD/2012/04
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 19/12/2020	Date of Completion of Test : 26/12/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.72	IS 3025 (Part - 1): 2017 Electrode Method
2	Colour	Co-pt	10	IS 3025 (Part - 4): 2017
3	Conductivity	mmhos/cm	0.42	IS 3025 (Part - 14): 2019
4	Turbidity	NTU	0.44	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17): 2017
6	Total Dissolved Solids	mg/L	258	IS 3025 (Part 16): 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 3510 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	84	IS 3025 (Part - 21): 2019 EDTA Method
10	Total Alkalinity	mg/L	132	IS 3025 (Part - 23): 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-54) : 1998 (Clause 2.3 (Reaffirmed 2009))
12	Chlorides as Cl	mg/L	79	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	10	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-46) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.065	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continued...

Mary
Macky Suraliwala
Sr. Scientist

Dr. Arun Sajpai
Dr. Arun Sajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● INSAI Approved Lab

● Recognized by MoEF, New Delhi Under
Sec. 12 of Environmental Protection Act-1986● GPCB approved
Water Pollution Control

● ISO 14001

● ISO 45001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinathi Silk Mill Lane, Near Gaytri Faresan Mart,
Navjivan Circle, Vidhansabha Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.8/37-WC

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

Test Report No. : **PL/BLD 0073A**
Issue Date : **26/12/2020**
Customer's Ref. : **W.O. No. 8520210015**
Dated:14.04.2020

Sampling Location : **Near Gram Panchayat****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	20	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	8.16	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	28	APHA (23 rd Edition 2017) 3111 H
30	Potassium as K	mg/L	5.2	APHA (23 rd Edition 2017) 3500 K F Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508.1-995/USEPA 525.2-1595/USEPA 532-2001

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.015 mg/L, Mercury as Hg : 0.001 mg/L, Nickel as Ni : 0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN : 0.02 mg/L, Zinc : 0.05 mg/L, O&G : 2.0 mg/L, Total Suspended Solids : 2.0 mg/L, BOD : 1.0 mg/L, COD : 8.0 mg/L, TOC : 0.1 mg/L, Fluorides as F : 0.05 mg/L, Magnesium as Mg : 0.05 mg/L, Pesticides : 0.1 µg/L

Macky Surajiwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7 8/37-WT

Customer's Name and Address :

Page 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0074 Issue Date : 26/12/2020 Customer's Ref. : W.O. No. 8570210015 Dated:14.04.2020
---	---

Sampling Location	Near Bus Station
-------------------	-------------------------

Description of Sample	: Ground Water sample	Quantity/No. of Samples	: 05 Lit./One
Date of Sampling	: 18/12/2020	Sampling Procedure	: IS:3025
Sampling by	: Pollucon Laboratories Pvt. Ltd	Protocol (purpose)	: QC/Env. Monitoring
Sample Receipt Date	: 19/12/2020	Lab ID.	: BLD/2012/05
Packing/ Seal	: Sealed	Test Parameters	: As per table
Date of Starting of Test	: 19/12/2020	Date of Completion of Test	: 26/12/2020

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.92	IS 3025 (Part - 31) 2017 Colorimetric Method
2	Colour	Co-pt	4.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	1.16	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.56	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	796	IS 3025 (Part 16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 3510 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 H Open Reflux Method
9	Total Hardness	mg/L	149	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	204	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS : 3025 (Part-34) 1986 Clause 2.1 (Reaffirmed 2005)
12	Chlorides as Cl	mg/L	272	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	30	IS 3025 (Part 24) 2017
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3113 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3112 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 (NH ₄) Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.078	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

CONTINUE...

Mackey
Mackey Suratiwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/18/21-WT

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH**

Test Report No. : **PL/BLD 0074**Issue Date : **26/12/2020**Customer's Ref. : **W.O. No. 8520210015
Dated:14.04.2020**Sampling Location : **Near Bus Station****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F ⁻	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	58	IS 3025 (Part - 40) 2015 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	23.76	IS 3025 (Part - 46) 2015 EDTA Method
29	Sodium as Na	mg/L	75	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	6.0	APHA (23 rd Edition 2017) 1500. K B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART - 44) 2015
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-39) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5500 H
34	Pesticides	µg/L	Not Detected	USEPA 508.1395/USEPA 525.2.1995/USEPA 532.2000

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02, Total Chromium : 0.025 mg/L, Mercury as Hg : 0.01 mg/L, Nickel as Ni : 0.02 mg/L, Arsenic as As : 0.1 mg/L, Ammonical Nitrogen : 0.2 mg/L, Chlorides as Cl⁻ : 0.02 mg/L, Zinc : 0.05 mg/L, DSS : 2.0 mg/L, Manganese as Mn : 0.1 mg/L, BOD : 1.0 mg/L, COD : 4.0 mg/L, Suspended Solids : 2.0 mg/L, TDS : 5.0 mg/L, Fluorides as F⁻ : 0.05 mg/L, Pesticides : 0.1 µg/L

M
Mackay Surratwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

GHT/837/W1

Page: 2 of 2


Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No : PL/BLD 0006 Issue Date : 13/01/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	--

Sampling Location : **Near Bus Station****RESULT TABLE:**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 450.1 (5485.05 Method)
27	Calcium as Ca	mg/L	16	IS 3025 (Part - 46) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	12.72	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	66	APHA (23 rd Edition 2017) 311.1
30	Potassium as K	mg/L	10	APHA (23 rd Edition 2017) 3501.4 (671.4) Barium Chloride Method
31	BOD	mg/L	Not Detected	IS 3025 (Part-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-09) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520.3
34	Pesticides	µg/L	Not Detected	USEPA 808.1 (555) USEPA 115.7 (99%) USEPA 532.2 (00)

Detection limit: TOC: 0.1 mg/L, COD: 5 mg/L, Total suspended solids: 2 mg/L, Total Chloride: 0.2 mg/L, Lead as Pb: 0.05 mg/L, Cadmium as Cd: 0.01 mg/L, Copper as Cu: 0.02 mg/L, Total Chromium: 0.05 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.01 mg/L, Manganese as Mn: 0.05 mg/L, Ammonical Nitrogen: 0.2 mg/L, Fluorides as F: 0.1 mg/L, Chlorides as Cl: 1 mg/L, and Calcium as Ca: 1 mg/L, Magnesium as Mg: 1 mg/L, Potassium as K: 1 mg/L, Sodium as Na: 1 mg/L, Phosphorus as P: 0.1 mg/L.


Macky Suraliwala
 Sr. Scientist


Dr. Arun Bajpai
 Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab

● Recognised by MoEF, New Delhi Under
Sec. 12 of Environmental Protection Act-1986● GPCB approved
in-schedule II auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinarth Silk Mill Lane, Near Gaytri Farsan Mart,
 Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016805174, WEB: www.polluconlab.com, E-mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QZ/2021/01

Page : of 2

Customer's Name and Address :

M/s. BETL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No : PL/BLD 0007 Issue Date : 13/01/2021 Customer's Ref : W.O.No.8520210015 Dated:14.04.2020
---	---


Sampling Location : Inside Mandir
--


Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 04/01/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 05/01/2021	Lab ID : BLD/2101/07
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 05/01/2021	Date of Completion of Test : 13/01/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.38	IS 3025 (Part - 1) 2017 Electrode Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 1) 2017
3	Conductivity	mmhos/cm	0.5h	IS 3025 (Part - 1) 2017
4	Turbidity	NTU	0.23	APHA (22 nd Edition 2017) 4100 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 1) 2017
6	Total Dissolved Solids	mg/L	395	IS 3025 (Part - 1) 2017
7	TOC	mg/L	Not Detected	APHA (22 nd Edition 2017) 8000 B
8	COD	mg/l	Not Detected	APHA (22 nd Edition 2017) 5200 B Open Reflux Method
9	Total Hardness	mg/l	108	IS 3025 (Part - 1) 2017 EDTA Method
10	Total Alkalinity	mg/L	142	IS 3025 (Part - 1) 2017
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part - 1) 2017 Distillation Method (Reduced) 4500 C
12	Chlorides as Cl	mg/L	103	IS 3025 (Part - 1) 2017 Argentometric Method
13	Sulphates as SO ₄	mg/L	15	IS 3025 (Part - 1) 2017
14	Nitrate	mg/l	Not Detected	APHA (22 nd Edition 2017) 4500 B
15	Lead as Pb	mg/L	Not Detected	APHA (22 nd Edition 2017) 3111 B
16	Cadmium as Cd	mg/l	Not Detected	APHA (22 nd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (22 nd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (22 nd Edition 2017) 4111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part - 1) 2017
20	Nickel as Ni	mg/L	Not Detected	APHA (22 nd Edition 2017) 4111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (22 nd Edition 2017) 4500 C 1 Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (22 nd Edition 2017) 3111 B
23	Manganese as Mn	mg/l	Not Detected	APHA (22 nd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.084	APHA (22 nd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (22 nd Edition 2017) 3111 B

Continue..


Macky Suraliwala
 Sr. Scientist


Dr. Arun Bajpai
 Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf

● FSSAI Approved Lab

● Recognized by MoEF, New Delhi India
Sec. 14 of Environmental (Protection) Act-1986● GPCB approved
Subsidiary B auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantirath Silk Mill Lane, Near Gaytri Farsan Mart,
 Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E-mail: pollucon@gmail.com, info@polluconlab.com



TEST REPORT

QI / 001 / 07

Page: 2 of 2

Customer's Name and Address :

M/6, BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL - VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0007 Issue Date : 13/01/2021 Customer's Ref. : W.O No.B520210015 Dated:14.04.2020
--	---

Sampling Location : **Inside Mandir**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500-F-ORNA JV Method
27	Calcium as Ca	mg/L	74	IS 3025 (Part - 10) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	10.56	IS 3025 (Part - 10) 2019 EDTA Method
29	Sodium as Na	mg/L	59	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	74	APHA (23 rd Edition 2017) 3500-KO7 Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (Part - 14) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-20) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 3120-3
34	Pesticides	µg/L	Not Detected	USEPA 506 (1995) EPA 816-L-1 (1995) EPA 816-L-2000

Detectable limit: TDS: 500 mg/L, Chloride: 100 mg/L, Total suspended Solids: 50mg/L, Total Kjeldahl Nitrogen: 1.0 mg/L, Lead as Pb: 0.05 mg/L, Cadmium as Cd: 0.01 mg/L, Copper as Cu: 0.02 mg/L, Zinc as Zn: 0.05 mg/L, Mercury as Hg: 0.01 mg/L, Arsenic as As: 0.01 mg/L, Nickel as Ni: 0.05 mg/L, Manganese as Mn: 0.1 mg/L, Ammonical Nitrogen: 0.2 mg/L, Cyanide as CN: 0.05 mg/L, Fluorides as F: 0.5 mg/L, Chloride: 100 mg/L, O&G: 2.0 mg/L, Pesticides: 0.01 mg/L

Macky Surallwala
Sr. Scientist

Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf

- ENSAI Approved Lab
- Recognized by MoEF, New Delhi Under Sec. 14 of Environmental Protection Act-1986
- CPCB approved schedule II auditor
- ISO 14001
- OLISAS 18601
- ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

Q/18/31-201

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0005 Issue Date : 13/01/2021 Customer's Ref : W.O.No.8520210015 Dated:14.04.2020
---	--


Sampling Location : Near Gram Panchayat
--

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 04/01/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 05/01/2021	Lab ID. : BLD/2101/05
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 05/01/2021	Date of Completion of Test : 13/01/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.56	IS 3025 (Part - 1) 2017 Electronic Method
2	Colour	Co pt	5.0	IS 3025 (Part - 1) 2017
3	Conductivity	mmhos/cm	0.53	IS 3025 (Part - 1) 2017
4	Turbidity	NTU	0.32	APHA (23 rd Edition 2017) 8110 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 1) 2017
6	Total Dissolved Solids	mg/L	358	IS 3025 (Part - 1) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 8130 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 8120 B Open Reflux Method
9	Total Hardness	mg/L	114	IS 3025 (Part - 1) 2017 3114 Method
10	Total Alkalinity	mg/L	138	IS 3025 (Part - 1) 2017
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part - 1) 1988 3114 2.1 (Revised 2002)
12	Chlorides as Cl	mg/L	106	IS 3025 (Part - 1) 2017 Argentometric Method
13	Sulphates as SO ₄	mg/L	12.6	IS 3025 (Part - 1) 2017
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-1B) 2017
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B Mercuric Nitrate Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B
24	Iron as Fe	mg/L	0.075	APHA (23 rd Edition 2017) 8110 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 8110 B

Continued...


Macky Suraliwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.



TEST REPORT

QPL/BLD/W1

Page: 1 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0005 Issue Date : 13/01/2021 Customer's Ref : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location	Near Gram Panchayat
-------------------	----------------------------

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2012) 4500 F (SPAN) IS Method
27	Calcium as Ca	mg/L	28	IS 3025 (Part - 45) 2019 (IS 4574) Titrimetric Method
28	Magnesium as Mg	mg/L	10.56	IS 3025 (Part - 45) 2019 (IS 4574) Titrimetric Method
29	Sodium as Na	mg/L	37	APHA (23 rd Edition 2012) 3111 A
30	Potassium as K	mg/L	5.1	APHA (23 rd Edition 2012) 3102 A (Flame Photometer)
31	BOD	mg/L	Not Detected	IS 3025 (Part - 44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part - 44) 2019 (Discoloration Method)
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2012) 4500 F
34	Pesticides	µg/L	Not Detected	USEPA 808 (9907) USEPA 8212 (1997) USEPA 832 (2000)

Quality Unit: Lead as Pb (µg/L), Nickel (mg/L), Cadmium as Cd (µg/L), Copper as Cu (µg/L), Zinc (mg/L), Total Chromium (µg/L), Boron as B (mg/L), Manganese as Mn (mg/L), Ammonical Nitrogen (mg/L), Cyanide as CN (mg/L), Chloride as Cl (mg/L), Sulfate as SO₄ (mg/L), O&G (mg/L), Fluorides as F (mg/L).

Macky Suraliwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

- HSNAL Approved Lab
- Recognized by MoER, New Delhi Under Sec. 12 of Environmental Protection Act-1986
- CPCB approved schedule II auditor
- ISO 14001
- OHSAS 18001
- ISO 9001

**TEST REPORT**

QF/7.8/37-WT

Page: 1 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. : PL/BLD 0015 Issue Date : 09/03/2021 Customer's Ref. : W.O.No.0520210015 Dated:14.04.2020
---	--

Sampling Location : Near Bus Station
Description of Sample : Ground Water sample Quantity/No. of Samples : 05 Lit. /One
Date of Sampling : 10/02/2021 Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt.Ltd. Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 11/02/2021 Lab ID. : BLD/2102/07
Packing/ Seal : Sealed Test Parameters : As per table
Date of Starting of Test : 11/02/2021 Date of Completion of Test : 20/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.48	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	1.37	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.59	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	914	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5510 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	216	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	189	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS :3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	302	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulfates as SO ₄	mg/L	26.4	IS 3025 (Part-24) 20:9
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-49) 20:9
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.098	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackay
Mackay Surajiwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QE/7.8/37-WT

Page: 2 of 2

Customer's Name and Address :

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0016**Issue Date : **09/03/2021**Customer's Ref. : **W.O.No.8520210015
Dated:14.04.2020**Sampling Location : **Near Bus Station****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F-CL SPANCS Method
27	Calcium as Ca	mg/L	42.4	IS 3025 (Part - 4C) 2019 EDTA Titrimetric Method;
28	Magnesium as Mg	mg/L	26.4	IS 3025 (Part - 4B) 2019 EDTA Method
29	Sodium as Na	mg/L	73	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	6.87	APHA (23 rd Edition 2017) 3500 K-B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-4A) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-3A) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 50B 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit: TC:0.3mg/L, COD:5.0mg/L, Total Suspended Solids: 2.0mg/L, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg : 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni:0.02 mg/L, Manganese as Mn:0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN : 0.001 mg/L, Fluorides as F : 0.5 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.

Macky Suraliwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

Q6/7.8/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0017A
	Issue Date : 09/03/2021
	Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020

Sampling Location : Inside Mandir
--

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 10/02/2021	Sampling Procedure : 15:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 11/02/2021	Lab ID. : BLD/2102/08
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 11/02/2021	Date of Completion of Test : 20/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.99	IS 3025 (Part - 1): 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.62	IS 3025 (Part - 4): 2017
4	Turbidity	NTU	0.34	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 3): 2017
6	Total Dissolved Solids	mg/L	41\$	IS 3025 (Part 16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open-Relux Method
9	Total Hardness	mg/L	115	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	120	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-31) :1989 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	93	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	16.4	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-18) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4530 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.098	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Macky Suraliwala
Sr. Scientist

Dr. Arun Bhatpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-WT

Customer's Name and Address :

Page: 2 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0017A**
Issue Date : **09/03/2021**
Customer's Ref. : **W.O.No.8520210015**
Dated:**14.04.2020**

Sampling Location : **Inside Mandir****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F D SPADIS Method
27	Calcium as Ca	mg/L	26.4	IS 3025 (Part - 40) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	11.76	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	68	APHA (23 rd Edition 2017) 3111 H
30	Potassium as K	mg/L	5.82	APHA (23 rd Edition 2017) 4500 K Pt Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	ORP	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508 1995/ USEPA 525.2 1995/ USEPA 532 2000

Detection Limit:1000.1mg/L,000.5.0mg/L, Total Suspended Solids: 2.0mg/l, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.001 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.075 mg/l, Mercury as Hg : 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni:0.02 mg/L, Manganese as Mn:0.01 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN:0.001 mg/L, Fluorides as F :0.5 mg/L, Zinc : 0.05 mg/l, DGB : 2.0 mg/L, Pesticides : 0.1 µg/l

Mackay Surallwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

◆ PSSAI Approved Lab

◆ Recognized by MoEF, New Delhi India
Sec. 12 of Environmental Protection Act-1986◆ GPCB approved
schedule II auditor

◆ ISO 14001

◆ ISO 45001

◆ ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0281-2635760, 0281-2635751, 0281-2635775, 07016805174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7 8/37-VT

Customer's Name and Address :

Page: 1 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0015 Issue Date : 09/03/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : Near Gram Panchayat
Description of Sample : Ground Water sample Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 10/02/2021 Sampling Procedure : 15:3025
Sampling by : Pollucon Laboratories Pvt. Ltd. Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 11/02/2021 Lab ID. : BLD/2102/06
Packing/ Seal : Sealed Test Parameters : As per table
Date of Starting of Test : 11/02/2021 Date of Completion of Test : 20/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.38	IS 3025 (Part - 11) 2017 Electrometric Method
2	Colour	Co-pt	10	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.48	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.37	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	329	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	128	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	110	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) :1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	37	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	14.8	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3114 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.098	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackey
Mackey Surjitwala
Sr. Scientist

Dr. Arun Bajpai
Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/37-W7

Customer's Name and Address :

Page: 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISTIT: BHARUCH	Test Report No. : PL/BLD 0015 Issue Date : 09/03/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location : Near Gram Panchayat
--

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F D SPANDS Method
27	Calcium as Ca	mg/L	34	IS 3025 (Part - 40) 7019 EDTA Titrimetric Method)
28	Magnesium as Mg	mg/L	10.32	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	27	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	4.30	APHA (23 rd Edition 2017) 3500 K B/ Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 508.1995/ USEPA 525.2.1995/ USEPA 522.2000

Detection Limit: Lead as Pb : 0.05 mg/L, Calcium as Ca : 0.04 mg/L, Copper as Cu : 0.02 mg/L, Total Chromium : 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni : 0.02 mg/L, Manganese as Mn:0.03 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as Cn: 0.001 mg/L, Fluorides as F : 0.5 mg/L, Zinc : 0.05 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.

Mackay
Mackay Suraiwala
Sr. Scientist

Dr. Arjun Bajpai
Dr. Arjun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ISSAI Approved Lab ● Recognized by MoEF, New Delhi Under Section 12 of Environmental Protection Act-1986 ● GPCR approved & Institute of Auditor ● ISO 14001 ● OHSAS 18001 ● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016005174, WEB www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QP/7.B/37-WT

Customer's Name and Address :

Page: 1 of 2

M/s. BELL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0023 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location	Near Bus Station		
Description of Sample	: Ground Water sample	Quantity/No. of Samples	: 05 Lit./One
Date of Sampling	: 20/03/2021	Sampling Procedure	: IS:3025
Sampling by	: Pollucon Laboratories Pvt. Ltd.	Protocol (purpose)	: QC/Env. Monitoring
Sample Receipt Date	: 21/03/2021	Lab ID.	: BLD/2103/05
Packing/ Seal	: Sealed	Test Parameters	: As per table
Date of Starting of Test	: 21/03/2021	Date of Completion of Test	: 02/04/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.54	IS 3025 (Part - 11) 2017 Electronic Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	1.28	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.52	APHA (21 st Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	822	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	198	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	178	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-24) 1988 clause 3.1 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	294	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	30.8	IS 3025 (Part-24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-08) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.082	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Mackay Suriwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ISO 9001 Approved Lab ● Recognized by MoEF, New Delhi under Sec - 12 of Environmental Protection Act-1986 ● CPCB approved schedule B auditor ● ISO 14001 ● OHSAS 18001 ● ISO 5001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinagar 6th ME Lane, Near Gayatri Faresan Mart, Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 8261-2835759, 8261-2836761, 8261-2836775, 87915884174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7 8/37-WT

Page: 2 of 2

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISTT: BHARUCH	Test Report No. : PL/BLD 0023 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : **Near Bus Station****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 F.D SPANCS Method
27	Calcium as Ca	mg/L	38.6	IS 3025 (Part - 40) 2015 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	24.36	IS 3025 (Part - 46) 2015 EDTA Method
29	Sodium as Na	mg/L	85	APHA (23 rd Edition 2017) 3111 D
30	Potassium as K	mg/L	4.8	APHA (23 rd Edition 2017) 3500 K.F Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART 44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pestocides	µg/L	Not Detected	USEPA 508.1595/ USEPA 525.2 (905) USEPA 532.2060

Detection Limit: DO:0.1mg/L, COD:5.0mg/L, Total Suspended Solids: 2.0mg/L, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb: 0.05 mg/L, Cadmium as Cd: 0.05 mg/L, Copper as Cu: 0.02 mg/L, Total Chromium: 0.025 mg/L, Mercury as Hg: 0.02 mg/L, Arsenic as As: 0.1 mg/L, Methyl as Hg: 0.02 mg/L, Manganese as Mn: 0.05 mg/L, Ammonical Nitrogen: 0.2 mg/L, Cyanides as Cn: 0.001 mg/L, Fluorides as F: 0.5 mg/L, Zinc: 0.26 mg/L, O&G: 2.0 mg/L, Pesticides: 0.1 µg/L


Macky Surafiwala
Sr. Scientist


Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ISO/9001 Approved Lab

● Recognised by MoEF, New Delhi Under Sec. 12 of Environmental Protection Act-1986

● CPEB approved schedule II auditor

● ISO 14001

● CRISAS 19901

● ISO 9001

**"Pollucon House", Plot No. 5 & 6, Opp. Bajaj Industrial Society, Old Shantirath 5th Mile Lane, Near Gayatri Farsan Mart,
Nandivan Circle, Vidhaya Magdalla Road, Surat-395007, Gujarat, India.**

Phone : 0261-2636780, 0261-2635751, 0261-2635775, 07918806174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7.R/37-W*

Page: 1 of 2

Customer's Name and Address :

M/S. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- YAGRA, DISTIT: BHARUCH	Test Report No. : PL/BLD 0024 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
---	---

Sampling Location : Inside Mandir
--

Description of Sample : Ground Water sample	Quantity/No. of Samples : 05 Lit./One
Date of Sampling : 20/03/2021	Sampling Procedure : IS:3025
Sampling by : Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) : QC/Env. Monitoring
Sample Receipt Date : 21/03/2021	Lab ID. : BLD/2103/06
Packing/ Seal : Sealed	Test Parameters : As per table
Date of Starting of Test : 21/03/2021	Date of Completion of Test : 02/04/2021

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.76	IS 3025 (Part - 11) 2017 Electrode Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm.	0.54	IS 3025 (Part - 14) 2019
4	Turbidity	NTU	0.28	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	364	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	108	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	104	IS 3025 (Part - 23) 2019
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part 31) : 1988 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	95	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	19.8	IS 3025 (Part - 24) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-48) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CN E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.078	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue..

Macky Suratiwala
Sr. Scientist

Dr. Arun Bajpal
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

QF/7.8/27 W*

Page: 2 of 2

Customer's Name and Address :


M/s. **BELL INFRASTRUCTURE LTD,**
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DIST: BHARUCH

Test Report No : **PL/BLD 0024**
 Issue Date : **02/04/2021**
 Customer's Ref. : **W.Q.No.8520210015**
Dated:14.04.2020

Sampling Location : **Inside Mandir****RESULT TABLE**

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 8500 F D SPECTRO Method
27	Calcium as Ca	mg/L	22.8	IS 3025 (Part - 40) 2019 HClA Titrimetric Method
28	Magnesium as Mg	mg/L	17.24	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	52	APHA (23 rd Edition 2017) 8111 B
30	Potassium as K	mg/L	3.5	APHA (23 rd Edition 2017) 8500 K BY Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART-14) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 D
34	Pesticides	µg/L	Not Detected	USEPA 502.1/505; USEPA 515 & 1999; USEPA 537 2000

Detection Limit: TOC: 0.1mg/L, COD: 5.0mg/L, Total Suspended Solids: 1.0mg/L, Total Kjeldahl Nitrogen: 0.2 mg/L, Lead as Pb: 0.015 mg/L, Cadmium as Cd: 0.004 mg/L, Copper as Cu: 0.02 mg/L, Total Chromium: 0.025 mg/L, Mercury as Hg: 0.001 mg/L, Arsenic as As: 0.1 mg/L, Nickel as Ni: 0.02 mg/L, Hexachloro as HxCl: 0.01 mg/L, Ammonical Nitrogen: 0.2 mg/L, Chlorides as Cl: 0.021 mg/L, Fluorides as F: 0.5 mg/L, Zinc: 0.06 mg/L, O&G: 2.0 mg/L, Pesticides: 0.1 µg/L


Macky Surendhara
 Sr. Scientist


Dr. Arun Bajpai
 Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ENSAI Approved Lab

● Recognised by MoEF, New Delhi Under Sec. 32 of Environmental Protection Act 1986

● CPCB approved Accredited & audited

● ISO 14001

● ISO 9001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Salaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Fashion Mart,
 Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2638750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E-mail: pollucon@gmail.com, info@polluconlab.com

**TEST REPORT**

QF/7 3/37 WT

Customer's Name and Address :

Page 1 of 2

**M/s. BEIL INFRASTRUCTURE LTD,
PLOT NO.D-43, GIDC, DAHEJ,
DAHEJ-392130, TAL :- VAGRA,
DISIT: BHARUCH**

Test Report No. : **PL/BLD 0022**
Issue Date : **02/04/2021**
Customer's Ref : **W.O.No.8520210015**
Dated:14.04.2020

Sampling Location : **Near Gram Panchayat**

Description of Sample : **Ground Water sample** Quantity/No. of Samples : **05 Lit./One**
Date of Sampling : **20/03/2021** Sampling Procedure : **IS:3025**
Sampling by : **Pollucon Laboratories Pvt. Ltd.** Protocol (purpose) : **QC/ Env. Monitoring**
Sample Receipt Date : **21/03/2021** Lab ID. : **BLD/2103/04**
Packing/ Seal : **Sealed** Test Parameters : **As per table**
Date of Starting of Test : **21/03/2021** Date of Completion of Test : **02/04/2021**

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
1	pH	--	7.46	IS 3025 (Part - 11) 2017 Electrode Method
2	Colour	Co-pt	5.0	IS 3025 (Part - 4) 2017
3	Conductivity	mmhos/cm	0.37	IS 3025 (Part - 14) 2015
4	Turbidity	NTU	0.34	APHA (23 rd Edition 2017) 2130 B
5	Total Suspended Solids	mg/L	Not Detected	IS 3025 (Part - 17) 2017
6	Total Dissolved Solids	mg/L	248	IS 3025 (Part-16) 2017
7	TOC	mg/L	Not Detected	APHA (23 rd Edition 2017) 5310 B
8	COD	mg/L	Not Detected	APHA (23 rd Edition 2017) 5220 B Open Reflux Method
9	Total Hardness	mg/L	122	IS 3025 (Part - 21) 2019 EDTA Method
10	Total Alkalinity	mg/L	102	IS 3025 (Part - 23) 2015
11	Total Kjeldahl Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) : 1998 Clause 2.3 (Reaffirmed 2009)
12	Chlorides as Cl	mg/L	44	IS 3025 (Part - 32) 2019 Argentometric Method
13	Sulphates as SO ₄	mg/L	10.8	IS 3025 (Part-31) 2019
14	Nitrate	mg/L	Not Detected	APHA (23 rd Edition 2017) 4110 B
15	Lead as Pb	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
16	Cadmium as Cd	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
17	Copper as Cu	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
18	Total Chromium	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
19	Mercury as Hg	mg/L	Not Detected	IS 3025 (Part-46) 2019
20	Nickel as Ni	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
21	Cyanides as CN	mg/L	Not Detected	APHA (23 rd Edition 2017) 4500 CH E Colorimetric Method
22	Arsenic as As	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
23	Manganese as Mn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B
24	Iron as Fe	mg/L	0.062	APHA (23 rd Edition 2017) 3111 B
25	Zinc as Zn	mg/L	Not Detected	APHA (23 rd Edition 2017) 3111 B

Continue...

Macky Suryawala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST REPORT**

CF/7.8/37-WT

Customer's Name and Address :

Page: 2 of 2

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0022 Issue Date : 02/04/2021 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Sampling Location : Near Gram Panchayat
--

RESULT TABLE

SR. NO.	TEST PARAMETERS	UNIT	RESULT	METHOD ADOPTED
26	Fluorides as F	mg/L	Not Detected	APHA (23 rd Edition 2017) 4503 F-2 SPANCO Method
27	Calcium as Ca	mg/L	26.2	IS 3025 (Part - 46) 2019 EDTA Titrimetric Method
28	Magnesium as Mg	mg/L	13.56	IS 3025 (Part - 46) 2019 EDTA Method
29	Sodium as Na	mg/L	32	APHA (23 rd Edition 2017) 3111 B
30	Potassium as K	mg/L	4.8	APHA (23 rd Edition 2017) 3503 K B Flame Photometer
31	BOD	mg/L	Not Detected	IS 3025 (PART 44) 2019
32	Ammonical Nitrogen	mg/L	Not Detected	IS 3025 (Part-34) 2019 Nesslerization Method
33	O&G	mg/L	Not Detected	APHA (23 rd Edition 2017) 5520 B
34	Pesticides	µg/L	Not Detected	USEPA 503 (995) USEPA 525.2 (995) USEPA 532 (2000)

Detection Limit: Lead as Pb : 0.005 mg/L, Cadmium as Cd : 0.004 mg/L, Copper as Cu : 0.01 mg/L, Total Chromium : 0.01 mg/L, Mercury as Hg : 0.01 mg/L, Arsenic as As : 0.1 mg/L, Nickel as Ni:0.02 mg/L, Hexachloro As Mu:0.01 mg/L, Ammonical Nitrogen : 0.2 mg/L, Cyanides as CN:0.01 mg/L, Fluorides as F : 0.1 mg/L, Zinc : 0.06 mg/L, O&G : 2.0 mg/L, Pesticides : 0.1 µg/L.

Macky Surajwala
Sr. Scientist

Dr. Arun Bajpai
Lab Manager(Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● ISO 9001:2015 Approved Lab

● Recognized by MS&ST, Govt. (Gujarat) Under
Sec. 10 of Environmental Protection Act-1986.● ISO 17025 Approved
Laboratory (I) Accredited

● ISO 14001

● ISO 45001

● ISO 9001

"Pollucon House", Plot No. 8 & 9, Opp. Balaji Industrial Society, Old Bhambhath Silk Mill Lane, Near Gayatri Farsan Mart,
New/Van Circle, Udhana Magdalla Road, Surat-392007, Gujarat, India.

Phone : 0291-2306750, 0291-2306751, 0291-2306778, 07940006174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

TEST CERTIFICATE FOR SOIL

QF/7.8/38-EX

Customer's Name and Address :

Page: 1 of 1

M/s. BEIL INFRATSTRCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD 0022 Issue Date : 29/05/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	---

Description of Sample	: Soil Sample	Quantity/No. of Samples	: 02 Kg/Three
Date of Sampling	: 19/05/2020	Sampling Procedure	: USEPA/IS 2720 etc.
Sampling By	: Pollucon Laboratories Pvt. Ltd.	Protocol (purpose)	: USEPA/IS 2720 etc.
Sample Receipt Date	: 20/05/2020	Lab ID	: BLD/2006/13 to16
Packing/ Seal	: Sealed	Test Parameters	: As per table
Date of Starting of Test	: 20/05/2020	Date of Completion of Test	: 29/05/2020
Test Method	: USEPA/IS 2720 etc.		

TEST RESULT

SR. NO.	TEST PARAMETERS	UNIT	RESULT		
			Near EB-1	Opp. Salt Farm	Near EB-2
1	pH	--	8.63	8.54	8.70
2	Conductivity	µmho/cm	2176	4451	1879
3	TDS	%	1.18	1.95	1.10
4	TOC	%	0.84	0.78	0.45
5	Cadmium BY TCLP	mg/L	Not Detected	Not Detected	Not Detected
6	Fluoride	mg/L	1.52	1.16	0.93
7	Lead Analyzed By TCLP	mg/L	0.36	0.48	Not Detected
8	Copper Analyzed By TCLP	mg/L	0.43	0.40	0.37
9	Chromium Analyzed By TCLP	mg/L	0.24	0.29	0.18
10	Mercury Analyzed By TCLP	mg/L	Not Detected	Not Detected	Not Detected
11	Nickel Analyzed By TCLP	mg/L	0.89	0.77	0.52
12	Cyanide	mg/L	Not Detected	Not Detected	Not Detected
13	Zinc Analyzed By TCLP	mg/L	0.93	0.86	0.41
14	Arsenic Analyzed By TCLP	mg/L	Not Detected	Not Detected	Not Detected
15	PAH	mg/L	Not Detected	Not Detected	Not Detected

ND*: Not Detected



MackySuraliwala
Sr. Scientist



Dr. ArunBajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

TEST CERTIFICATE FOR SOIL

QF/7.8/38-EX

Customer's Name and Address :

Page: 1 of 1

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. : PL/BLD0023 Issue Date : 29/05/2020 Customer's Ref. : W.O.No.8520210015 Dated:14.04.2020
--	--

Description of Sample	: Soil Sample	
Date of Sampling	: 19/05/2020	Quantity/No. of Samples : 02 Kg/Three
Sampling By	: Pollucon Laboratories Pvt. Ltd.	Sampling Procedure : USEPA/IS 2720 etc.
Sample Receipt Date	: 20/05/2020	Protocol (purpose) : USEPA/IS 2720 etc.
Packing/ Seal	: Sealed	Lab ID : BLD/2005/17 & 18
Date of Starting of Test	: 20/05/2020	Test Parameters : As per table
Test Method	: USEPA/IS 2720 etc.	Date of Completion of Test : 29/05/2020

TEST RESULT

SR. NO.	TEST PARAMETERS	UNIT	RESULT		
			Opp. Khetan Industries	Near ADM Building	Behind Tegros Company
1	pH	--	8.27	8.34	8.91
2	Conductivity	µmho/cm	3180	1746	2840
3	TDS	%	1.54	1.05	1.25
4	TOC	%	0.49	0.56	0.93
5	Cadmium BY TCLP	mg/L	Not Detected	Not Detected	Not Detected
6	Fluoride	mg/L	0.87	1.14	1.38
7	Lead Analyzed By TCLP	mg/L	0.24	Not Detected	Not Detected
8	Copper Analyzed By TCLP	mg/L	0.32	0.24	0.39
9	Chromium Analyzed By TCLP	mg/L	0.10	0.11	0.19
10	Mercury Analyzed By TCLP	mg/L	Not Detected	Not Detected	Not Detected
11	Nickel Analyzed By TCLP	mg/L	0.59	0.63	0.72
12	Cyanide	mg/L	Not Detected	Not Detected	Not Detected
13	Zinc Analyzed By TCLP	mg/L	0.45	0.59	0.81
14	Arsenic Analyzed By TCLP	mg/L	Not Detected	Not Detected	Not Detected
15	PAH	mg/L	Not Detected	Not Detected	Not Detected

ND*: Not Detected



Macky Suraliwala
Sr. Scientist



Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

ANNEXURE 7



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: BSM/16102020	Date: 16-10-2020	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	14-10-2020
Sampling Location	BOILER PLANT	Date of Receipt Sample	14-10-2020
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	14-10-2020
Sampling Procedure	---	Date of Completion Analysis	15-10-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	78.12	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	19.19	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	17.51	IS:5182 (P-6) 2006

Remarks (if Any):

For, BEIL INFRASTRUCTURE LTD.


Chemist


MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: BSM/13112020	Date: 13-11-2020	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	12-11-2020
Sampling Location	BOILER PLANT	Date of Receipt Sample	12-11-2020
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	12-11-2020
Sampling Procedure	---	Date of Completion Analysis	13-11-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	74.74	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	20.62	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	15.73	IS:5182 (P-6) 2006

Remarks (if Any):

For, BEIL INFRASTRUCTURE LTD.


Chemist


MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD
ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY
CERTIFICATE OF ANALYSIS

Report No: BSM/23122020	Date: 23-12-2020	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	22-12-2020
Sampling Location	BOILER PLANT	Date of Receipt Sample	22-12-2020
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	22-12-2020
Sampling Procedure	---	Date of Completion Analysis	23-12-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	88.64	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	21.70	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	18.28	IS:5182 (P-6) 2006

Remarks (if Any):

For, BEIL INFRASTRUCTURE LTD.

ASD

Chemist

A. Satish Kumar Gaddam
MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: BSM/13012021	Date: 13-01-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	12-01-2021
Sampling Location	BOILER PLANT	Date of Receipt Sample	12-01-2021
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	12-01-2021
Sampling Procedure	---	Date of Completion Analysis	13-01-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	84.62	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	20.66	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	17.21	IS:5182 (P-6) 2006

Remarks (if Any):

For, BEIL INFRASTRUCTURE LTD.


MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)


Chemist

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: BSM/11022021	Date: 11-02-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	09-02-2021
Sampling Location	BOILER PLANT	Date of Receipt Sample	09-02-2021
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	10-02-2021
Sampling Procedure	---	Date of Completion Analysis	11-02-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	76.94	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	21.06	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	15.89	IS:5182 (P-6) 2006

Remarks (if Any):

AC

ANALYSED BY

BEIL

VERIFIED BY

For BEIL Infrastructure Ltd

A. Sathish Kumar

AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130

E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)

CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: BSM/16032021	Date: 16-03-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	BOILER Stack
Sample Quantity	---	Date of Sampling	15-03-2021
Sampling Location	BOILER PLANT	Date of Receipt Sample	15-03-2021
Sample Collected by	Ashish Chaudhary	Date of Start Analysis	15-03-2021
Sampling Procedure	---	Date of Completion Analysis	16-03-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	84.12	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	22.99	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	16.03	IS:5182 (P-6) 2006

Remarks (if Any):

ANALYSED BY

VERIFIED BY

For BEIL Infrastructure Ltd.

AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/17102020	Date: 17-10-2020	Page No : 1/1
-------------------------	------------------	---------------


Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	16-10-2020
Sampling Location	DG Room	Date of Receipt Sample	16-10-2020
Sample Collected by	Kamalakant Raut	Date of Start Analysis	16-10-2020
Sampling Procedure	---	Date of Completion Analysis	17-10-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	73.86	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	15.87	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	19.18	IS:5182 (P-6) 2006

Remarks (if Any):


Chemist

For, BEIL INFRASTRUCTURE LTD.


MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/20112020	Date: 20-11-2020	Page No : 1/1
-------------------------	------------------	---------------


Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	19-11-2020
Sampling Location	DG Room	Date of Receipt Sample	19-11-2020
Sample Collected by	Kamalakant Raut	Date of Start Analysis	19-11-2020
Sampling Procedure	---	Date of Completion Analysis	20-11-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	69.79	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	14.15	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	21.53	IS:5182 (P-6) 2006

Remarks (if Any):

For, BEIL INFRASTRUCTURE LTD.


Chemist


MR. SATISH KUMAR GADDAM
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/10122020	Date: 10-12-2020	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	08-12-2020
Sampling Location	DG Room	Date of Receipt Sample	08-12-2020
Sample Collected by	Kamal Kant Raut	Date of Start Analysis	08-12-2020
Sampling Procedure	---	Date of Completion Analysis	09-12-2020

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	78.59	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	13.22	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	17.87	IS:5182 (P-6) 2006

Remarks (if Any):


Chemist

For, BEIL INFRASTRUCTURE LTD.


MR. SATISH KUMAR GADDAM
(Sr. Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/12012021	Date: 12-01-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	11-01-2021
Sampling Location	DG Room	Date of Receipt Sample	11-01-2021
Sample Collected by	Kamalakant Raut	Date of Start Analysis	11-01-2021
Sampling Procedure	---	Date of Completion Analysis	12-01-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	72.88	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	11.62	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	19.67	IS:5182 (P-6) 2006

Remarks (if Any):


Chemist

For, BEIL INFRASTRUCTURE LTD.


MR. SATISH KUMAR GADDAM

(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/18022021	Date: 18-02-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	17-02-2021
Sampling Location	DG Room	Date of Receipt Sample	17-02-2021
Sample Collected by	Kamalakant Raut	Date of Start Analysis	17-02-2021
Sampling Procedure	---	Date of Completion Analysis	18-02-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	76.74	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	10.64	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	21.34	IS:5182 (P-6) 2006

Remarks (if Any):

[Signature]
ANALYSED BY

[Signature]
VERIFIED BY

For BEIL Infrastructure Ltd.
[Signature]
AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: DSM/12032021	Date: 12-03-2021	Page No : 1/1
-------------------------	------------------	---------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43,DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-390 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Stack Sampling	Sample Identification/Code	DG Stack
Sample Quantity	---	Date of Sampling	11-03-2021
Sampling Location	DG Room	Date of Receipt Sample	11-03-2021
Sample Collected by	Kamalakant Raut	Date of Start Analysis	11-03-2021
Sampling Procedure	---	Date of Completion Analysis	12-03-2021

Sr No	Parameters	Permissible Unit	Unit	Results	Method Ref.
1	PM	150	Mg/Nm ³	78.95	IS:5182 (P-4) 1999
2	SULPHUR DIOXIDE	100	ppm	11.53	IS:5182 (P-2) 2001
3	NITROGEN OXIDE	50	ppm	20.18	IS:5182 (P-6) 2006

Remarks (if Any):

For BEIL Infrastructure Ltd.

F. 18/03
ANALYSED BY

P. A. G.
VERIFIED BY

Sathish Kumar Gaddam
AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
E-mail-mistryrg@beil.co.in Cell no: 9099057365

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696

ANNEXURE 8

**TEST CERTIFICATE**

QF/7.8/38-AQ

Customer's Name and Address :

Page: 1 of 1

M/s. BEIL INFRATSTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. :	PL/BLD 0061A2
	Issue Date :	11/10/2020
	Customer's Ref. :	W.O. No. 8520210015 Dated:14.04.2020

Location of Sampling :	Nr. Khetan Industries		
Date of Sampling :	03/10/2020	Sampling Procedure :	As per table
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) :	Ambient Air Quality Monitoring
Sample Receipt Date^ :	05/10/2020	Lab ID :	BLD/2010/09 [A-L]
Date of Starting of Test^ :	05/10/2020	Date of Completion of Test :	11/10/2020

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT®	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	74.6	100	IS 5182 (Part-23) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	33.2	60	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	12.4	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO ₂	µg/m ³	23.6	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) [§]	µg/m ³	Not Detected	180	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO [§]	mg/m ³	0.74	04	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	10.4	400	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS*	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) – particulate phase only	ng/m ³	Not Detected	NS*	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS*	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS*	CPCB guidelines for AAQM (Vol.I, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	0.39	1.0	CPCB guidelines for AAQM (Vol.I, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS*	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS*	USEPA 26A:1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS*	IS 5182 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS*	IS 5182 (Part-7) 2014

NS*: Not Specified, @Limit as per GPCB Consent Order No.AWH -109249 Issue Date: 14/09/2020 Up to 17/04/2025.

§: Carbon Monoxide as CO sampling duration 1 hrs. NS*: Not Specified. ^§:Ozone (O₃) sampling duration 1 hrs and sample Analyzed on same Day,Detection Limit : Benzene as C₆H₆: 2.0 µg/m³, Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³, Arsenic as As: 2.0 ng/m³, Nickel as Ni: 5.0 ng/m³, Hydrocarbon as HC:50 µg/m³, HydroChloric Acid As HCl: 5.0 µg/m³, Chlorine as Cl₂: 150 µg/m³, Hydrogen Sulphide as H₂S: 6.0 µg/m³,Ozone (O₃): 5.0 µg/m³.


Ravi Jariwala
Sr. Environmental Scientist


Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab ● Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986 ● GPCB approved schedule II auditor ● ISO 14001 : 2004 ● OHSAS 18001 : 2007 ● ISO 9001 : 2008

"Pollucon House", Plot No.5/6, Opp.Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart,
 Navjivan Circle,Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST CERTIFICATE**

QF/7.8/38-AQ

Customer's Name and Address :

Page: 1 of 1


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. :	PL/BLD 0070
	Issue Date :	14/11/2020
	Customer's Ref. :	W.O. No. 8520210015 Dated:14.04.2020


Location of Sampling :	Near Main Gate		
Date of Sampling :	07/11/2020	Sampling Procedure :	As per table
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Protocol (purpose) :	Ambient Air Quality Monitoring
Sample Receipt Date^ :	08/11/2020	Lab ID :	BLD/2011/08 [A-L]
Date of Starting of Test^ :	08/11/2020	Date of Completion of Test :	14/11/2020

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT[®]	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	83.4	100	IS 5182 (Part-23) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	36.9	60	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	10.6	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO ₂	µg/m ³	25.1	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) [§]	µg/m ³	Not Detected	180	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO [§]	mg/m ³	0.78	04	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	12.4	400	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) – particulate phase only	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	Not Detected	1.0	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS [†]	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS [†]	USEPA 26A:1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-7) 2014

NS[†]: Not Specified, ®LIMIT as per GPCB Consent Order No.AWH-109249 Issue Date: 14/09/2020 Up to 17/04/2025.§: Carbon Monoxide as CO sampling duration 1 hrs. NS[†]: Not Specified. †§:Ozone (O₃) sampling duration 1 hrs and sample Analyzed on same Day.Detection Limit : Benzene as C₆H₆: 2.0 µg/m³, Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³, Arsenic as As: 2.0 ng/m³, Nickel as Ni: 5.0 ng/m³, Hydrocarbon as HC:50 µg/m³, Hydro Chloric Acid As HCl: 5.0 µg/m³, Chlorine as Cl₂: 150 µg/m³, Hydrogen Sulphide as H₂S: 6.0 µg/m³, Lead as Pb: 0.1 µg/m³, Ozone (O₃): 5.0 µg/m³


Ravi Jagiwal
Sr. Environmental Scientist


Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● PSSAI Approved Lab

● Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986

● GPCB approved schedule II auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST CERTIFICATE**

QF/7.8/38-AQ

Page: 1 of 1

Customer's Name and Address :

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISIT: BHARUCH	Test Report No. :	PL/BLD 0070A
	Issue Date :	26/12/2020
	Customer's Ref. :	W.O. No. 8520210015 Dated:14.04.2020

Location of Sampling :	Near EB-2 Borewell	Sampling Procedure :	As per table
Date of Sampling :	18/12/2020	Protocol (purpose) :	Ambient Air Quality Monitoring
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Lab ID :	BLD/2012/01 [A-L]
Sample Receipt Date^ :	19/12/2020	Date of Completion of Test :	25/12/2020
Date of Starting of Test^ :	19/12/2020		

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT [®]	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	67.82	100	IS 5182 (Part-23) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	26.92	60	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	12.9	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO ₂	µg/m ³	28.6	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) [§]	µg/m ³	Not Detected	180	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO [§]	mg/m ³	0.98	04	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	3.42	400	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) - particulate phase only	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS [†]	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	Not Detected	1.0	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS [†]	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS [†]	USEPA 26A: 1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS [†]	IS 5182 (Part-7) 2014

NS[†]: Not Specified, @Limit as per CPCB Consent Order No. AWH-105249 Issue Date: 14/09/2020 Up to 17/04/2025.§: Carbon Monoxide as CO (sampling duration) hrs. NS[†]: Not Specified. ^: Ozone (O₃) (sampling duration) hrs and sample Analyzed on same Day.
Detection Limit : Benzene as C₆H₆: 2.0 µg/m³, Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³, Arsenic as As: 2.0 ng/m³, Nickel as Ni: 5.0 ng/m³, Hydrocarbon as HC: 50 µg/m³, Hydro Chloric Acid As HCl: 5.0 µg/m³, Chlorine as Cl₂: 150 µg/m³, Hydrogen Sulphide as H₂S: 6.0 µg/m³, Lead as Pb: 0.1 µg/m³, Ozone (O₃): 5.0 µg/m³


Ravi Jariwala
Sr. Environmental Scientist


Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

● FSSAI Approved Lab

● Recognised by MoEF, New Delhi Under Sec. 12 of Environmental (Protection) Act-1986

● GPCB approved schedule II auditor

● ISO 14001

● OHSAS 18001

● ISO 9001

"Pollucon House", Plot No. 5 & 6, Opp. Balaji Industrial Society, Old Shantinath Silk Mill Lane, Near Gaytri Farsan Mart,
Navjivan Circle, Udhana Magdalla Road, Surat-395007, Gujarat, India.

Phone : 0261-2635750, 0261-2635751, 0261-2635775, 07016605174, WEB: www.polluconlab.com, E. mail: pollucon@gmail.com, info@polluconlab.com

**TEST CERTIFICATE**

QF/7.8/38-AQ

Customer's Name and Address :

Page: 1 of 1

M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISTIT: BHARUCH	Test Report No. : PL/BLD 0001
	Issue Date : 13/01/2021
	Customer's Ref. : W.O. No. 8520210015 Dated:14.04.2020

Location of Sampling	: Nr. Khetan Industries	Sampling Procedure	: As per table
Date of Sampling	: 04/01/2021	Protocol (purpose)	: Ambient Air Quality Monitoring
Sampling by	: Pollucon Laboratories Pvt. Ltd.	Lab ID	: BLD/2101/01 [A-L]
Sample Receipt Date^	: 05/01/2021	Date of Completion of Test	: 11/01/2021
Date of Starting of Test^	: 05/01/2021		

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT ⁹	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	84.4	100	IS 5182 (Part-23) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	30.6	60	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	17.4	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO ₂	µg/m ³	33.9	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) ⁸	µg/m ³	Not Detected	180	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO ⁸	mg/m ³	1.16	04	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	9.4	400	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS ⁷	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) - particulate phase only	ng/m ³	Not Detected	NS ⁷	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS ⁷	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS ⁷	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	Not Detected	1.0	CPCB guidelines for AQM (Vol. 1, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS ⁷	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS ⁷	USEPA 26A 1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS ⁷	IS 5182 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS ⁷	IS 5182 (Part-7) 2014

NS⁷: Not Specified, NS⁸: as per CPCB Consent Order no. AWT-107341 Issue Date: 14/09/2020 up to 12/04/2025.8: Carbon Monoxide as CO sampling duration hrs. NS⁷: Not Specified. 9: Ozone (O₃) sampling duration 3 hrs and sample Analyzed on Same Day.Detection Limit: Benzene as C₆H₆: 2.0 µg/m³; Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³; Arsenic as As: 2.0 ng/m³; Nickel as Ni: 5.0 ng/m³; Hydrocarbon as HC: 50 µg/m³; Hydro Chloric Acid as HCl: 5.0 µg/m³; Chlorine as Cl₂: 150 µg/m³; Hydrogen Sulphide as H₂S: 6.0 µg/m³; Lead as Pb: 0.1 µg/m³; Ozone (O₃): 5.0 µg/m³

Ravi Jariwala

Sr. Environmental Scientist

Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST CERTIFICATE**

Customer's Name and Address :

QF/7.8/38-AQ

Page: 1 of 1

M/s. BELL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DIST: BHARUCH	Test Report No. :	PL/BLD 0010
	Issue Date :	09/03/2021
	Customer's Ref. :	W.O. No. 852010015 Dated:14.04.2020

Location of Sampling :	Nr. Main Gate	Sampling Procedure :	As per table
Date of Sampling :	10/02/2021	Protocol (purpose) :	Ambient Air Quality Monitoring
Sampling by :	Pollucon Laboratories Pvt. Ltd.	Lab ID :	BLD/2102/01 [A-L]
Sample Receipt Date :	11/02/2021	Date of Completion of Test :	17/02/2021

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT ^o	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	81.9	100	IS 5182 (Part-73) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	42.6	60	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	13.5	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO _x	µg/m ³	31.6	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) ^s	µg/m ³	9.4	180	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO ^s	mg/m ³	0.95	04	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	11.6	400	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS ^s	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) - particulate phase only	ng/m ³	Not Detected	NS ^s	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS ^s	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS ^s	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	Not Detected	1.0	CPCB guidelines for AAQM (Vol. I, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS ^s	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS ^s	USEPA 26A:1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS ^s	IS 5182 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS ^s	IS 5182 (Part-7) 2014

NS^s Not Specified, ^oLimit as per CPCB Consent Order No.4089 - 129219 Issue Date: 14/02/2020 Exp by: 17/04/2025.
^s Carbon Monoxide as CO sampling duration: 1hr, NS^s: Not Specified, ^sVolume (V₁) sampling duration: 1 hrs and sample analyzed on same day.
 Detection Limit - Benzene as C₆H₆: 2.0 µg/m³, Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³, Arsenic as As: 2.0 ng/m³, Nickel as Ni: 5.0 ng/m³, Hydrocarbon as HC: 50 µg/m³, Hydro Chloric Acid As HCl: 5.0 µg/m³, Chlorine as Cl₂: 150 µg/m³, Hydrogen Sulphide as H₂S: 6.0 µg/m³, Lead as Pb: 0.3 µg/m³

Ravi Janyala
 Sr. Environmental Scientist

Dr. Arun Bajpai
 Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

**TEST CERTIFICATE**

QF/7.8/38-AQ

Customer's Name and Address :

Page: 1 of 1


M/s. BEIL INFRASTRUCTURE LTD, PLOT NO.D-43, GIDC, DAHEJ, DAHEJ-392130, TAL :- VAGRA, DISTIT: BHARUCH	Test Report No. : PL/BLD 0019
	Issue Date : 02/04/2021
	Customer's Ref. : W.O. No. 8520210015 Dated:14.04.2020

Location of Sampling	: Nr. EB-2	Sampling Procedure	: As per table
Date of Sampling	: 20/03/2021	Protocol (purpose)	: Ambient Air Quality Monitoring
Sampling by	: Pollucon Laboratories Pvt. Ltd.	Lab ID	: BLD/2103/01 [A-L]
Sample Receipt Date	: 21/03/2021	Date of Completion of Test	: 27/03/2021
Date of Starting of Test	: 21/03/2021		

RESULT TABLE

SR. NO.	TEST PARAMETER	UNIT	RESULTS	LIMIT*	METHOD OF MEASUREMENT
1	Particulate Matter (PM ₁₀)	µg/m ³	72.4	100	IS 5182 (Part-3) 2017
2	Particulate Matter (PM _{2.5})	µg/m ³	30.4	60	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
3	Sulphur Dioxide as SO ₂	µg/m ³	10.9	80	IS 5182 (Part-2) 2017
4	Oxides of Nitrogen as NO ₂	µg/m ³	23.4	80	IS 5182 (Part-6) 2017
5	Ozone (O ₃) [§]	µg/m ³	Not Detected	180	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
6	Carbon Monoxide as CO [§]	mg/m ³	1.1	04	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
7	Ammonia as NH ₃	µg/m ³	8.5	400	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
8	Benzene as C ₆ H ₆	µg/m ³	Not Detected	NS [¶]	IS 5182 (Part-11) 2017
9	Benzo (a) Pyrene (BaP) - particulate phase only	ng/m ³	Not Detected	NS [¶]	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
10	Arsenic as As	ng/m ³	Not Detected	NS [¶]	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
11	Nickel as Ni	ng/m ³	Not Detected	NS [¶]	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
12	Lead as Pb	µg/m ³	Not Detected	1.0	CPCB guidelines for AQMN (Vol. I, NAAQMS/36/2012-13)
13	Hydrocarbon as HC	ppm	Not Detected	NS [¶]	Gas chromatography
14	HCl	µg/m ³	Not Detected	NS [¶]	USEPA 26A-1996
15	Chlorine as Cl ₂	µg/m ³	Not Detected	NS [¶]	IS 5162 (Part-19) 2014
16	Hydrogen Sulphide as H ₂ S	µg/m ³	Not Detected	NS [¶]	IS 5182 (Part-7) 2014

NS[¶]: Not Specified, Limit as per CPCB Consent Order No. AWH-109749 Issue Date: 14/09/2020 Up to 17/09/2025§: Ozone (O₃) & Carbon Monoxide (CO): Sampling 1 Hr.Detection Limit: Benzene as C₆H₆: 2.0 µg/m³; Benzo (a) Pyrene (BaP) - particulate phase only: 0.5 ng/m³; Arsenic as As: 2.0 ng/m³; Nickel as Ni: 5.0 ng/m³; Hydrocarbon as HC: 50 µg/m³; Hydro Chloric Acid As HCl: 5.0 µg/m³; Chlorine as Cl₂: 150 µg/m³; Hydrogen Sulphide as H₂S: 6.0 µg/m³; Lead as Pb: 0.1 µg/m³; Ozone (O₃): 5.0 µg/m³.


Ravi Jariwala
Sr. Environmental Scientist


Dr. Arun Bajpai
Lab Manager (Q)

Note: This report is subject to terms & conditions mentioned overleaf.

ANNEXURE 9



o/c

BEIL/GPCB/BRCH/2020/01

To,
Mr. F. M. Modi
Regional Officer
Gujarat Pollution control board
Bharuch

Date: 01.06.2020
PCB ID # 40137

Subject: Monsoon Planning for Monitoring & Control of Pollution.
Ref: GPCB/BRCH/TECH/T-183/3418 dated 15/05/2020

This is with reference to your above letter GPCB/BRCH/TECH/T-183/3418 dated 15/05/2020, we have taken following action as Monsoon Planning.

- We are regularly monitoring the Storm water at different points and taking all the necessary precautions required for preventing the contamination of storm water.
- We are also monitoring the Final discharge of our industry for any irregular discharges by any means.
- We have already provided a proper Storage Shed of capacity of 4000 MT with appropriate roof in order to avoid mixing up of rainwater/ industrial effluent while the entire landfill site will be covered with two layers of Tarpaulins to prevent any mixing of rainwater with the hazardous waste. Covering of Landfill photographs is attached for your ready reference.
- We are implementing all the relevant guidelines for management plan for used/discarded packages/materials etc.
- We are monitoring all the Chemical Storage tanks/Hazardous waste storage sites and ensuring that there is no overflow/leakage to the surrounding environment.
- We are regularly monitoring & operating Air Pollution Control equipment's / measures efficiently in such a manner that flue gas / process emissions conform to the GPCB norms We are also ensuring that the accidental leakages, fugitive emissions are prevented.
- We have provided lids on storage tanks and intermediate tanks to control odor.
- We will regularly monitor all the ETP Units and ensure that there is no flooding.
- Entire site is cleaned, and its housekeeping is being maintained to keep it in good condition.
- We are regularly reviewing all the safety measures in the plant and we are following all the Act/Rules/Guidelines issued by the various authorities.
- We have provided 15meter greenbelt surrounding periphery of our compound wall. We will plant trees wherever required in our existing green belt.

We hope the above adequately meets your guideline for monsoon management.

Thanking you,
Yours faithfully,

For BEIL Infrastructure Limited, Dahej

Authorized Signatory

Encl

1. Landfill Monsoon Cover Photographs
2. Green Belt Plan

C.C. Mr. D.M.Thaker
Unit Head, Hazardous Waste Cell
Gujarat Pollution Control Board
Gandhinagar - 382010

Post Received
Gujarat Pollution Control Board
BHARUCH

CIN NO: U45300GJ1907PLC032696

Works Office - Plot No. D-43, Dahej Anand Road, GIDC Estate, Dahej, T. Vagra - 392 130, Dist. Bharuch (Gujarat)
Phone : (02641) 291129, E-mail: mistryrg@beil.co.in
Regd. Office - Plot No. 9701-16, GIDC Estate, Post Box No. 62, Ankleshwar 393 002, Dist. Bharuch (Gujarat)
Phones : (02546) 253135, 225228, Fax : (02642) 222649, E-mail: dalwedibd@beil.co.in

Landfill Monsoon Cover Photographs



ANNEXURE 10



Ref: BEIL/DAHEJ/20-21

Date: 01-02-2020

To,
Joint Director of Industrial Safety and Health,
2nd Floor, Multi Storage Building,
Opp. Gayatrinagar,
Kanbivaga, Bharuch-392001


Sub: Submission of Onsite Emergency Plan

Dear Sir,

With reference to above subject, we are submitting Onsite Emergency Plan as per GFR rule 68 | Sub rule (12).


This is for your information and record please.
We hope that the above is in order.
Thanking you,

For, BEIL Infrastructure Limited, Dahej





(Authorized Signatory)


સહી અને સ્ટામ્પ
બેઈલ ઇન્ફ્રાસ્ટ્રક્ચર લિમિટેડ
દાહેજ



BEIL Infrastructure Limited

**(FORMERLY KNOWN AS BHARUCH ENVIRO INFRASTRUCTURE
LIMITED)**

ONSITE EMERGENCY PLAN

Update On February, 2020

Plot No # D-43, GIDC Industrial Estate, Dahej - 392130

Ta - Vagra, Dist - Bharuch, Gujarat

On-Site Emergency Plan of M/s BEIL Infrastructure Ltd. Dahej

CONTENTS

CHAPTER NO.	DESCRIPTION	PAGE NO.
01	ORGANIZATION INFORMATION	06
02	SITE DEMOGRAPHY	07
	2.1 DETAILS OF COMPANY	07
	2.2 SITE PLAN	08
03	INFORMATION ON THE PRELIMINARY HAZARD ANALYSIS	09
	3.1 TYPES OF ACCIDENT	15
	3.2 SYSTEM ELEMENTS OR EVENT THAT CAN LEAD A MAJOR ACCIDENT	15
	3.3 MAJOR HAZARDS IN STORAGE AREAS	15
	3.4 SAFETY RELEVANT COMPONENTS	16
	3.5 OTHER HAZARDS AND CONTROLS	16
04	DESCRIPTION OF HAZARDOUS CHEMICALS AT PLANT SITE	16
	4.1 STORAGE HAZARDS: (QUANTITIES AND TOXICOLOGICAL DATA)	16
	4.2 PROCESS HAZARD	17
05	MAXIMUM CREDIBLE ACCIDENT SCENARIO & CONSEQUENCES ANALYSIS	18
	5.1 INTRODUCTION	18
	5.2 MAXIMUM CREDIBLE ACCIDENT (MCA)	18
06	EMERGENCY MANAGEMENT PROCEDURES AND SYSTEM	21
	6.1 WARNING ALARM AND SAFETY AND SECURITY SYSTEM	21
07	ROLES AND RESPONSIBILITY OF KEY PERSONNEL	24
	7.1 ROLES AND RESPONSIBILITY OF EMERGENCY RESPONSE PERSONNEL	30
	7.2 INCIDENT CONTROLLERS	38
	7.3 DEPUTY INCIDENT CONTROLLERS	38
	7.4 SITE MAIN CONTROLLERS	39
	7.5 KEY PERSONS	39
	7.6 ESSENTIAL PERSONS	40
	7.7 EMERGENCY CONTROL CENTRE	41
08	FIRE FIGHTING AND OTHER ARRANGEMENTS FOR OFF-SITE EMERGENCY	44
	8.1 AVAILABILITY OF FIRE FIGHTING FACILITES	44
	8.2 AVAILABILITY OF FIRE EXTINGUISHERS	45
09	MEDICAL ARRANGEMENTS FOR ON-SITE PLAN	46
10	EMERGENCY DUE TO NATURAL CALAMITIES	47
	10.1 TYPES OF NATURAL CALAMITIES & ITS ACTION PLAN	47
11	MUTUAL AID ARRANGEMENTS	50
	11.1 TYPES OF ACCIDENT	50
	11.2 RESPONSIBILITY ASSIGNED	50
	11.3 MUTUAL AID	50
12	COMMUNICATION ARRANGEMENTS DURING EMERGENCY AND FOR OFF-SITE EMERGENCY	56
	12.1 RAISING THE ALARM	56
	12.2 DECLARING THE MAJOR EMERGENCY	56
	12.3 TELEPHONE MESSAGES	56

	12.4 RUNNER	57
	12.5 COMMUNICATION OF EMERGENCY	57
CHAPTER NO.	DESCRIPTION	PAGE NO.
	12.6 IMPORTANT INTERNAL TELEPHONE NUMBERS	59
	12.7 IMPORTANT EXTERNAL TELEPHONES NUMBERS	60
13	INTEGRATION OF SITE ON-SITE EMERGENCY PLAN WITH DISTRICT OFF-SITE PLAN	63
	13.1 PURPOSE OF THE OFF SITE EMERGENCY PLAN	63
	13.2 A SCHEMATIC DIAGRAM SHOWING ACTION FROM INCIDENT PLACE TO STATE LEVEL GROUP IS SHOWN BELOW	65
	13.3 ROLES AND RESPONSIBILITIES OF STAKEHOLDERS INCLUDING EXTERNAL AGENCIES	66



Ref: BEIL/DAHEJ/20-21

Date: 01-02-2020

To,
Joint Director of Industrial Safety and Health,
2nd Floor, Multi Storage Building,
Opp. Gayatrinagar,
Kanbivaga, Bharuch-392001

Sub: Submission of Mock Drill report

Dear Sir,

With reference to above subject, we would like to inform you that we have conducted a mock drill on 1st February 2020 to test our procedure of On-Site Emergency Plan and preparedness. We are submitting herewith report of mock drill.

We hope that the above is in order.

Thanking you,

For: BEIL Infrastructure Limited, Dahej



[Authorized Signatory]

શ્રી. દલિપ
કચ્છીયત મેમ્બરી એન્ડ ટ્રસ્ટ
૧૫૨૫



BEIL Infrastructure Limited

(FORMERLY KNOWN AS BHARUCH ENVIRO INFRASTRUCTURE
LIMITED)

DISASTER MANAGEMENT PLAN

Update On February, 2020

Plot No # D-43, GIDC Industrial Estate, Dahej – 392130

Ta – Vagra, Dist – Bharuch, Gujarat

On-Site Emergency Plan of M/s BEIL Infrastructure Ltd. Dahej

CONTENTS

CHAPTER NO.	DESCRIPTION	PAGE NO.
01	ORGANIZATION INFORMATION	06
02	SITE DEMOGRAPHY	07
	2.1 DETAILS OF COMPANY	07
	2.2 SITE PLAN	08
03	INFORMATION ON THE PRELIMINARY HAZARD ANALYSIS	09
	3.1 TYPES OF ACCIDENT	15
	3.2 SYSTEM ELEMENTS OR EVENT THAT CAN LEAD A MAJOR ACCIDENT	15
	3.3 MAJOR HAZARDS IN STORAGE AREAS	15
	3.4 SAFETY RELEVANT COMPONENTS	16
	3.5 OTHER HAZARDS AND CONTROLS	16
04	DESCRIPTION OF HAZARDOUS CHEMICALS AT PLANT SITE	16
	4.1 STORAGE HAZARDS: (QUANTITIES AND TOXICOLOGICAL DATA)	16
	4.2 PROCESS HAZARD	17
05	MAXIMUM CREDIBLE ACCIDENT SCENARIO & CONSEQUENCES ANALYSIS	18
	5.1 INTRODUCTION	18
	5.2 MAXIMUM CREDIBLE ACCIDENT (MCA)	18
06	EMERGENCY MANAGEMENT PROCEDURES AND SYSTEM	21
	6.1 WARNING ALARM AND SAFETY AND SECURITY SYSTEM	21
07	ROLES AND RESPONSIBILITY OF KEY PERSONNEL	24
	7.1 ROLES AND RESPONSIBILITY OF EMERGENCY RESPONSE PERSONNEL	30
	7.2 INCIDENT CONTROLLERS	38
	7.3 DEPUTY INCIDENT CONTROLLERS	38
	7.4 SITE MAIN CONTROLLERS	39
	7.5 KEY PERSONS	39
	7.6 ESSENTIAL PERSONS	40
	7.7 EMERGENCY CONTROL CENTRE	41
08	FIRE FIGHTING AND OTHER ARRANGEMENTS FOR OFF-SITE EMERGENCY	44
	8.1 AVAILABILITY OF FIRE FIGHTING FACILITIES	44
	8.2 AVAILABILITY OF FIRE EXTINGUISHERS	45
09	MEDICAL ARRANGEMENTS FOR ON-SITE PLAN	46
10	EMERGENCY DUE TO NATURAL CALAMITIES	47
	10.1 TYPES OF NATURAL CALAMITIES & ITS ACTION PLAN	47
11	MUTUAL AID ARRANGEMENTS	50
	11.1 TYPES OF ACCIDENT	50
	11.2 RESPONSIBILITY ASSIGNED	50
	11.3 MUTUAL AID	50
12	COMMUNICATION ARRANGEMENTS DURING EMERGENCY AND FOR OFF-SITE EMERGENCY	56
	12.1 RAISING THE ALARM	56
	12.2 DECLARING THE MAJOR EMERGENCY	56
	12.3 TELEPHONE MESSAGES	56
	12.4 RUNNER	57

	12.5 COMMUNICATION OF EMERGENCY	57
CHAPTER NO.	DESCRIPTION	PAGE NO.
	12.6 IMPORTANT INTERNAL TELEPHONE NUMBERS	59
	12.7 IMPORTANT EXTERNAL TELEPHONES NUMBERS	60
13	INTEGRATION OF SITE ON-SITE EMERGENCY PLAN WITH DISTRICT OFF-SITE PLAN	63
	13.1 PURPOSE OF THE OFF SITE EMERGENCY PLAN	63
	13.2 A SCHEMATIC DIAGRAM SHOWING ACTION FROM INCIDENT PLACE TO STATE LEVEL GROUP IS SHOWN BELOW	65
	13.3 ROLES AND RESPONSIBILITIES OF STAKEHOLDERS INCLUDING EXTERNAL AGENCIES	66

ANNEXURE 11



BEIL INFRASTRUCTURE LTD.
ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY
CERTIFICATE OF ANALYSIS

Report No: NM/19102020	Date: 19-10-2020	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43, NEAR BHARAT RASAYAN LIMITED, DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	19-Oct-2020	Date of Sample Receipt	19-Oct-2020
Sample Monitored by	Kamalakant Raut	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standards	Remarks
1	Nr. Main Gate	Industrial	dB(A)	64	75	OK
2	B/H. ADM Building	Industrial	dB(A)	62	75	OK
3	Nr. EB-1 Bore well	Industrial	dB(A)	63	75	OK
4	B/H. Landfill Cell No.04	Industrial	dB(A)	58	75	OK
5	Nr. Drum shed Area	Industrial	dB(A)	70	75	OK
6	Opp. Khetan Industrial	Industrial	dB(A)	66	75	OK
7	Nr. Stabilization Plant	Industrial	dB(A)	65	75	OK
8	Nr. DG Set	Industrial	dB(A)	71	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dB(A)	68	75	OK

Remarks (if Any):

For, BEIL Infrastructure Limited


Chemist


Mr. Sathishkumar Gaddam
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
Tel : (02641)291129E-mail-mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD.

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: NM/19112020	Date: 19-11-2020	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43, NEAR BHARAT RASAYAN LIMITED. DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	19-Nov-2020	Date of Sample Receipt	19-Nov-2020
Sample Monitored by	Vishal C. Patel	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standards	Remarks
1	Nr. Main Gate	Industrial	dBa	61.8	75	OK
2	B/H. ADM Building	Industrial	dBa	57.6	75	OK
3	Nr. EB-1 Bore well	Industrial	dBa	64.6	75	OK
4	B/H. Landfill Cell No.04	Industrial	dBa	59.2	75	OK
5	Nr. Drum shed Area	Industrial	dBa	73.6	75	OK
6	Opp. Khetan Industrial	Industrial	dBa	64.6	75	OK
7	Nr. Stabilization Plant	Industrial	dBa	56.8	75	OK
8	Nr. DG Set	Industrial	dBa	72.6	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dBa	72.8	75	OK

Remarks (if Any):

For, BEIL Infrastructure Limited


Chemist


Mr. Sathishkumar Gaddam
(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.- Bharuch (Gujarat) Dahej-392130
Tel : (02641)291129E-mail-mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD.

ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY

CERTIFICATE OF ANALYSIS

Report No: NM/18122020	Date: 18-12-2020	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43, NEAR BHARAT RASAYAN LIMITED. DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	18-Dec-2020	Date of Sample Receipt	18-Dec-2020
Sample Monitored by	Vishal C. Patel	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standards	Remarks.
1	Nr. Main Gate	Industrial	dBA	66.4	75	OK
2	B/H. ADM Building	Industrial	dBA	58.2	75	OK
3	Nr. EB-1 Bore well	Industrial	dBA	63.6	75	OK
4	B/H. Landfill Cell No.04	Industrial	dBA	51.4	75	OK
5	Nr. Drum shed Area	Industrial	dBA	70.6	75	OK
6	Opp. Khetan Industrial	Industrial	dBA	65.4	75	OK
7	Nr. Stabilization Plant	Industrial	dBA	62.6	75	OK
8	Nr. DG Set	Industrial	dBA	67.4	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dBA	64.5	75	OK

Remarks (if Any):

Chemist

For, BEIL Infrastructure Limited

Mr. Sathishkumar Gaddam

(Sr.Manager-QA)

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130

Tel : (02641)291129E-mail-mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)

CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD.
ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY
CERTIFICATE OF ANALYSIS

Report No: NM/05012021	Date: 05-01-2021	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO.D/43, NEAR BHARAT RASAYAN LIMITED, DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	05-Jan-2021	Date of Sample Receipt	05-Jan-2021
Sample Monitored by	Vishal C. Patel	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standards	Remarks.
1	Nr. Main Gate	Industrial	dBA	64.2	75	OK
2	B/H. ADM Building	Industrial	dBA	57.2	75	OK
3	Nr. EB-1 Bore well	Industrial	dBA	62.6	75	OK
4	B/H. Landfill Cell No.04	Industrial	dBA	53.4	75	OK
5	Nr. Drum shed Area	Industrial	dBA	70.2	75	OK
6	Opp. Khetan Industrial	Industrial	dBA	62.8	75	OK
7	Nr. Stabilization Plant	Industrial	dBA	61.7	75	OK
8	Nr. DG Set	Industrial	dBA	65.6	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dBA	72.8	75	OK

Remarks (if Any):

For, BEIL Infrastructure Limited

Mr. Sathishkumar Gaddam

(Sr.Manager-QA)

Chemist

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
Tel : (02641)291129E-mail-mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD.
ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY
CERTIFICATE OF ANALYSIS

Report No: NM/04022021	Date: 04-02-2021	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO. D/43, NEAR BHARAT RASAYAN LIMITED. DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	04-Feb-2021	Date of Sample Receipt	04-Feb-2021
Sample Monitored by	Vishal C. Patel	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standards	Remarks.
1	Nr. Main Gate	Industrial	dB(A)	63.5	75	OK
2	B/H. ADM Building	Industrial	dB(A)	58.4	75	OK
3	Nr. EB-1 Bore well	Industrial	dB(A)	60.6	75	OK
4	B/H. Landfill Cell No.04	Industrial	dB(A)	55.2	75	OK
5	Nr. Drum shed Area	Industrial	dB(A)	68.2	75	OK
6	Opp. Khetan Industrial	Industrial	dB(A)	60.4	75	OK
7	Nr. Stabilization Plant	Industrial	dB(A)	61.2	75	OK
8	Nr. DG Set	Industrial	dB(A)	65.3	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dB(A)	72.6	75	OK

Remarks (if Any):

For, BEIL Infrastructure Ltd.

For
ANALYSED BY

ASB
VERIFIED BY

Mr. Sathish Kumar Gaddam
AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
Tel : (02641)291129E-mail-mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696



BEIL INFRASTRUCTURE LTD.
ANALYTICAL RESEARCH AND DEVELOPMENT LABORATORY
CERTIFICATE OF ANALYSIS

Report No: NM/17032021	Date: 17-03-2021	Page No: 1/1
------------------------	------------------	--------------

Name and Address of the Customer	BEIL INFRASTRUCTURE LIMITED PLOT NO. D/43, NEAR BHARAT RASAYAN LIMITED, DAHEJ-AMOD ROAD, G.I.D.C-DAHEJ-392 130 TALUKA-VAGRA, DIST-BHARUCH (GUJARAT)		
Sample Description	Noise Monitoring	Sample Identification/Code	---
Date of Sampling	17-Mar-2021	Date of Sample Receipt	17-Mar-2021
Sample Monitored by	Vishal C. Patel	Sampling Procedure	Integrating Noise meter

Sr No	Noise Monitoring Sample Location	Category	Unit	Results (Avg.) Day time (06:00 am to 10:00 pm)	Day Standar ds	Remarks.
1	Nr. Main Gate	Industrial	dBa	66.2	75	OK
2	B/H. ADM Building	Industrial	dBa	62.3	75	OK
3	Nr. EB-1 Bore well	Industrial	dBa	63.4	75	OK
4	B/H. Landfill Cell No.04	Industrial	dBa	58.6	75	OK
5	Nr. Drum shed Area	Industrial	dBa	69.8	75	OK
6	Opp. Khetan Industrial	Industrial	dBa	64.2	75	OK
7	Nr. Stabilization Plant	Industrial	dBa	63.2	75	OK
8	Nr. DG Set	Industrial	dBa	67.4	75	OK
9	Nr. Monsoon Shed (New)	Industrial	dBa	71.8	75	OK

Remarks (if Any):

For, BEIL Infrastructure Ltd.

VSP
ANALYSED BY

FIAA
VERIFIED BY

A. Sathish Kumar
AUTHORIZED SIGNATORY
MR. SATHISHKUMAR GADDAM

Plot No.D-43 GIDC Dahej, Dist.: Bharuch (Gujarat) Dahej-392130
Tel : (02641)291129E-mail:mistryrg@beil.co.in

Regd. Office: Plot No 117-118, GIDC Estate, Ankleshwar-393002, Dist.: Bharuch (Gujarat)
CIN No: U45300GJ1997PLC032696

ANNEXURE 12



BUREAU
VERITAS

Bureau Veritas Certification

BEIL INFRASTRUCTURE LTD.



PLOT NO.D. 43, DAHEJ INDUSTRIAL ESTATE, TALUKA-VAGRA,
DIST. BHARUCH – 392 130, GUJARAT, INDIA.

Bureau Veritas Certification Holding SAS – UK Branch certifies that the Management System of the above organization has been audited and found to be in accordance with the requirements of the Management System standards detailed below.

Standards

ISO 14001:2015 & ISO 45001:2018

Scope of certification

OPERATION & MAINTENANCE OF COMMON HAZARDOUS WASTE TREATMENT, STORAGE AND DISPOSAL FACILITY (SECURE LANDFILL & MEE) AND RELATED ANALYTICAL SERVICES.

Original cycle start date for ISO 14001:	25 June 2016
Original cycle start date for ISO 45001:	08 March 2021
Expiry date of previous cycle for ISO 14001:	25 June 2019
Expiry date of previous cycle for ISO 45001:	Not Applicable
Recertification Audit date for ISO 14001:	04 May 2019
Certification Audit date for ISO 45001:	27 June 2020
Recertification cycle start date for ISO 14001:	24 June 2019
Certification cycle start date for ISO 45001:	08 March 2021

Subject to the continued satisfactory operation of the organization's Management System, this certificate expires on: **25 June 2022**

Certificate No. **IND.19.12190U** Version : **2** Revision date: **08 March 2021**

Signed on behalf of BVCH SAS – UK Branch
Jagdheesh N. MANIAN
Head – CERTIFICATION, South Asia
Commodities, Industry & Facilities Division



0008

Certification body address: 5th Floor, 66 Prescott Street, London, E1 8HG, United Kingdom.

Local office: Bureau Veritas (India) Private Limited (Certification Business)
72 Business Park, Marol Industrial Area, MIDC Cross Road "C",
Andheri (East), Mumbai – 400 093, India.

Further clarifications regarding the scope of this certificate and the applicability of the management system requirements may be obtained by consulting the organization.
To check this certificate validity please call **+91 22 6274 2000**.

ANNEXURE 13



O/C

Ref: BEIL/DHJ/2020/20

Date: 31.12.2020
PCB ID # 40137

To,
The Director
Ministry of Environment, Forest & Climate Change
Western Region Office,
Kendriya Paryavaran Bhavan,
Link Road No.3, E-5 Ravishankar Nagar
Bhopal-462016

Sub.: Half yearly compliance report of two EC's for Common Treatment, Storage, Disposal facility (TSDf) & Multi Effect Evaporator (MEE) and Installation of two incinerators & capacity enhancement of existing landfill, period Apr'20 to Sep'20.

Ref: 1. Environmental Clearance No. SEIAA/GUJ/EC/7(d)/227/2013 dated 22nd July, 2013 for setting up of common hazardous waste Treatment, Storage, Disposal facility (TSDf) and Multi Effect Evaporator (MEE)
2. Environmental Clearance No. IA/GJ/MIS/55789/2016 dated 11th June, 2018 for Installation of two incinerators and capacity enhancement of Existing Landfill Facility

Dear Sir,

BEIL is operating a TSDf facility consisting of a secured land fill Facility and Multi Effect Evaporator (MEE) followed by spray dryer located at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch, Gujarat.

We are submitting here with the half yearly Compliance status report of both the above referred Environment Clearances for period April 2020 to September 2020. With this, we would also like to inform that EC no. IA/GJ/MIS/55789/2016 dated 11th June, 2018 for Installation of two incinerators and capacity enhancement of existing Landfill has not been implemented till date. However, planning stage is complete, and we have received CTE No 164667 on 24.12.2019.

BEIL has received and disposed land fillable Hazardous waste: During 1st April 2020 to 30th September 2020 is 62622.827 MT. Cumulative quantity disposed in landfill from the beginning (up to 30.09.2020) is 445818.623 MT.



We hope that the above is in order. In case you need any additional information, we can provide the same on hearing from you.

Thanking you,

Yours faithfully,
For, BEIL Infrastructure Limited

Authorized Signatory

Encl: As above
✓ CC: Gujarat Pollution Control Board,
Bharuch

CC: Central Pollution Control Board,
Vadodara

18/2-1-2021
Post Received
Gujarat Pollution Control Board
BHARUCH

ANNEXURE 14



Ref: BEIL/DAHEJ/2015

30th July, 2014

PCD-ID 40137

To,
 Ministry of Environment, Forest and Climate Change,
 Regional Office, Western Region,
 Kendriya Parivahan Bhavan,
 Lakh Road 3
 E-5, Ravishankar Nagar
 Bhopal-462016

Kind Attn: Dr. A. Mehta, Director (5)

Subject: Compliance with point no. 64 and 70 of Environmental Clearance

Reference: Environmental Clearance order no. SEA/AA/GJ/EC/E(D)/227/2013, Dated: 22/07/2013

Dear Sir,

Bharuch Enviro Infrastructure Ltd., is a Secured Landfill Facility for Hazardous waste at Dahaj Industrial Estate. We had received our Environmental Clearance for our TSDF and MEF facility at Plot no. D-40, Dahaj Industrial Estate, Tal. Vagra, Dist: Bharuch (Gujarat) in category II(c) of Schedule annexed with EIA Notification dated 14/09/2006, vide order no. SEA/AA/GJ/EC/7(D)/227/2013, Dated: 22/07/2013.

We would like to submit the following information in compliance to Point No.64 & 70 of the said Environmental Clearance.

1. Date of Application for loan	24.10.2012
2. Financial Closure (Date of Sanction of Loan)	07.03.2014 (Copy Attached)
3. Drawings Approved by DT, Delhi on	21.10.2013 (Copy Attached)
4. Land Development and construction work Started on	13.09.2014
5. Date of Commissioning	29.04.2015

Please consider the above details. Copy of Environmental Clearance Attached.

Thanking you,

For, Bharuch Enviro Infrastructure Ltd. (Dahaj Unit)

B. D. Dholwadi
 Chief Executive Officer

VSD
 1-8-2015
 Project Officer, GPCB
 Regional Office, Gandhinagar
 Gandhinagar, Gandhinagar

C.C: (1) State Level Environment Impact Assessment Authority
 Gujarat Pollution Control Board,
 "Parivahan Bhavan" Sector 10-A,
 Gandhinagar - 382010

(2) Mr. K. C. Mistry - Sr. Environment Engineer, GPCB, Gandhinagar

(3) The Regional Officer, GPCB, Bharuch

ANNEXURE 15

EC

A.A.DOLTI
MEMBER SECRETARY
SEIAA (GUJARAT)



Government of Gujarat

STATE LEVEL ENVIRONMENT
IMPACT ASSESSMENT
AUTHORITY
GUJARAT

No. SEIAA/GUJ/EC/7(d)/ 227/2013

Date: 22 JUL 2013
Time Limit

Sub: Environment Clearance for M/s. Bharuch Enviro Infrastructure Limited (BEIL) for setting up of a common hazardous waste Treatment, Storage, Disposal Facility (TSDF) and Multiple Effect Evaporation (MEE) Plant at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch..... in Category 7 (d) of Schedule annexed with EIA Notification dated 14/9/2006.

Dear Sir,

This has reference to your application along with Form-I vide letter dated 30/12/2011, Final Environmental Impact and Risk Assessment Report vide letter dated 22/04/2013, submitted to the SEAC, seeking Environmental Clearance under Environment Impact Assessment Notification, 2006.

The proposal is for Environmental Clearance for M/s. Bharuch Enviro Infrastructure Limited (BEIL) for setting up of a common hazardous waste Treatment, Storage, Disposal Facility (TSDF) and Multiple Effect Evaporation (MEE) Plant at Plot No. D-43, Dahej Industrial Estate, Tal. Vagra, Dist. Bharuch. M/s. Bharuch Enviro Infrastructure Ltd. [BEIL] proposes to set up TSDF (14-Lac MT) and MEE Plant (3 x 200 KL/day) at Plot No. D-43, Dahej Industrial Estate, Dist. Bharuch. The proposal falls under project / activity no. 7(d) in the Schedule of the EIA Notification, 2006.

The proposed project falls under category 7(d) of the schedule of the EIA Notification, 2006. As the proposed project is situated in the industrial area which is not notified, it falls in Category B as per the schedule of the EIA Notification-2006.

The project activity is covered in 7(d) and is of 'B' Category. Since, the proposed project is located in the industrial area which is not notified, public consultation is required as per paragraph 7(i) (iii) (i) (b) of the Environment Impact Assessment Notification-2006. Public hearing of the project was conducted by the GPCB on 05/04/2013 at 11:30 Hrs. at P. J. Chheda Janki Vidyalay, Dahej, Tal. Vagra, Dist. Bharuch.

The SEAC, Gujarat had recommended to the SEIAA, Gujarat, to grant the Environment Clearance to this project for the above-mentioned project. The proposal was considered by SEIAA, Gujarat in its meeting held on 22.07.2013 at Gandhinagar. Since the public consultation is required for the project, the SEIAA hereby accords Environmental Clearance to above project under the provisions of EIA Notification dated 14th September, 2006 subject to the compliance of the following conditions.

A.SPECIFIC CONDITIONS:

1. Ground water table at the project site shall be ascertained through the GWRDC before initiating construction of secured landfill site. The depth of the secured land fill site shall be decided based on the ground water level at the site and bottom of the secured landfill site shall be kept at least 2 m above the ground water table.
2. Construction of the secured landfill site shall be undertaken meticulously keeping in view the existing natural drainage pattern of the site to ensure that the natural drainage is not affected. All construction designs/drawings relating to the proposed landfill site must have approvals of reputed institutes like NPC / IIT.
3. The proponent shall ensure that design and construction of secured landfill site is as per the guidelines of CPCB with proper leachate collection arrangement.
4. The proponent shall ensure that the transportation of the Hazardous wastes to the TSDF conforms to the norms laid down in the Hazardous Wastes (Management, Handling and Transboundary Movement) Rules, 2008.
5. Project proponent shall ensure that wastes with organic content > 5% of degradable organic matters are not disposed in to the landfill. However, required arrangement for collection, treatment and disposal of gases from the secured landfill, if any, shall be provided.
6. The TSDF & MEE shall only handle the waste generated from the member units.
7. The project proponent shall set up necessary facility for on site testing of wastes to decide the requirement of treatment if any, before disposal.
8. Project proponent shall carryout periodical ground water/soil monitoring in and around the site to check the contamination including TCLP test for heavy metals.
9. The third party assessment on functioning of the TSDF and MEE shall be carried out through a reputed institute like NPC, IIT

or any academic / research institute of similar repute once in a year and mitigation measures as may be suggested by such institute shall be implemented in consultation with the Gujarat Pollution Control Board.

A.1 WATER:

10. Fresh water requirement shall not exceed 350 KL/day and it shall be met only through water supply from the GIDC. Metering of water shall be done and its records shall be maintained. No ground water shall be tapped for the project requirements in any case.
11. A leachate collection system shall be provided to collect the leachates at a collection point. Leachate shall be pumped from leachate wells and shall be treated in in-house MEE. However, in the initial two - three years, the leachate shall be sent to BEIL, Ankleshwar for treatment with MEE.
12. BEIL shall explore the possibilities for reuse of condensate water generated from MEE plant for landfill construction, gardening and domestic purpose within the BEIL.
13. Domestic wastewater and condensate water from the MEE shall be disposed off as per the norms to be laid down by the GPCB.
14. Enough care shall be taken to prevent any leakages/accidental spillages during conveyance of the effluent from the member units to the MEE.
15. Separate electricity meter shall be provided at the MEE. A proper operation logbook of the MEE containing records of quantities and qualities of leachate from secured landfill site and effluent received from the member units, energy consumption etc. shall be maintained and furnished to the GPCB from time to time.
16. Storage Tank of adequate capacity shall be provided to hold effluent for at least 48 hours in the case of either maintenance of the MEE or disturbances in MEE operations.
17. In case of power failure, stand-by D.G.Set/s having power generation capacity equivalent to the requirement of power to run the MEE shall be installed, so that the MEE can be operated even in case of power failure.

A.2 AIR:

18. Natural gas to the tune of 440 Nm³/day shall be used as a fuel in Boiler (5 T/Hr.) and a stack of 30 m height shall be provided to Boiler.
19. HSD to the tune of 3 KL/Month shall be used as a fuel in D.G. Set (600 KVA) and a stack of 9.3 m height shall be provided to D. G. Set.
20. The flue gas emission from Boiler and D.G.Set shall conform to the standards prescribed by GPCB. At no time, the emission levels shall go beyond the stipulated standards.
21. Project proponent shall carryout periodical air quality monitoring in and around the site including VOC, HC. Locations of ambient air quality monitoring stations shall be fixed in consultation with the GPCB.
22. All transporting routes within the premises shall have asphalt roads to minimize fugitive emission.

A.3 SOLID / HAZARDOUS WASTES:

23. The proponent shall ensure that the TSDF fulfills all the provisions of Hazardous Wastes (Management, Handling and Transboundary Movement) Rules, 2008 and the design and construction of secured landfill site is as per the guidelines of CPCB with proper leachate collection arrangement.
24. Temporary hazardous waste storage area of about 4000 MT capacity having impervious bottom and roof cover shall be provided as proposed.
25. The project proponent shall not store the hazardous wastes more than the quantity that has been permitted by the CPCB / Gujarat State Pollution Control Board.
26. The main operational site shall be kept covered by tarpaulin with separate rain water collection system during monsoon period.
27. Silt from MEE and discarded bags shall be disposed in the secured landfill site.
28. BEIL shall explore possibilities with respect to reduction and reuse of hazardous waste generated by member units and received at the project site.
29. Used oil shall be sold only to the registered recyclers.

A.4 SAFETY:

30. All necessary precautionary measures shall be taken to avoid any kind of accident during storage and handling of hazardous wastes.
31. Handling and storage of wastes shall be done in such a manner that minimal human exposure occurs.
32. All transportation of hazardous materials shall be as per the Motor Vehicle Act & Rules.
33. Hazardous materials storage shall be at an isolated designated location, bund/dyke walls shall be provided for storage tanks for Hazardous Chemicals.
34. Personal Protective Equipment shall be provided to workers and its usage shall be ensured and supervised.
35. First Aid Box and required Antidotes for the chemicals used in laboratory shall be made readily available in adequate quantity at all the times.

36. Training shall be given to all workers on safety and health aspects of handling hazardous wastes.
37. Occupational health surveillance of the workers shall be carried out on a regular basis and records shall be maintained as per the Factories Act and Rules. Pre-employment and periodical medical examination for all workers shall be undertaken as per statutory requirement.
38. Project proponent shall prepare and implement an On Site Emergency Management Plan and Disaster Management Plan (DMP) for the project as per the guidelines from Directorate of Industrial Safety and Health. Adequate fire fighting facilities shall be installed to handle the fire.

A.6 NOISE:

39. The overall noise level in and around the premises shall be kept well within the standards by providing noise control measures including engineering controls like acoustic insulation hoods, silencers, enclosures etc. on all sources of noise generation. The ambient noise level shall conform to the standards prescribed under The Environment (Protection) Act, 1986 & Rules.

A.6 GREEN BELT AND OTHER PLANTATION:


40. Project proponent shall develop green belt all along the periphery of the TSDF as per the CPCB guidelines with plant species that are significant and used for the pollution abatement. Drip irrigation system shall be used for the green belt for optimum utilization of the water resources.
41. BEIL shall also tie up with local agencies like gram panchayat, schools, social forestry office etc. for plantation at suitable open places in GIDC estate and nearby villages and shall submit an action plan of plantation for next five years to the GPCB.

B. OTHER CONDITIONS:

42. Project proponent shall obtain necessary Authorization / Consents from the Gujarat Pollution Control Board.
43. A separate Environment Management Cell equipped with full fledged testing laboratory facilities shall be set up to carry out the Environment Management and Monitoring functions.
44. In the event of de-functioning of MEE, receipt of effluent from member units shall be immediately stopped and they shall be intimated about the same. Effluent from the member units shall not be received until the desired efficiency of MEE has been achieved.
45. Adequate spares for waste and effluent collection, handling and transfer shall be maintained at all times.
46. BEIL shall comply with all the provisions of CPCB guidelines for TSDF as may be applicable from time to time.
47. BEIL shall maintain accurate records of their member units in respect of quantity of each product manufactured, quantities and qualities of waste & effluent generated, booked & supplied to the TSDF & MEE on day to day basis and shall submit the compiled records to the GPCB on monthly basis.
48. BEIL shall ensure that each & every member unit renews the agreement / membership on/before expiry of said agreement / membership and shall inform the GPCB about any unit not renewing the agreement / membership within stipulated period. BEIL shall immediately inform the Gujarat Pollution Control Board about termination / suspension of membership of any member unit.
49. BEIL shall instruct and make sure that each member unit provides effluent storage tank and hazardous waste storage area having adequate retention time.
50. BEIL shall not allow any new member or enhance waste / effluent quantity of existing members unless & until they have prior requisite permissions from competent authorities.
51. Pucca flooring / impervious layer shall be provided in the work areas, chemical storage areas and chemical handling areas to minimize soil contamination.
52. Good house keeping shall be maintained within the premises. All pipes, valves and drains shall be leak proof. Leakages from the pipes, pumps, shall be minimal and if occurs, shall be arrested promptly. Floor washing shall be admitted in to the effluent collection system for subsequent treatment and disposal through MEE.
53. During effluent transfer, spillages shall be avoided and gulland drain be constructed to avoid mixing of accidental spillages with storm water.
54. Necessary measures shall be taken to prevent contamination of storm water from wastes / effluent handled at site. The storm water drains shall be kept separate and shall remain dry throughout the year except monsoon.
55. BEIL shall intimate the GPCB about occurrence of any accident, act or event resulting in discharge of poisonous, noxious or polluting matter or the likelihood of the same into a stream or land or well.
56. The funds earmarked for environment protection measures should be maintained in a separate account and there should be no diversion of these funds for any other purpose. A year-wise expenditure on environmental safeguards should be reported.
57. All the issues raised in the public hearing shall be comprehensively addressed / complied with in a time bound manner.
58. BEIL shall assign specific budget for socio-economic upliftment of the surrounding villages and shall undertake eco-developmental measures including community welfare program most useful in the project area for the overall improvement of the environment in consultation with the District Development Officer / District Collector.
59. BEIL shall comply with all the recommendations as well as the environmental protection measures and risk mitigation measures/safeguards proposed in the REIA Report, Risk Assessment Report & Disaster Management Plan of the project.

60. In the event of a change in project profile or change in the implementation agency, a fresh reference shall be made to SEIAA / SEAC.
61. BEIL shall strive to obtain the ISO 14001 and OSHAS 18001 certification.
62. The project management shall extend full support to the officers of MoEF / GPCB during inspection of the project for monitoring purposes by furnishing full details and action plan including action taken reports in respect of mitigation measures and other environmental protection activities.
63. A six monthly monitoring report shall need to be submitted by the project proponents to the Regional Office of the MoEF and SEIAA regarding the implementation of the stipulated conditions in hard and soft copies to the regulatory authority concerned, on 1st June and 1st December of each calendar year..
64. The project proponents shall inform the Regional Office of MoEF at Bhopal as well as the SEIAA, the date of financial closure and final approval of the project by the concerned authorities and the date of start of land development work
65. BEIL shall also comply with any additional condition that may be imposed by the SEAC or the SEIAA or any other competent authority for the purpose of the environmental protection and management.
66. No further expansion or modifications in the plant likely to cause environmental impacts shall be carried out without obtaining prior Environment Clearance from the concerned authority.
67. The project authorities shall earmark adequate funds to implement the conditions stipulated by SEIAA as well as GPCB along with the implementation schedule for all the conditions stipulated herein. The funds so provided shall not be diverted for any other purpose.
68. The applicant shall inform the public that the project has been accorded environmental clearance by the SEIAA and that the copies of the clearance letter are available with the GPCB and may also be seen at the Website of SEIAA/ SEAC/ GPCB. This shall be advertised within seven days from the date of the clearance letter, in at least two local newspapers that are widely circulated in the region, one of which shall be in the Gujarati language and the other in English. A copy each of the same shall be forwarded to the concerned Regional Office of the Ministry.
69. The project authorities shall also adhere to the stipulations made by the Gujarat Pollution Control Board.
70. The project authorities shall inform the GPCB, Regional Office of MoEF and SEIAA about the date of financial closure and final approval of the project by the concerned authorities and the date of start of the project.
71. The SEIAA may revoke or suspend the clearance, if implementation of any of the above conditions is not found satisfactory.
72. The company in a time bound manner shall implement these conditions. The SEIAA reserves the right to stipulate additional conditions, if the same is found necessary. The above conditions will be enforced, inter-alia under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, Hazardous Wastes (Management, Handling and Transboundary Movement) Rules, 2008 and the Public Liability Insurance Act, 1991 along with their amendments and rules.
73. This environmental clearance is valid for five years from the date of issue.
74. Any appeal against this environmental clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 10 of the National Green Tribunal Act, 2010.

With regards,
Yours sincerely,


A.A. DOLTI)

Member Secretary

Issued to:

Shri B. D. Dalwadi, Sr. G.M. - Works,
Bharuch Enviro Infrastructure Ltd. [BEIL]
Plot No. 9701-16, GIDC Estate.
Post Box No. 82, Ankleshwar,
Dist. Bharuch - 393 002.

Copy to:-

1. The Secretary, SEAC, C/O. G.P.C.B. Gandhinagar - 382010.
2. The Chairman, Central Pollution Control Board, Parivesh Bhavan, CBD -cum-Office Complex,

East Arjun Nagar, New Delhi-110032

3. The Chief Conservator of Forests (Central), Ministry of Environment & Forests,
Regional Office (WZ), E-5, Arera Colony, Link Road-3, Bhopal-462016, MP
4. Monitoring Cell, Ministry of Environment and Forests, Paryavaran Bhavan, CGO Complex, New Delhi-110003.
5. The Member Secretary, Gujarat Pollution Control Board, Paryavaran Bhavan, Sector-10 A, Gandhinagar-382010
6. Select File


(A.A. DOLTI)

Member Secretary

S. K. I. S.

23 AUG 2013

Invoice No. 719

Time 1:30 P.M. Sign. 

TIMES CITY



ACCOUNTANT
 A professional accountant with 10 years of experience in the field of tax and auditing is seeking a challenging position with a leading organization. Please send your resume to: [Contact Info]

MARKETING MANAGER
 A marketing manager with 5 years of experience in the field of product and brand management is seeking a challenging position with a leading organization. Please send your resume to: [Contact Info]

S.R. Tradlink Pvt. Ltd.
 200-201, Market Complex, Near New Market, Gurgaon, Haryana, India. Contact: [Phone Number]

Blue Jade Textlink Pvt. Ltd.
 We are Manufacturing Company in Gurgaon, Haryana. We are looking for a Marketing Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

RTO launches learner's licence app Receives 150 Applications Through The App In Two Days

By [Author Name]

Maharashtra's Road Transport Department (RTD) has launched a mobile application for learner's licence applications. The app, named 'Learner's Licence', is available on both Android and iOS platforms. It allows users to apply for a learner's licence online, upload necessary documents, and track the status of their application. The app has received 150 applications in just two days, indicating a high level of interest from the public.



A person riding a motorcycle on a road, likely related to the article about learner's licences.

The app is designed to be user-friendly and accessible to a wide range of users. It provides a step-by-step guide for the application process, from creating an account to submitting the application. The RTD officials are optimistic about the app's success and hope it will streamline the process for applicants.

The app is available for free download from the Google Play Store and the Apple App Store. Users can also visit the RTD website for more information. The RTD is committed to providing efficient and transparent services to its citizens.

Category	Page No.	Start Date	End Date
Public Notice	10	10/10/2023	10/10/2023
Public Notice	10	10/10/2023	10/10/2023

PUBLIC NOTICE ENVIRONMENTAL CLEARANCE
 The Government of Maharashtra, Department of Environment and Forests, is seeking applications for Environmental Clearance (EC) for the proposed project. The project is located in the [Location]. The EC is required for the project to be implemented. The application should be submitted to the [Authority].

PUBLIC NOTICE ENVIRONMENTAL CLEARANCE
 The Government of Maharashtra, Department of Environment and Forests, is seeking applications for Environmental Clearance (EC) for the proposed project. The project is located in the [Location]. The EC is required for the project to be implemented. The application should be submitted to the [Authority].

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

URGENT REQUIREMENT
 Technical consultant & Production Manager. We are looking for a Technical consultant & Production Manager. Contact: [Phone Number]

ANNEXURE 16

Environmental Management Plan Compliance

Discipline	Environmental hazard	Mitigation Measures and Action plan	Compliance Status
Secured Landfill Facility			
Temporary storage of Hazardous waste	Leachate Generation	Collection of leachate and treatment	Complied. Temporary storage of hazardous waste is provided for monsoon period. Leachate generated is collected and send to MEE at BEIL, Ankleshwar unit.
Loading the hazardous waste in dumper	Fugitive emission	Coverage of the dumper to prevent dusting	Complied. Secured authorized dedicated closed dumpers are being used.
	Spillage of waste on the the floor	Avoid spillages by careful handling of the solid waste Clean the floor regularly and collect the waste & dispose in landfill	Complied. Handling has been carried out to avoid spillage of the solid waste. Regular cleaning is also done.
	Leakage/spillage during transportation	inspection of the dumpers and ensuring that there is no leakage/spillage	Complied. Regular inspection carried out of dumpers for detecting any leakages or spillage.
	Health impacts on the workers	Usage of Hydraulic dumpers/hook loaders to prevent manual handling Usage of PPEs by all Employees Medical checkup - pre employment and routine	Complied. Hydraulic dumpers are used for transporting waste. Appropriate PPEs are provided to the workers while manual handling of the waste. Pre-employment and routine medical checkups are being carried out.

Transportation			
Transportation of Waste	Littering the waste on the road	Inspect the dumpers and ensure that there is no leakage/spillage from the vehicle Loaded dumpers/trucks with waste should be fully covered. Impart training to the drivers Dumpers/trucks should be leak proof	Complied. Regular inspection of the dumpers is also done to ensure that there is no leakage/spillage from the vehicle. Loaded dumpers/ vehicles are being covered, leak proof as well. Drivers are given training also.
	Disposal of waste at non designated place	Manifest System	Complied. We are following valid manifest system according to new hazardous and other waste (Handling and management) rules 2016.
	Contamination of the tyres of vehicles entering landfill area	After loading/unloading the waste, tyres should be washed and washed water shall be sent for treatment	Complied. After loading/ unloading the tires are washed and waste water is sent for treatment.
Final Disposal			
Final Disposal of the hazardous waste into secured landfill facility	Violent reaction/ fire	Strictly to follow the acceptance criteria Check the reactivity of the wastes prior to disposal	Complied. Comprehensive and fingerprint analysis are carried out before accepting the waste to strictly following acceptance criteria for landfill.
	Excessive leachate generation in monsoon season	Cover the sub-cells of the facility with tarpaulin to prevent entry of rain water Close monitoring of the site round the clock during monsoon	Complied. Adequate covering of the sub cells with tarpaulin is done during monsoon.
	Blowing away of the waste dust with the wind	Spray water during summer season Cover the waste layer with fresh soil and compact it.	Complied. Water is being sprayed for dust suppression. And daily coverage of waste with clay layer is being done.

	Disposal of waste at the wrong place in the premises leachate handling	Provide indicators and sign boards for systematic operation. Properly designed leachate collection wells Daily monitoring of levels in the wells Transfer of leachate from the wells to storage for treatment	Complied. Necessary sign board are provided. Adequate numbers of leachet collection wells are constructed, daily level monitoring is being done.
Sanitary facilities for the staff	Generation of the waste water.	Sewage water to be taken to Septic Tank for disposal	Complied. Soak pit/septic tank are provided to dispose domestic waste water
Laboratory facilities	Generation of the waste water.	Segregation of the waste water Toxic waste should be sent for incineration Contaminated water to be taken to MEE	Complied. Contaminated water from the laboratory is sent to MEE at BEIL, Ankleshwar unit.
Operation, Maintenance and Closure of the Facility	Contamination of Environment	The site will be operated, maintained and closure of the facility will be done as per approved plan by SPCB and in accordance with guidelines published by CPCB	Complied. The site is being operated, maintained and closure of the facility will be done as per approved plan by SPCB and in accordance with guidelines published by CPCB
Post Closure Phase	Ambient air Quality	Monitoring of ambient air quality for various parameters	Complied. Monitoring of ambient air quality for various parameters is being done.
	Emission from landfill vents	Monitoring of vents for HCs, VOCs, monthly	Complied. Monitoring of vents for HCs, VOCs is being done.
	Leachate Generation	Sampling and analysis of leachate for various parameters, monthly Treatment of generated leachate in Multiple Effect Evaporator	Complied. Sampling and analysis of leachate for various parameters is being done. Leachate generated is collected and send to MEE at BEIL, Ankleshwar unit.

	Ground water Monitoring	Monitoring of Ground Water	Complied. Monitoring of Ground Water on regular basis is being conducted.
	Soil contamination	Monitoring of soil samples	Complied. Monitoring of soil samples on regular basis is being conducted.
	Stability of the landfill	Regular inspection and maintenance of the coverage system	Complied. Regular inspection and maintenance of the coverage system is being done.

ANNEXURE 17



UNITED INDIA INSURANCE COMPANY LIMITED
2ND FLOOR,OPP HOTEL LORDS PLAZA ,B/H RAILWAY STATION OLD N.H. NO-
8,GIDC,ANKLESHWAR ,BHARUCH ANKLESHWAR, BHARUCH, GUJARAT
BHARUCH - 393002 GUJARAT
PHONE: (2646) 220151 FAX: EMAIL:

PUBLIC LIABILITY ACT POLICY
Policy No.:1806012721P100990596

PERIOD OF INSURANCE
From 00:00 hrs of 01/05/2021
To midnight of 30/04/2022

Insured

M/s BEIL INFRASTRUCTURE LTD

PLOT NO.(1) 9701 TO 9716/ 9801 TO 9828/ 9901 TO 9906/ 9923 TO 9928(2) KISHOKLAND
BET. NO. 9701 TO 16.(3) ROAD AREA BET.NO.9801 TO 9814/ VAR PLOT NO. OF JITALI , GIDC,
(4) AHMEDABAD UNIT MUNICIPAL SOLID WASTE SITE,B/H TORRENT POWER SUB
STATION,NR HOTEL DEV,NAROL-SARKHEJ HIGHWAY,GYASPUR,AHMEDABAD (5)DAHEJ UNIT
PLOT NO. 43, GIDC DAHEJ, BHARUCH,ANKLESHWAR.(6)JHAGADIA UNIT,PLOT NO. 911/C,GIDC
JHAGADIA,DIST:BHARUCH-393110.
BHARUCH
393002
GUJARAT

Agent Name : DIPIKABEN H JADAV
Agent Code : AGN1028172
Mobile/Landline Number/Email : 9558465778
: hiteshjadav66@gmail.com

The genuineness of the policy can be verified through "Verify Your Policy" link at www.uiic.co.in.

For any Information, Service Requests, Claim intimation and Grievances please write to 180601@uiic.co.in

Download Customer App(www.uiic.co.in). REGD. & HEAD OFFICE, 24, WHITES ROAD, CHENNAI - 600014.

Website : <http://www.uiic.co.in>

Printed By : CUSTOMER @ 30/04/2021 4:21:53 PM

This document is digitally signed

Signer: N MOHAN SANKAR
Date: Fri, Apr 30, 2021 16:21:44 IST
Location: United India Insurance Company Ltd
Reason: Signing Policy for UIIC

PUBLIC LIABILITY ACT POLICY SCHEDULE

Policy No.	1806012721P100990596	Prev. Pol. No.	1806012720P100738031
Name Of Insured/ID	M/s BEIL INFRASTRUCTURE LTD/23074087603		
Tel.(O)	Fax	Tel.(R)	Mobile
Business/Occupation	None	Email	siddharth.shah@beil.co.in
Period of Insurance	From 00:00Hours of 01/05/2021		To Midnight of 30/04/2022

CO-INSURANCE DETAILS:	UIIC 180601 : 100%
PREMIUM:	THIRTY-SIX THOUSAND SEVEN HUNDRED SIXTY-TWO RUPEES ONLY

Description of risk : DISP. OF SOLID & LIQUID WASTE

Territory(Geographical Limits)/Jurisdiction:-

Territory	Jurisdiction	Details	Description
India	India	PLOT NO.(1) 9701 TO 9716/ 9801 TO 9828/ 9901 TO 9906/ 9923 TO 9928(2) KISHOKLAND BET. NO. 9701 TO 16.(3) ROAD AREA BET.NO.9801 TO 9814/ VAR PLOT NO. OF JITALI , GIDC, ANKLESHWAR.(4) AHMEDABAD UNIT MUNICIPAL SOLID WASTE SITE,B/H TORRENT POWER SUB STATION,NR HOTEL DEV,NAROL-SARKHEJ HIGHWAY,GYASPUR,AHMEDABAD (5)DAHEJ UNIT PLOT NO. 43, GIDC DAHEJ, BHARUCH (6) BHARUCH ENVIRO INFRASTRUCTURE LTD, JHAGADIA UNIT,PLOT NO. 911/C,GIDC JHAGADIA,DIST:BHARUCH-393110.	ANKLESHWAR/DAHEJ/AHMD/JHAGADIA UNIT

Subsidiaries:-

Excess/Deductible:-	
Compulsory Excess/Deductible:-	₹209,301.70
Voluntary Excess/Deductible:-	₹0.00

TRANSPORTATION OF CHEMICALS

INDEMNITY LIMIT	
Any One ACCIDENT	: ₹ 41,860,340.00
Aggregate During the Policy Period (Not exceeding three Times of any one accident of Indemnity Limit)	: ₹ 125,581,020.00
Contribution to environment Relief fund	: ₹ 36,762.00
Other Discount Amount	: ₹ 129444.01

Estimated Annual turnover	
Proposed Year	Previous Year
3500000000	2500000000

Premium	: ₹	36,762.00
CGST(9%)	: ₹	3,309.00
SGST(9%)	: ₹	3,309.00
Stamp duty	: ₹	1.00
Total	: ₹	80,142.00
Receipt Number	: 10118060121100854149	
Receipt Date	: 28/04/2021	

Agency/Broker Code:	AGN1028172
Dev.Officer Code:	20683

Underwriting Remarks	DISPOSAL OF HAZARDOUS, SOLID AND LIQUID WEST BY INCINERATION AND LANDFILLING, ON VARIOUS PLOTS MANTIONED AS ABOVE.
-----------------------------	--

Customer GST/UIN No.:	24AAACB8075F1ZU	Office GST No.:	24AAACU5552C3ZN
SAC Code:	997139	Invoice No. & Date:	27211100990596 & 28/04/2021
Amount Subject to Reverse Charges-NIL			

Anti Money Laundering Clause:-In the event of a claim under the policy exceeding ₹ 1 lakh or a claim for refund of premium exceeding ₹ 1 lakh, the insured will comply with the provisions of AML policy of the company. The AML policy is available in all our operating offices as well as Company's web site.

LET US JOIN THE FIGHT AGAINST CORRUPTION. PLEASE TAKE THE PLEDGE AT <https://pledge.cvc.nic.in>.

Extension Names	LIMIT OF INDEMNITY (₹) AOA : AOY
Indemnity Cover	41860340:125581020

Underwriting Remarks	DISPOSAL OF HAZARDOUS, SOLID AND LIQUID WEST BY INCINERATION AND LANDFILLING, ON VARIOUS PLOTS MANTIONED AS ABOVE.
-----------------------------	--

RETROACTIVE DATE	LIMIT OF INDEMNITY(₹)
01/05/1998	41860340

Date of Proposal and Declaration: 01/05/2021

IN WITNESS WHEREOF, the undersigned being duly authorised has hereunto set his/her hand at
BO ANKLESHWAR 180601 on this 28th day of April ,2021

For United India Insurance Co. Ltd.

Affix Policy
Stamp here.

Authorised Signatory.

**LIABILITY INSURANCE POLICY
(UNDER PUBLIC LIABILITY INSURANCE ACT 1991)**

1. OPERATIVE CLAUSE

Whereas the Insured Owner named in the Schedule hereto and carrying on business described in the said Schedule has applied to the UNITED INSURANCE COMPANY LIMITED (hereinafter called the "Company") for the indemnity hereinafter contained and has made a written proposal and declaration which shall be the basis of this contract and is deemed to be incorporated herein and has paid the premium and statutory contributions towards the Environmental Relief Fund as per the provision of the Public Liability Insurance Act, 1991 and the rules framed there under, as amended from time to time..

NOW THIS POLICY WITNESSETH that subject to the terms, exceptions and conditions contained herein or endorsed herein, the Company will indemnify the Insured Owner against the statutory liability arising out of accidents occurring during the currency of the Policy due to handling hazardous substances as provided for in the said Act and the Rules framed thereunder as amended from time to time.

2. DEFINITIONS:

- a) "ACT" unless otherwise specifically mentioned shall mean the Public Liability Insurance Act 1991 as amended from time to time.
- b) "Accident" means an accident involving a fortuitous sudden or unintentional occurrence while handling any hazardous substance resulting in continuous, intermittent or repeated exposure to death of, or injury to any person or damage to any property but does not include an accident by reason only of war or radioactivity.
- c) "Handling" in relation to any hazardous substance means the manufacture processing, treatment, package, storage, transportation by vehicle, use, collection, destruction, conversion, offering for sale, transfer or the like of such hazardous substances.
- d) "Hazardous Substance" means any substance or preparation which is defined as hazardous substance under the Environment (Protection) Act, 1986 and exceeding such quantity as may be specified, by notification by the Central Government;
- e) "Owner" means a person who owns, or has control over handling any hazardous substance at the time of accident and includes:
 - i) in the case of a firm, any of its partners;
 - ii) in the case of an association, any of its members and
 - iii) in the case of a company, any of its directors, managers, secretaries or other officers who is directly in charge of, and is responsible to the company for the conduct of the business of the company;
- f) "Turnover" shall mean
 - i) manufacturing units- Annual Gross Sales of all goods including all levies and taxes
 - ii) Godowns/ Warehouse owners - Total Annual rental receipts
 - iii) Transport Operators - Total Annual freight receipts
 - iv) Others - Total Annual gross receipts.

3. EXCLUSIONS:

This Policy does not cover liability;

- 1. arising out of wilful or intentional non-compliance of any Statutory provisions.
- 2. in respect of fines, penalties, punitive and / or exemplary damages.
- 3. arising under any other legislation except in so far as provided for in Section 8 Sub-Section (1) and (2) of the "Act".
- 4. in respect of damage to property owned, leased or hired or under hire purchase or on loan to the Insured or otherwise in the Insured Owner's control, care or custody.
- 5. directly or indirectly occasioned by, happening through or in consequence of war, invasion, act of foreign enemy, hostilities (whether war be declared or not) civil war, rebellion, revolution, insurrection or military or usurped power;
- 6. directly or indirectly caused by or contributed to by:

- a) ionising radiation or contamination by radioactivity from any nuclear fuel or from any nuclear waste from the combustion of nuclear fuel;
- b) the radioactive, toxic, explosive or other hazardous properties of any explosive nuclear assembly or nuclear component thereof.

4. CONDITIONS:

1. The Insured Owner shall give written notice to the Company as soon as reasonably practicable of any claim made against the Insured Owner or of any specific event or circumstance that may give rise to a claim. The Insured Owner shall immediately give to the Company copies of notice of application forwarded by the Collector and all such additional information and or assistance that the Company may require.
2. No admission, offer, promise or payment shall be made or given by or on behalf of the Insured Owner under this Policy without the written consent of the Company.
3. The Company shall not be liable for any claim for relief made after five years from the date of occurrence of the accident.
4. The Insured Owner shall keep record of annual turnover, and at the time of renewal of insurance declare such turnover and all other details as may be required by the Company. The Company shall at all reasonable times have full rights to call for and examine such records.
5. If at the time of happening of any accident resulting in a claim under this Policy there be any other insurance covering the same liability then the Company shall not be liable to pay or contribute more than its rateable proportion of such liability.
6. This Policy may be cancelled by the Insured Owner by giving 30 days' notice in writing to the Company in which event the Company will retain the premium at short period scale of rates subject to there not having occurred an accident during the Policy period which may give rise to a claim(s), failing which no refund of premium shall be allowable.
7. This insurance may be terminated at any time at the request of the Insured, in which case the Company will retain the premium at customary short period rate for the time the policy has been in force. This insurance may also at any time be terminated at the option of the Company, on 15 days' notice to that effect being given to the Insured, in which case the Company shall be liable to repay on demand a rateable proportion of the premium for the unexpired term from the date of the cancellation. In either case premium will be refunded only if there is no claim under the policy
8. If the Company shall disclaim liability to the Insured Owner for any claim hereunder and if such claim shall not within 12 calendar months from the date of such disclaimer have been made the subject matter of a suit in a competent court of law, then the claim for all practical purposes shall be deemed to have been abandoned and shall not thereafter be recoverable hereunder or be made the subject matter of any suit.
9. The Company shall not be liable to make any payment in respect of any claim if such claim shall be in any manner fraudulent or supported by any person on behalf of the Insured Owner and/or if the Insurance has been continued in consequence of any material misstatement or non disclosure of any material information by or on behalf of the Insured Owner. In such a case if the Company pays any amount to the claimant due to any Statutory provision, such amount shall be recoverable from the Insured Owner.
10. The Policy and the Schedule shall be read together as one contract and any word or expression to which a specific meaning has been assigned in the Act and the Rules framed thereunder or under this Policy shall bear such specific meaning.
11. Any dispute regarding interpretation of the terms, conditions and exceptions of this Policy shall be determined in accordance with the law and practice of a court of competent jurisdiction within India.

Communicable Disease Exclusion Clause:

1. Notwithstanding any provision, clause or term of this insurance contract to the contrary, this insurance Contract excludes any loss, cost, damage, liability, claim, fines, penalty or expense or any other amount of whatsoever nature, whether directly or indirectly and/or in whole or in part, related to, caused by, contributed to by, resulting from, as a result of, as a consequence of, attributable to, arising out of, arising under, in connection with, or in any way involving (this includes all other terms commonly used and/or understood to reflect or describe nexus and/or connection from one thing to another whether direct or indirect):
 - 1.1 a Communicable Disease and/or the fear or threat (whether actual or perceived) of a Communicable Disease and/or the actual or alleged transmission of a Communicable Disease regardless of any other cause or event contributing and/ or occurring concurrently or in any sequence thereto, and
 - 1.2 a pandemic or epidemic, as declared by the World Health Organisation or any governmental authority.
2. As used herein, Communicable Disease means: any infectious, contagious or communicable substance or agent and/or any infectious, contagious or communicable disease which can be caused and/or transmitted by means of substance or agent where:
 - 2.1 the disease includes, but is not limited an illness, sickness, condition or an interruption or disorder of body functions, systems or organs, and
 - 2.2 the substance or agent includes, but is not limited to, a virus, bacterium, parasite, other organism or other micro-organism (whether asymptomatic or not); including any variation or mutation thereof, whether deemed living or not, and
 - 2.3 the method of transmission, whether direct or indirect, includes but not limited to, airborne transmission, bodily fluid transmission, transmission through contact with human fluids, waste or the like, transmission from or to any surface or object, solid, liquid or gas or between organisms including between humans, animals, or from any animal to any human or from any human to any animal, and
 - 2.4 the disease, substance or agent is such:
 - 2.4.1 that causes or threatens damage or can cause or threaten damage to human health or human welfare, or
 - 2.4.2 that causes or threatens damage to or can cause or threaten damage to, deterioration to, contamination of, loss of value of, loss of marketability of or loss of use or usefulness of, tangible or intangible property. For avoidance of doubt, Communicable Disease includes but is not limited to Coronavirus Disease 2019 (Covid -19) and any variation or mutation thereof.
3. For further avoidance of doubt, any contingent or other business interruption loss, cost, damage, loss of income, loss of use, increased cost of working and/or extra expense arising out of or attributable to:
 - 3.1 any partial or complete closure of and/or slowdown in, including but not limited to any closure by or under the advisories of public, military, government or civil authorities, or any denial of access to insured premises, or customer and or supplier premises (including service / utility providers), or

3.2 change in consumer behaviour, or

3.3 an absence of infected employees or employees suspected of being infected shall not be covered by this insurance Contract. .

4. For still further avoidance of doubt, loss, cost, damage, liability, claim, fines, penalty or expense or any other amount excluded hereby, includes but is not limited to any cost to identify, clean-up, detoxify, disinfect, decontaminate, mitigate, remove, evacuate, repair, replace, monitor, sanitize or test: (1) for a Communicable Disease or (2) any tangible or intangible property covered by this [insurance Contract] that is affected by such Communicable Disease.

5. It is clarified that (1) no other prior, concurrent or subsequent provision, clause, term or exception of this insurance Contract (including (but not limited to) any prior, concurrent or subsequent endorsement and/or any provision, clause, term, buy back or exception that operates, or is intended to operate, to extend the coverage of, or protections provided by, this insurance Contract] by whatever name called like any coverage extension, additional coverage, global extension, exception to any exclusion); (2) any change in the law, clause or similar provision; (3) any follow the fortunes clause or similar provision; and/or (4) no change in the law or any regulation (to the extent permitted by applicable law), shall operate to provide any insurance, coverage or protection under this insurance Contract that would otherwise be excluded through the exclusion set forth in this [Endorsement][Clause].

6. If the insurer alleges that by reason of this [Endorsement][Clause] any amount is not covered by this insurance Contract the burden of proving the contrary shall rest in the insured.

Pandemic /Epidemic Specific Exclusion Clause:

Notwithstanding any provision, clause or term of this Contract, this insurance Contract excludes any first party and/or third party actual or alleged loss, injury, sickness, disease, death, medical payment, defence cost, cost, damage, liability, claim, fines, penalty, compensation, expenses or any amount of whatsoever nature, whether directly or indirectly and/or in whole or in part, arising out of (this includes all other terms commonly used and/or understood to reflect or describe, direct or indirect nexus and/or connection between one thing and another), intentional or unintentional violation of

a. The provisions of Disaster Management Act, 2005 as amended from time to time

b. The provisions of The Epidemic Diseases Act 1897 as amended from time to time

c. The provisions of any act dealing with public health and/or public safety

d. The rules, regulations, orders, guidelines, policies, notification etc issued from time to time under any of the above acts.

'Policy form - Claims made with right to defend.'

This is a system generated document and any manual alteration / correction / overwriting in the document will make it invalid.

ANNEXURE 18



BHARUCH ENVIRO INFRASTRUCTURE LTD.

Plot No.9701-16, GIDC, Ankleshwar.

PROCEDURE TO BE FOLLOWED FOR LANDFILL MEMBERSHIP

01. Application in standard form (Available at BEIL)
02. Document to be submitted with Application.
 - (i) List of Directors.
 - (ii) List of Raw Materials.
 - (iii) Effluent Treatment flow sheet diagram.
 - (iv) Solid Waste storage facility details.
 - (v) Authorization (Solid Waste) copy of GPCB.
 - (vi) Sludge Analysis Report by approved Laboratory by GPCB.
 - (vii) SSI Certificate.
 - (viii) Plot Allotment Letter.
 - (ix) Board Resolution / Partnership Deed Copy
 - (x) GST Acknowledgment No:-
03. On clearance / scrutinize of Application, fees to be paid by **D.D payable at Ankleshwar (Capacity Commitment Charge / Member Ship Fess Non Refundable).**
 - (a) **Bharuch District – Medium Scale & Large Scale Member**
 - Rs.1500/- Per MT Annual Quantity.
 - GST @ 18% (CGST @ 9% and SGST @ 9%)
04. On clearance / scrutinize of Application, fees to be paid by **D.D payable at Ankleshwar.**
05. Stamp papers of **Rs.50/-** value of fees paid are to be submitted to BEIL. After submission of stamp papers, after 15-20 days for agreement. Please contact the following address:

P.S:- Stamp paper is valid for Six Month from the date of purchase.

06. Agreement to be signed by Authorised person approved by members Board of Directors proof to be submitted.
07. BEIL will issue a **certificate** after signing Agreement.
08. Member has to obtained a valid authorisation from GPCB mentioning permission disposal of solid waste at BEIL. Its copy to be submitted to BEIL otherwise waste not be accepted.
09. A TREM CARD to be submitted to BEIL and to be used for every consignment of waste.
10. Operation charges are to be paid in advance by local Chequ / D.D. as per enclosed sheet.
11. Only following solid waste are accepted as per authorisation given by GPCB to BEIL.

Sr.No.	Waste	Sr.No.	Waste
01.	Gypsum Sludge	06.	Waste Insulation Material
02.	ETP Sludge	07.	Non-Recyclable Plastic Waste
03.	Iron Sludge		
04.	Incineration Ash Sludge.		
05.	Brine Sludge		



BHARUCH ENVIRO INFRASTRUCTURE LTD.

Plot No.9701-9716, GIDC, ANKLESHWAR

Tel No.(02646)253 135, 225 228

APPLICATION FORM

1. Name of the unit :
2. Names of Directors / Partners :
3. Address :
4. Type of Industry : Small Scale / Medium Scale / Large Scale
5. Qty. of solid waste expected to be disposed off in the landfill per annum. :
6. **Capacity Commitment Charge / Membership paid by D. D. Payable at Ankleshwar.** : DD No._____ Date_____ Drawn on_____ for Rs._____

I/We have gone through the details of the landfill facility proposed to be developed at Ankleshwar GIDC Estate. We agree to become a member of the proposed company and would like to utilize the facility on a long term basis. We shall make further payments against equity as shown in the covering letter.

Place :

Date :

(Signature & Rubber Stamp)



BHARUCH ENVIRO INFRASTRUCTURE LTD.

Plot No.9701-9716, GIDC, ANKLESHWAR

Tel No.(02646)253 135, 225 228

SOLID WASTE DATA

PART – I UNIT INFORMATION

- a. Name of the Unit :
- b. Unit In-Charge :
- c. Address of the Unit :

Phone No.:

Email Add:

- d. Location : ANKLESHWAR / PANOLI / JHAGADIA

Sector

- (Tick) : (1) Drugs &Pharma (2) Dyes & Inter
(3) Pesticides (4) Organic
(5) Inorganic (6) Others

PART-II PRODUCTS AND BY-PRODUCTS MANUFACTURED:

Major Products/
By-Products

Quantity Per Year

PART-III

- (a) Would you like to avail the facility of proposed Centralized Secured Landfill at Ankleshwar Industrial Estate : Yes / No
- (b) If yes, mention the quantity of solid waste to be disposed off. : _____MT / Year
- (c) Do you have the facility of storing the solid waste in monsoon? : Yes / No
- (d) Whether the unit is having Authorization from GPCB ? If yes attach a copy of the same



BHARUCH ENVIRO INFRASTRUCTURE LTD.

Plot No.9701-9716, GIDC, ANKLESHWAR

Tel No.(02646)253 135, 225 228

PART-IV SOLID WASTE INFORMATION

(A) INFORMATION ABOUT SOLID WASTE TO BE LAND FILLED:

Type of Solid Wastes	Source	Physical property (Slurry / Sludge / Solid)	Quantity	
			Ton Per Day	Ton Per Year
1. Gypsum / Lime Sludge				
2. ETP Sludge				
3. Iron Sludge				
4. Incineration Ash				
5. Brine Sludge				
6. Others				

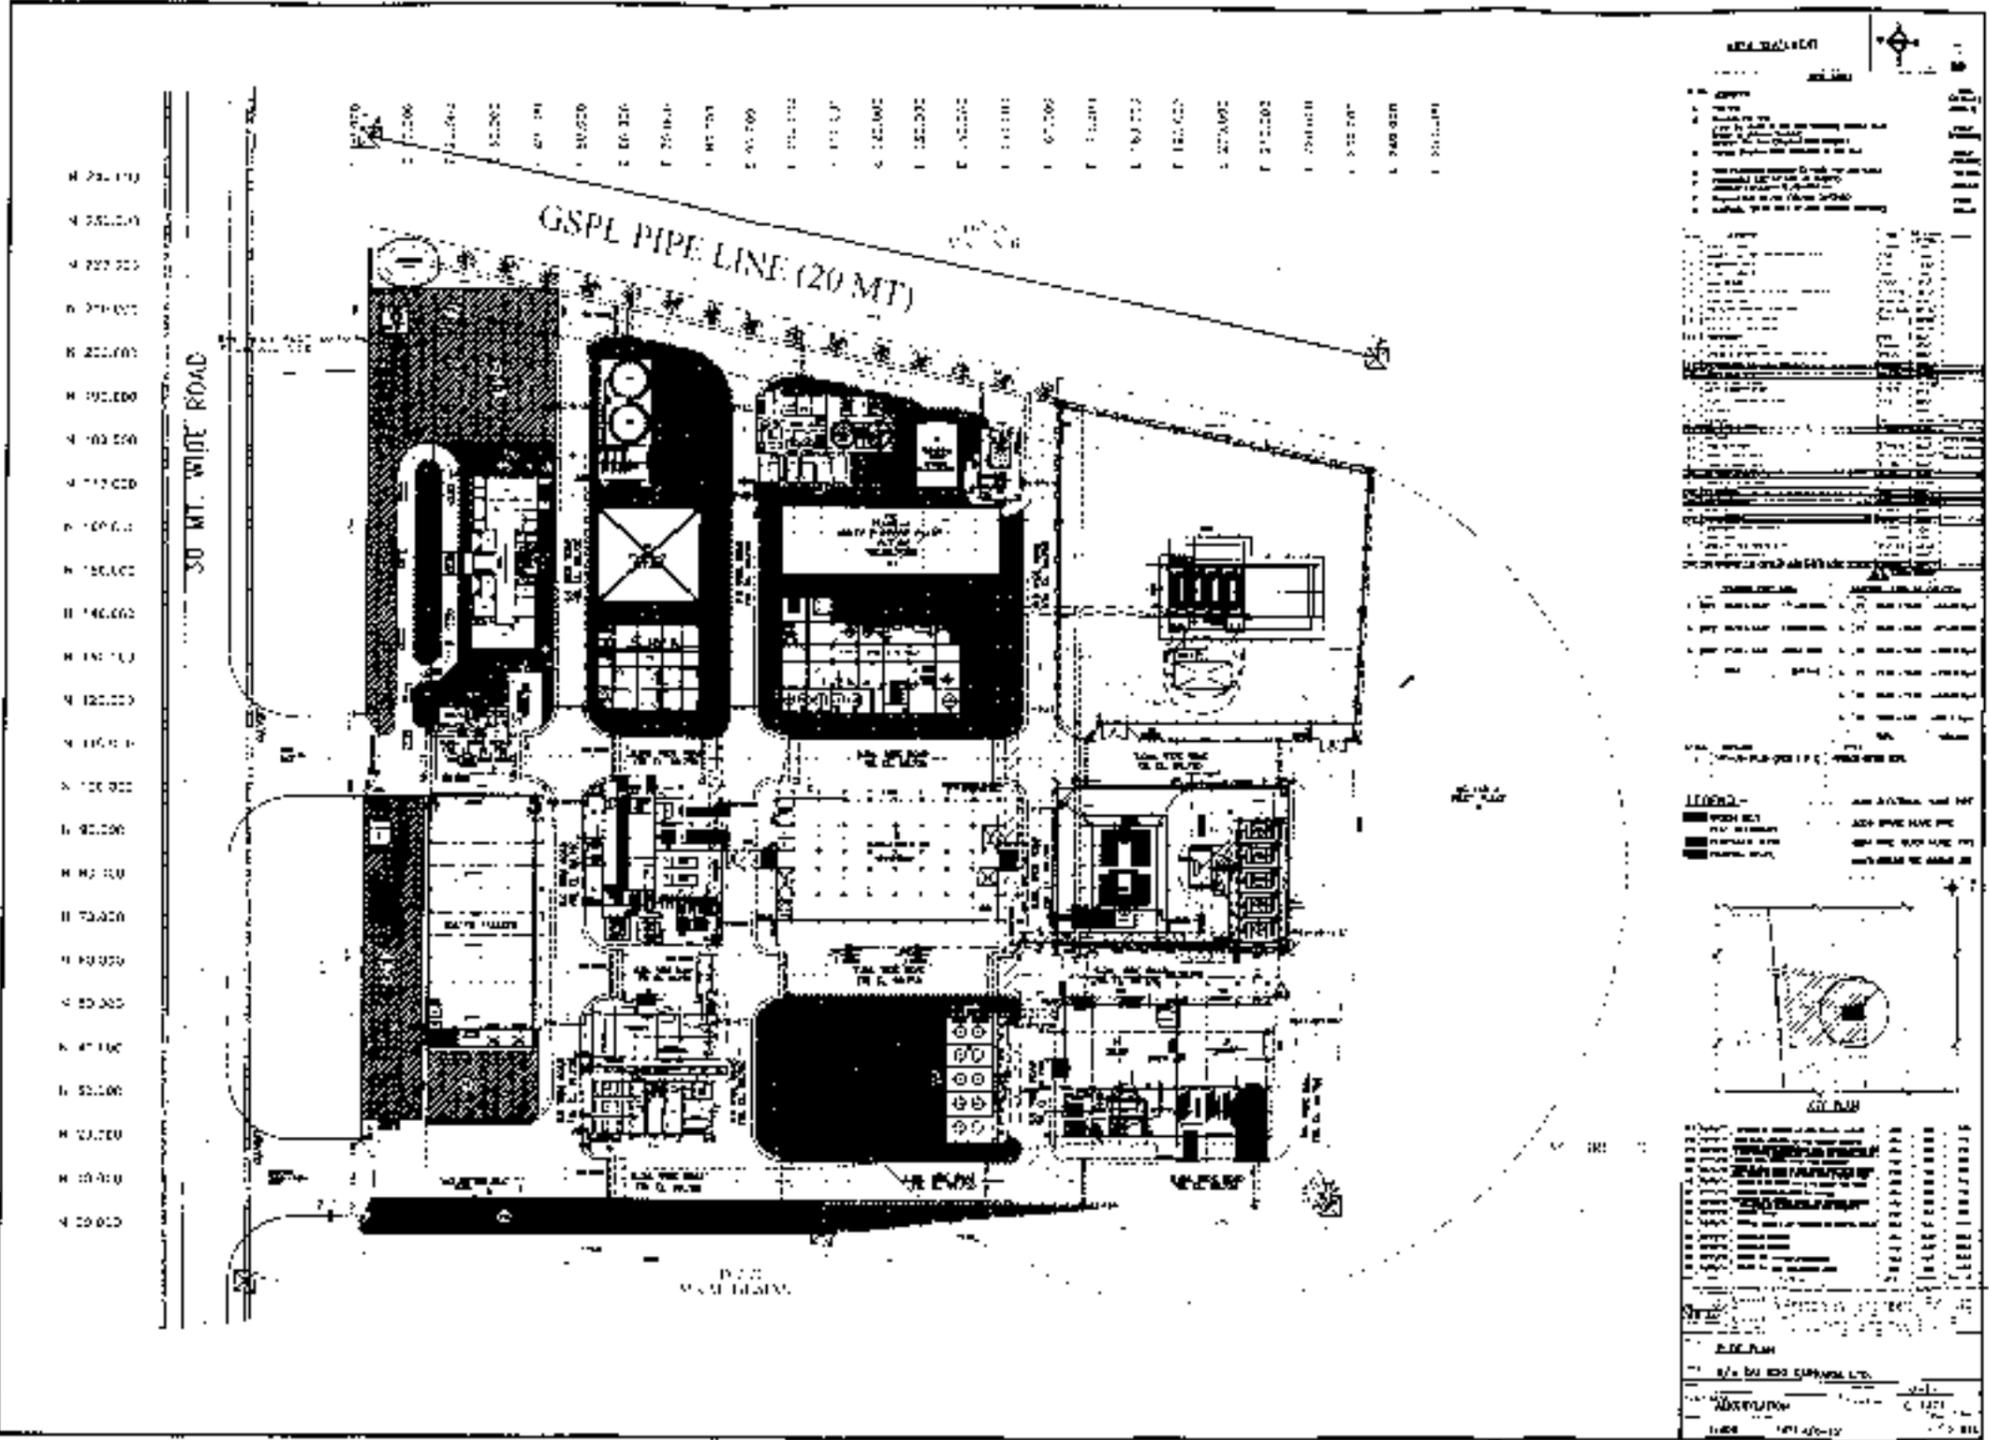
(B) SOLID WASTE NOT FOR LANDFILL.

Type of Solid Wastes	Source	Physical property (Slurry / Sludge / Solid)	Quantity	
			Ton Per Day	Ton Per Year
1. Treated Heavy Metal Sludge				
2. Treated CN Waste Sludge				
3. Spent Carbon Residue				
4. Spent Activated Clay				
5. Alkaline Sludge				
6. Any Other				

<u>SR. NO.</u>	<u>CUSTOMER NAME</u>	<u>BOOKING</u>	<u>CUST. CITY</u>	<u>GPCB CONSENT NO</u>	<u>STORAGE FACILITY</u>
1	ALKYL AMINES CHEMICALS LTD.	25	DAHEJ	AWH-76129	YES
2	BHARAT RASAYAN LIMITED	3000	DAHEJ	AWH-90645	YES
3	CHLORIDES INDIA	100	DAHEJ	AWH-33367	YES
4	DARAMIC BATTERY SEPARATOR INDIA PVT. LTD.	100	DAHEJ	AWH-83988	YES
5	FERMENTA BIOTECH LTD.	125	DAHEJ	AWH-76123	YES
6	FIRMENICH AROMATICS PRODUCTS (I) PVT. LTD.	400	DAHEJ	AWH-32740	YES
7	GUJARAT FLUORO CHEMICALS LTD. (12/A)	1000	DAHEJ	AWH-16130	YES
8	GUJARAT NARMADA VALLEY FERTILIZERS & CHEMICALS LTD. (TDI DAHEJ UNIT)	1000	DAHEJ	AWH-60288	YES
9	HEMANI INDUSTRIES LTD.-DAHEJ	410	DAHEJ	AWH-65178	YES
10	INDO BAIJIN CHEMICALS PVT. LTD.	158	DAHEJ	AWH-64169	YES
11	INSECTICIDES INDIA LTD.	150	DAHEJ	AWH-77931	YES
12	MEGHMANI ORGANICS LTD. (P. NO.Z-31)	100	DAHEJ	AWH-61030	YES
13	MEGHMANI UNICHEM LLP (P. NO.CH-3)	100	DAHEJ	AWH-48306	YES
14	MEHALI PAPERS PVT. LTD.	150	DAHEJ	AWH-84029	YES
15	NOCIL LIMITED	20	DAHEJ	AWH-53656	YES
16	PIDILITE INDUSTRIES LTD. - DAHEJ	8	DAHEJ	AWH-81053	YES
17	ROXUL ROCKWOOL INSULATION INDIA PVT. LTD.	1000	DAHEJ	AWH-43715	YES
18	SRF LIMITED	300	DAHEJ	AWH-24521	YES
19	TORRENT PHARMACEUTICALS LTD. - DAHEJ	150	DAHEJ	AWH-66310	YES
20	UNIVERSAL CHEMICALS & INDUSTRIES PVT. LTD.	300	DAHEJ	AWH-62153	YES
21	WELSPUN CORP LTD.	20	DAHEJ	AWH-45026	YES
22	TTK PRESTIGE LTD.	45	KARJAN	AWH-59849	YES
23	KERAKOLL INDIA PVT LTD	300	VADODARA	AWH-69417	YES
24	POLY CAB WIRE PVT. LTD. (UNIT-4)	10	VADODARA	AWH-16971	YES
25	INDUCTOTHERM (INDIA) PVT LTD.	25	AHMEDABAD	AWH-77965	YES
26	EURECAT INDIA CATALYST PVT. LTD.	25	JHAGADIA	AWH-55123	YES
27	PAYAL POLYPLAST PVT. LTD.	1224	DAHEJ	AWH-52435	YES
28	TRANSPEK SILOX INDUSTRY PVT. LTD.	1834	VADODARA	AWH-55938	YES
29	PREM INDUSTRY	25	AHMEDABAD	AWH-51688	YES
30	MEGHMANI ORGANIC LTD. UNIT-3	1000	DAHEJ	AWH-40978	YES
31	OIL AND NATURAL GAS CORPORATION LTD. (ONGC) - AHMEDABAD	500	AHMEDABAD	AWH-67587	YES
32	SURVIVAL TECHNOLOGIES PVT. LTD. - UNIT-1	6	ANKLISHWAR	AWH-44075	YES
33	SYNBIOTICS LTD.	75	VADODARA	AWH-66678	YES
34	ALOK INDUSTRIES LTD.	25	VAPI	AWH-55204	YES
35	STANDARD PESTICIDES PVT. LTD.	10	VADODARA	AWH-70858	YES
36	MACLEODS PHARMACEUTICALS LTD.	500	VALSAD	AWH-87207	YES
37	MUNDRA SOLAR PV LIMITED	1580	KUTCH	AWH-22608	YES
38	PHILODEN INDUSTRIES PVT. LTD.	25	VADODARA	AWH-68031	YES
39	LONSEN KIRI CHEMICAL INDUSTRY LTD.	3600	VADODARA	AWH-33583	YES
40	BAKUL PHARMA PVT. LTD.	150	ANKLISHWAR	AWH-69872	YES

H. W. Storage Area detail

Sr. No.	Storage area	Tag No.	Nos.	Size
1	Sludge Drying Beds	EQ A-D	4	4.0m x 4.0m – Each
2	Hazardous Waste Storage Room - RCC	T-26	1	15m x 11m x 3m Ht.
3	Sludge Drying Beds For STP		2	2.6 m x 2.6 m + 0.3 m Sludge Application



N 29.170
 N 29.150
 N 29.130
 N 29.110
 N 29.090
 N 29.070
 N 29.050
 N 29.030
 N 29.010

E 17.200
 E 17.300
 E 17.400
 E 17.500
 E 17.600
 E 17.700
 E 17.800
 E 17.900
 E 18.000
 E 18.100

GSPL PIPE LINE (20 MT)

30 MT. WIDE ROAD

LEGEND

ROAD
 PIPE LINE
 BUILDING
 TANK
 UTILITY LINE
 FENCE
 DRIVE

NOTES

1. ALL DIMENSIONS ARE IN METERS.
 2. THE SITE IS TO BE DEVELOPED IN ACCORDANCE WITH THE REQUIREMENTS OF THE LOCAL AUTHORITY.
 3. THE PROPOSED DEVELOPMENT IS SUBJECT TO THE APPROVAL OF THE LOCAL AUTHORITY.
 4. THE SITE IS TO BE DEVELOPED IN ACCORDANCE WITH THE REQUIREMENTS OF THE LOCAL AUTHORITY.

SCALE

1:1000

DATE

1/1/2024

DRAWN BY

J. J. J.

CHECKED BY

K. K. K.

APPROVED BY

L. L. L.


PROJECT NO.

123456

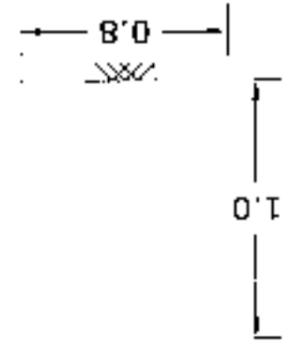
SHEET NO.

1 OF 1

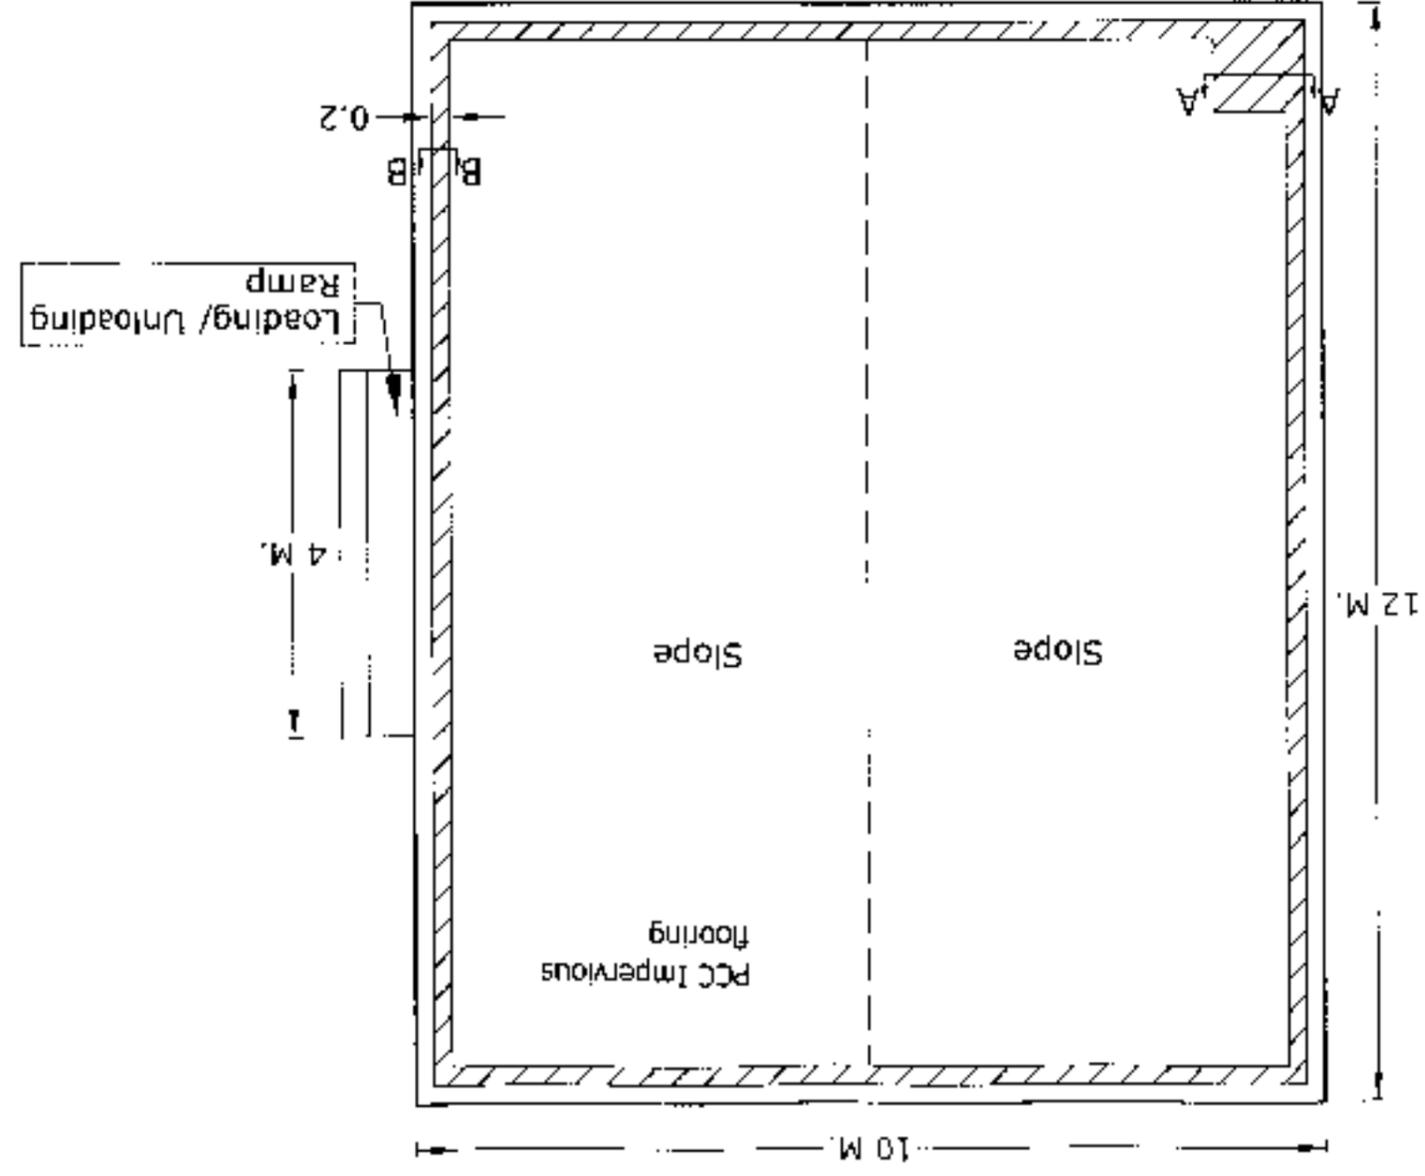
Section B-B



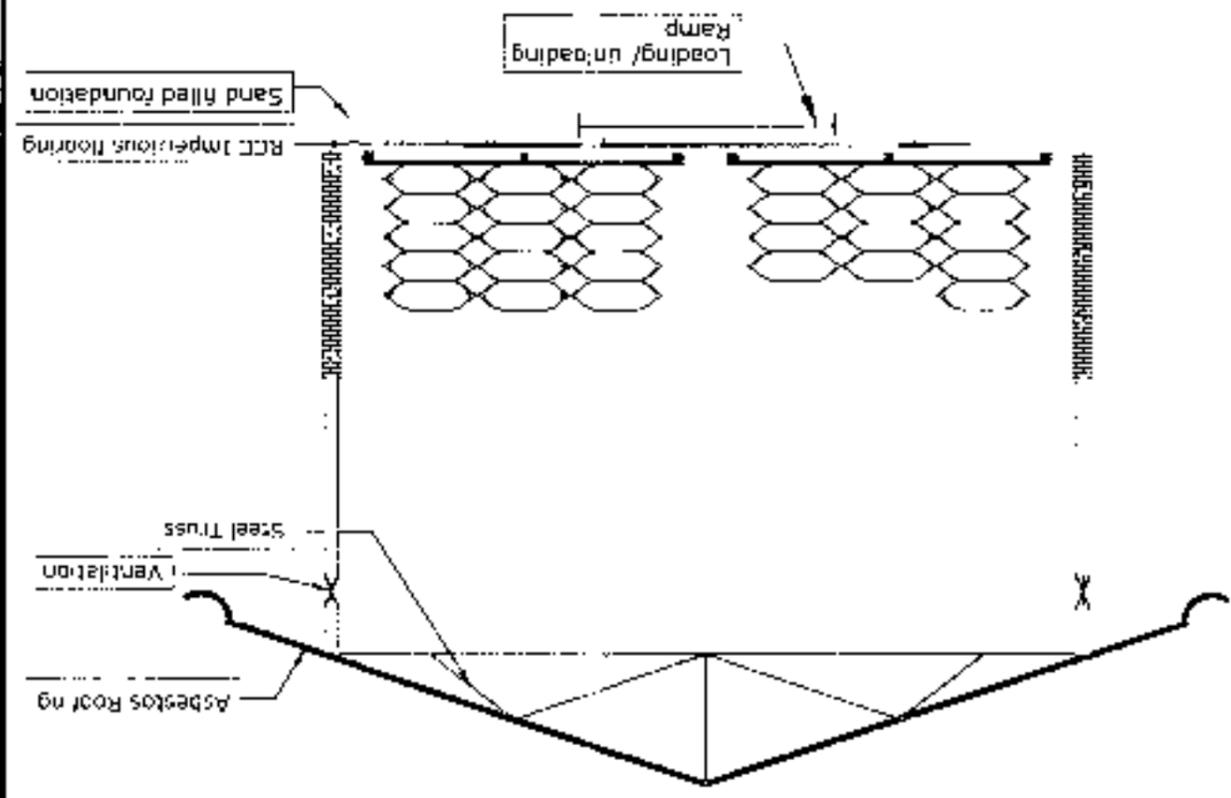
Section A-A



PLAN



ELEVATION





HAZARDOUS
SOLID WASTE
AREA
ETP WASTE
CMT NO. 243



ANNEXURE 19

BEIL INFRASTRUCTURE LTD.

Plot no.: D-43, GIDC Estate, Dahej.
2019-2020

TRAINING CALENDAR FOR THE YEAR 2019-2020

Day	Date	October-19	Day	Date	November-19	Day	Date	December-19
Tue	1		Fri	1		Sun	1	SUNDAY
Wen	2	Operation of fire hydrant system	Sat	2		Mon	2	
Thu	3		Sun	6		Tue	3	
Fri	4		Mon	4		Wen	4	Electrical Safety
Sat	5		Tue	5		Thu	5	
Sun	6	SUNDAY	Wen	6	Work permit (Class-D)	Fri	6	
Mon	7		Thu	7		Sat	7	
Tue	8		Fri	8		Sun	8	SUNDAY
Wen	9	Work permit (Class-A)	Sat	9		Mon	9	
Thu	10		Sun	6		Tue	10	
Fri	11		Mon	11		Wen	11	Use of PPE's
Sat	12		Tue	12		Thu	12	
Sun	13	SUNDAY	Wen	13	Work permit (Class-E)	Fri	13	
Mon	14		Thu	14		Sat	14	
Tue	15		Fri	15		Sun	15	SUNDAY
Wen	16	Work permit (Class-B)	Sat	16		Mon	16	
Thu	17		Sun	6		Tue	17	
Fri	18		Mon	18		Wen	18	Safety Induction
Sat	19		Tue	19		Thu	19	
Sun	20	SUNDAY	Wed	20	Use of Fire extinguisher	Fri	20	
Mon	21		Thu	21		Sat	21	
Tue	22		Fri	22		Sun	22	SUNDAY
Wen	23	Safety Induction	Sat	23		Mon	23	
Thu	24		Sun	24		Tue	24	
Fri	25		Mon	25		Wed	25	Use of Fire extinguisher
Sat	26		Tue	26		Thu	26	
Sun	27	SUNDAY	Wed	27	Use of PPE's	Fri	27	
Mon	28		Thu	28		Sat	28	
Tue	29		Fri	29		Sun	29	SUNDAY
Wen	30	Work permit (Class-C)	Sat	30		Mon	30	
Thu	31					Tue	31	

Prepared By.:

Parth Jani

BEIL INFRASTRUCTURE LTD.

Plot no.: D-43, GIDC Estate, Dahej.

TRAINING CALENDAR FOR THE YEAR 2020

Day	Date	January-20	Day	Date	February-20	Day	Date	March-20
Wen	1		Sat	1		Sun	1	
Thu	2	Awareness of safety	Sun	2		Mon	2	
Fri	3		Mon	6		Tue	3	
Sat	4		Tue	4		Wen	4	
Sun	5		Wen	5	Awareness of safety	Thu	5	
Mon	6		Thu	6		Fri	6	
Tue	7		Fri	7		Sat	7	
Wen	8		Sat	8		Sun	8	
Thu	9		Sun	9		Mon	9	
Fri	10		Mon	6		Tue	10	
Sat	11		Tue	11		Wen	11	
Sun	12		Wen	12		Thu	12	
Mon	13		Thu	13		Fri	13	
Tue	14		Fri	14		Sat	14	
Wen	15		Sat	15	Material handling	Sun	15	
Thu	16	Work permit system	Sun	16		Mon	16	
Fri	17		Mon	6		Tue	17	Corona Virus Awareness
Sat	18		Tue	18	USE of PPE's	Wen	18	
Sun	19		Wen	19		Thu	19	
Mon	20		Thu	20		Fri	20	Corona Virus Awareness
Tue	21		Fri	21		Sat	21	
Wen	22		Sat	22		Sun	22	
Thu	23	Safety in work at Height	Sun	23		Mon	23	
Fri	24		Mon	6		Tue	24	
Sat	25		Tue	25		Wed	25	
Sun	26		Wed	26		Thu	26	
Mon	27		Thu	27		Fri	27	
Tue	28		Fri	28		Sat	28	
Wed	29					Sun	29	
Thu	30					Mon	30	
Fri	31					Tue	31	

Prepared By.:

Parth Jani

BEIL INFRASTRUCTURE LTD.

Plot no.: D-43, GIDC Estate, Dahej.

TRAINING CALENDAR FOR THE YEAR 2020

Day	Date	April-20	Day	Date	May-20	Day	Date	June-20
Wen	1	Corona Virus Awareness	Fri	1		Mon	1	
Thu	2		Sat	2		Tue	2	
Fri	3		Sun	3		Wen	3	
Sat	4		Mon	4		Thu	4	Safety in material handling
Sun	5		Tue	5		Fri	5	
Mon	6		Wen	6		Sat	6	
Tue	7		Thu	7	General Safety Awareness	Sun	7	
Wen	8		Fri	8		Mon	8	
Thu	9		Sat	9		Tue	9	
Fri	10		Sun	10		Wen	10	
Sat	11		Mon	11		Thu	11	Safety In Welding Machine
Sun	12		Tue	12		Fri	12	
Mon	13		Wen	13		Sat	13	
Tue	14	General Safety Awareness	Thu	14	On site Emergency plan	Sun	14	
Wen	15		Fri	15		Mon	15	
Thu	16		Sat	16		Tue	16	
Fri	17		Sun	17		Wen	17	
Sat	18		Mon	18		Thu	18	Safety in Work at Height
Sun	19		Tue	19		Fri	19	
Mon	20		Wen	20		Sat	20	
Tue	21		Thu	21		Sun	21	
Wen	22		Fri	22		Mon	22	
Thu	23		Sat	23	Behavior Safety	Tue	23	
Fri	24		Sun	24		Wed	24	
Sat	25		Mon	25		Thu	25	Safety in Excavation work
Sun	26		Tue	26		Fri	26	
Mon	27		Wen	27		Sat	27	
Tue	28	USE of PPE's	Thu	28		Sun	28	
Wen	29		Fri	29		Mon	29	
Thu	30		Sat	30		Tue	30	
			Sun	31				

Prepared By.:

Parth Jani

BEIL INFRASTRUCTURE LTD.

Plot no.: D-43, GIDC Estate, Dahej.

TRAINING CALENDAR FOR THE YEAR 2020

Day	Date	July-20	Day	Date	August-20	Day	Date	September-20
Wen	1		Sat	1		Tue	1	
Thu	2	Operation of fire hydrant system	Sun	2		Wen	2	
Fri	3		Mon	6		Thu	3	Operation of fire hydrant system
Sat	4		Tue	4		Fri	4	
Sun	5		Wen	5		Sat	5	
Mon	6		Thu	6	Electrical Safety	Sun	6	
Tue	7		Fri	7		Mon	7	
Wen	8		Sat	8		Tue	8	
Thu	9	Electrical Safety	Sun	9		Wen	9	
Fri	10		Mon	6		Thu	10	Safety of gas cylinder
Sat	11		Tue	11		Fri	11	
Sun	12		Wen	12		Sat	12	
Mon	13		Thu	13	Use of PPE's	Sun	13	
Tue	14		Fri	14		Mon	14	
Wen	15		Sat	15		Tue	15	
Thu	16	Safety Induction	Sun	16		Wen	16	
Fri	17		Mon	6		Thu	17	Material handling
Sat	18		Tue	18		Fri	18	
Sun	19		Wed	19		Sat	19	
Mon	20		Thu	20	Use of Fire extinguisher	Sun	20	
Tue	21		Fri	21		Mon	21	
Wen	22		Sat	22		Tue	22	
Thu	23	General Safety Awareness	Sun	23		Wed	23	
Fri	24		Mon	6		Thu	24	Safety Induction
Sat	25		Tue	25		Fri	25	
Sun	26		Wed	26		Sat	26	
Mon	27		Thu	27	Electrical Safety	Sun	27	
Tue	28		Fri	28		Mon	28	
Wen	29		Sat	29		Tue	29	
Thu	30		Sun	30		Wed	30	
Fri	31		Mon	31				

BEIL INFRASTRUCTURE LTD.

Plot no.: D-43, GIDC Estate, Dahej.

TRAINING CALENDAR FOR THE YEAR 2020

Day	Date	October-20	Day	Date	November-20	Day	Date	December-20
Thu	1	Operation of fire hydrant system	Sun	1		Tue	1	SUNDAY
Fri	2		Mon	2		Wen	2	
Sat	3		Tue	3		Thu	3	Electrical Safety
Sun	4		Wen	4		Fri	4	
Mon	5		Thu	5	Work permit (Class-D)	Sat	5	
Tue	6		Fri	6		Sun	6	
Wen	7		Sat	7		Mon	7	
Thu	8	Work permit (Class-A)	Sun	8		Tue	8	
Fri	9		Mon	9		Wen	9	
Sat	10		Tue	10		Thu	10	Use of PPE's
Sun	11		Wen	11		Fri	11	
Mon	12		Thu	12	Work permit (Class-E)	Sat	12	
Tue	13		Fri	13		Sun	13	
Wen	14		Sat	14		Mon	14	
Thu	15	Work permit (Class-B)	Sun	15		Tue	15	
Fri	16		Mon	16		Wen	16	
Sat	17		Tue	17		Thu	17	Safety Induction
Sun	18		Wed	18		Fri	18	
Mon	19		Thu	19	Use of Fire extinguisher	Sat	19	
Tue	20		Fri	20		Sun	20	
Wen	21		Sat	21		Mon	21	
Thu	22	Safety Induction	Sun	22		Tue	22	
Fri	23		Mon	23		Wed	23	
Sat	24		Tue	24		Thu	24	Use of Fire extinguisher
Sun	25		Wed	25		Fri	25	
Mon	26		Thu	26	Use of PPE's	Sat	26	
Tue	27		Fri	27		Sun	27	
Wen	28		Sat	28		Mon	28	
Thu	29	Work permit (Class-C)	Sun	29		Tue	29	
Fri	30		Mon	30		Wed	30	
Sat	31					Thu	31	


TRAINING CALENDAR FOR THE YEAR 2021

SR.NO	SUBJECTS	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
1	Operation of fire hydrant System			•			•			•			•
2	Use of Fire Extinguisher		•			•			•			•	
3	Use of PPEs	•			•			•			•		
4	Safety Awareness			•			•			•			•
5	Material Handling		•			•			•			•	
6	Corona Virus	•			•			•			•		
7	Behaviour Safety			•			•			•			•
8	Height work permit		•			•			•			•	
9	Hot work Permit	•			•			•			•		
10	LOTO			•			•			•			•
11	Excavation Permit		•			•			•			•	
12	On site emergency plan	•			•			•			•		

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	22/10/2021
Time :	11:30 to 16:15
Venue :	FIND Pump house.
Topic :	operation of fire Hydrant system
Reference :	Parth jawi

Sr. No.	Name of Participants	Dept.	Sign.
1	Hanakesh Shah		
2	ashish Kumar		
3	Ravindra		
4	Arjun Patel		31-03
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.- DAHEJ
Training Attendance Sheet

F/HRD/002



Date : 19/10/2020

Time : 10:00

Subject : Safety induction Training

Venue : AHC

Faculty : Ms. Pooja Jyoti

Sr. No.	Name	Dept.	Signature
1	Raj Rizwan	Process	
2	Mansuri Dazuk	Process	
3	Chirag Parmar	11	
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	19-11-20
Time :	15:30 to 16:15
Venue :	Near Pump house.
Topic :	USE OF fire extinguisher
Reference :	Parth Jani

Sr. No.	Name of Participants	Dept.	Sign
1	Valsamit Rajan		वसंत
2	Paradishi		पारदेशी
3	Navin Valsava		नवीन
4	Sachin Valsava		सचिन
5	Shilesh Valsava		शिलेश
6	Mosin Patel		मोसिन
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	26-11-2020
Time :	14:30 to 15:00
Venue :	MCC Plant.
Topic :	USE of PPE
Reference :	Parth jani

Sr. No.	Name of Participants	Dept.	Sign.
1	Sanjeet		Sanjeet
2	Parmed		Parmed
3	Shiv Bahadur		Shiv
4	Amit Kumar		Amit
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

**BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.**

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET









Date :	28/12/2020
Time :	2:25 to 3:15
Venue :	PCC. off dt Plant
Topic :	Electrical safety
Reference :	For the time

Sr. No.	Name of Participants	Dept.	Sign.
1	bhuvya (eng)	Ro plant.	Bhuvya
2	myburaj (eng)	mee	Myburaj
3	mustekim (eng)	mee	Mustekim
4	Sufiyun (op)	mee/SPD	Sufiyun
5	Indran Singh (helper)	mee/SPD	Indran
6	Khumam Singh (helper)	mee/SPD	Khumam
7	Arvind (helper)	mee/SPD	Arvind
8	Solamjay Altomash	Boiler	Solamjay
9	Surpur (chil)	Boiler	Surpur
10	Chetan bhai	ment.	Chetan
11	Indran vafidam	ment.	Indran
12	Subham	ment.	Subham
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	20/12/2020
Time :	11:00 to 11:45
Venue :	Hitech contract
Topic :	Safety Induction
Reference :	Perth Jone

Sr. No.	Name of Participants	Dept.	Sign.
1	Bhrijesh	Hitech	
2	Katpes Kalash	"	
3	Som Lal	"	
4	Videshi	"	
5	Sarvam	"	
6	Manish	"	
7	Samto Sh	"	
8	Ashoka	"	
9	Sonu	"	
10	Rajesh	"	
11	Bipin	"	
12	Jitendra	"	
13	Sarvam	"	
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

**BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.**

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	12/07/2021
Time :	11:30 to 12:15
Venue :	Bhavanani
Topic :	Hot Work Permitt
Reference :	Permit Time

Sr. No.	Name of Participants	Dept.	Sign.
1	सुरेश कुमार	Bhavanani	सुरेश कुमार
2	सनीष कुमार	"	सनीष कुमार
3	वीनेश कुमार	"	वीनेश कुमार
4	सरवण कुमार	"	Sharwan Kumar
5	सोहन	"	सोहन
6	किंदेश कुमार	"	किंदेश कुमार
7	मनीष	"	मनीष कुमार
8	वीनेश कुमार	"	वीनेश कुमार
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	23-01-21
Time :	10:45 to 11:15
Venue :	Near Plant Area.
Topic :	one side emergency Plant
Reference :	Parth Jawi

Sr. No.	Name of Participants	Dept.	Sign.
1	Kashi Parm		काशी पारम
2	Paashumt		पार्शुमंत
3	Shushumt		शुशुमंत
4	Motilal		मोतीलाल
5	Mohit Parm		मोहित पारम
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.- DAHEJ
Attendance Sheet

F/HRD/002







Date : 27/02/2021

Time : 10:20 to 11:40

Subject : Excavation & civil work in safety.

Venue : Near PCC Room

Faculty : Ms. Pooja Jemi

Sr. No.	Name	Dept.	Signature
1	Vishnu Vadhavi	Sugar Constuction	
2	memhan bhui	"	
3	Punika bhui	"	
4	Umeshbhui bhui	"	
5	Sureshbhai bhui	"	
6	Rupasingha bhui	"	
7	Tedubhai	"	
8	manish bhui	"	
9	Kavita	"	KAVITA
10	Satish bhui	" (sup.)	Zensoo
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	12-02-2021
Time :	14:00 to 14:25
Venue :	Project area
Topic :	Excavation Permit
Reference :	Sanjay Jashi

Sr. No.	Name of Participants	Dept.	Sign.
1	Rakesh Kumar		Rakesh
2	Nagendra Yadav		Nagendra
3	Nishala Ahmad		Nishala
4	Ashish		Ashish
5	Vasudev		Vasudev
6	Jay Shankar		Jay Shankar
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	12.03-21
Time :	11:00 - 11:30
Venue :	Pump house
Topic :	operation of fire Hydrant system
Reference :	Shubham Shah.

Sr. No.	Name of Participants	Dept.	Sign.
1	Nirav Bharti	Inst.	B. Bharti
2	Prakash Patil	mech.	Patil
3	Siddhik Desai	Inst.	Desai
4	mohsin patel	Elec.	mpatel
5	Suresh charan	Elec.	charan.
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

BEIL INFRASTRUCTURE LTD.
Plot No 43, GIDC, Dahej-392130.

INTERNAL/EXTERNAL/INDUCTION TRAINING ATTENDANCE SHEET

Date :	17-03-21
Time :	15:45 to 16:15
Venue :	Mce Panel Room.
Topic :	Loto
Reference :	Mehul Prajapati

Sr. No.	Name of Participants	Dept.	Sign.
1	PRATIK OSHA		Pratik
2	Mehul Prajapati		Mehul
3	Suydar Chikar		Suydar
4	S		
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
23			
24			

ANNEXURE 20

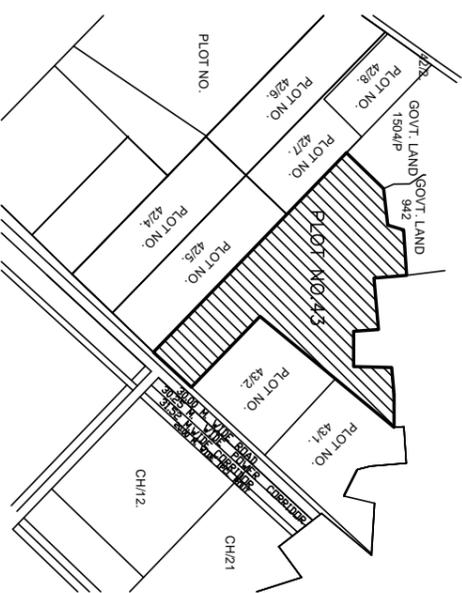


BLDG. NAME

1. SECURITY CABIN
2. ADM BUILDING & LAB
3. MCC/PC & DG ROOM
4. WEIGH BRIDGE
5. FRESH WATER TANK
6. STORAGE SHED
7. DIAPPER TYER WASHING
8. U/G WATER TANK
9. EFFLUENT TANK
10. TANKER DE-CONTAMINATION SHED
11. DRUM DE-CONTAMINATION & DRUM STACKING PLATFORM & ETP TANK & TANK FARM
12. FIRE WATER TANK
- 12/A FIRE WATER TANK
13. H.E. ROOM + D.G.SET
14. CONDENSATE WATER TANK
15. AQUIOUS WASTE STORAGE TANK
16. CENTRIFUGE SHED
17. MEE PLANT
18. COOLING TOWER
19. BOILER SHED & F.O. TANK
20. CANTENEN
21. ELE. ROOM
22. ELE. ROOM
23. SPRAY DRYING PLANT
24. DM TANK
25. TOILET BLOCK
26. ELE.-CONTROL ROOM
27. STRIPPER PLANT

NOTE: PREVIOUSLY PLAN APPROVED BY DJRIS & HF SURAT REGION WIDE LETTER NO. **1637** DATE: 01/04/2016

KEY PLAN
SCALE:-1:CM=40MT.



SITE PLAN
SCALE:-1:10MT.



EXTENSION PLAN SHOWING FACTORY BLDG. WITH M/C LAY OUT
BHARUCH ENVIRO INFRASTRUCTURE LTD.
PLOT NO : 43
G.I.D.C., DAHEJ
TAL.: VAGRA
DIST : BHARUCH.
SIGN OF OWNER

COLOUR CODE

1. PLOT BOUNDARY IS SHOWN	[Red Line]
2. EXTENSION AREA IS SHOWN	[Blue Line]
3. APPROVED AREA IS SHOWN	[Green Line]
4. FIRE HYDRANT LINE IS SHOWN	[Brown Line]

TITLE : SITE PLAN & KEY PLAN

SCALE	DATE	DESIGNED BY	DRG. NO.
1:100	07/03/17	KENYAKARIA	1/3
		M.983447343	
		95588-31856	

Tree Plantation Photographs







Photographs of Drip Irrigation



ANNEXURE 21

દહેજ ગામ પંચાયત

મુ.પો. દહેજ, તા. વાગરા, જી. ભરૂચ.



DAHEJ GAM PANCHAYAT

AT. & Po. DAHEJ, TA. VAGRA, DIST. BHARUCH.

CP-3-18

તા. ૬ - ૬ - ૨૦૧૬

પ્રતિ શ્રી,

મેનેજર સ્ત્રી
ભરૂચ એલાયસ ઈન્ડસ્ટ્રીઅલ લિમિટેડ
પ્લોટ નંબર ૩૧, ૪૩
દહેજ

વિષય - મોજે દહેજ ઈન્ડસ્ટ્રીઅલ એરેટ સ્થાન નંબર
૧૧ વિસ્તારે માં લૂકાચોપણનું આયોજન આપવા
બાબત.

રેફરન્સ - આપનો તા. ૩૧/૧૨/૧૬ નો પત્ર.
અમારી ગામ પંચાયતે સામુહિક રીતે વલેના પાંચ(૫)
વર્ષમાં આપની કંપની પકડી અને ગામ પંચાયત પકી નીચે
મુજબનું આયોજન કરેલ છે.

- (૧) બાલીયાદેવ મંદિર તથા ભાઈપુ મુખ્ય મંદિર વર્ષ ૨૦૧૬-૧૭
- (૨) ભુવનરાય ટેમ્પલ વર્ષ ૨૦૧૬-૨૦૨૦
- (૩) હોડા પુર્ણમ્ફુલ વર્ષ ૨૦૨૦-૨૦૨૧
- (૪) દહેજ ચોકડી સ્ત્રી ગામ મુદ્દી વર્ષ ૨૦૨૧-૨૦૨૨
- (૫) રામપુ મંદિર વર્ષ ૨૦૨૨-૨૩

લૂકાચોપણ માટે જરૂરી છોડ તથા છોડના અણા માટે સ્ત્રી
પ્રોટેક્ટર કંપની દવાલા પુરા પાડવાના રહેશે.
આભાર મણુ.

જાણપતિ આર. રહા
સુરપંચ
ગામ પંચાયત - દહેજ
તા. વાગરા, જી. ભરૂચ





DGVCL

DAKSHIN GUJARAT VIJ COMPANY LIMITED



DGVCL DAHEJ SUB DIVISION OFFICE

66KV DAHEJ SS COMPOUND, DAHEJ-AMOD CHOWKDI, PORT ROAD, DAHEJ-392130 PH.NO.02641-256123, 8758338214

DHJ/TECH/ 2454

Date:- 20/09/2018

No. Dahej/O&M/Estt/Tech/Billing/24/18

Dakshin Gujarat Vij Co. Ltd.

O & M Sub. Division, Dahej.

Appreciation Letter

To,

M/s. Bharuch Enviro Infrastructure Ltd.,

P.No. D-43, GIDC Estate,

Dahej Ta. Vagra, Dist. Bharuch.

Sub.:-Appreciation Regarding Tree plantation at DGVCL, Dahej sdn office.

With reference to the above subject M/s. Bharuch Enviro Infrastructure Ltd. had arranged tree plantation program on dated:21.08.18 as per this office request in our office premises. We are very thankful of M/s. Bharuch Enviro Infrastructure Ltd. for this noble "Save Environment" activity.

Thanking you.

Deputy Engineer (O&M)
Dahej S/Dn,
DGVCL



વાવ ગામ પંચાયત

મુ.પો. વાવ. તા. વાગરા. જી. ભરૂચ.

ક્રમાંક :

જવક નં.

CP-117

તા. - - - ૨૦૧૧

પતિ શ્રી,

શ્રી મેનેજર અફિસ

C S R યુ.પી એલ લીમિટેડ

આપી અમે આપનો આભાર વ્યક્ત કરતા આનંદ અને ગૌરવની લાગણીઓ અનુભવીએ છીએ કે યુ.પી.એલ કંપની દ્વારા. અમારા ગામની આવેલી ગાંધી કમીનમાં C એકર પહોંચીકરણની કામગીરી કરેલ છે.

જે યુ.પી.એલ કંપની અને BEAL દ્વારા કચ્છમાં આવેલ પહોંચીકરણની તકિદમાં પહોંચીકરણ અને લોકોની સુવિધાઓમાં એકમ તેજા આરા પરીણામ આવશે એવું અમારું માનવું છે. આવી જ રીતે અમારા ગામના અન્ય લોકોની સુવિધાઓમાં કામ કરતા રહો એવી અમે તમારીપાસે અપેક્ષા રાખીએ છીએ. અને અમે તમારો અમારા ગામ તથા ગ્રામ પંચાયત તરફથી તમારો હૃદયપૂર્વક આભાર માનીએ છીએ. કચ્છ હીંદ કચ્છભારત.

મુરખંચ

ગામ પંચાયત - વાવ
તા. વાગરા, જી. ભરૂચ

ડાક્ટર મુખર્જીભાઈભાઈ



નાંદરખા ગામ પંચાયત

મુ.પો. નાંદરખા. તા. વાગરા. જી. ભરૂચ.

ક્રમાંક :

જાવક નં.



CP-1-16


તા. 03 - 06 - 2016


પ્રતિ શ્રી,

રિપોર્ટ

ગ્રામ પંચાયત નાંદરખા
તા- વાગરા, જિ- ભરૂચ

વિષય:- પુસ્તક સંગ્રહણા બધી સ્થાપના બાબત.
અધિકાર સહ ઉપગ્રાહક વિસ્તરણા સ્થળનાંદાને
લગ્ની જમાવણાં ત્રી મોર્ક ગામ નાંદરખા તા- વાગરાના
ગામે પુસ્તકો લાવેલ છે. લેખક આર્થુ વર્લ હરચાવ રિખલ
પુસ્તકોંગ વાગેતર સંપાદનું થાય છે. તો સભાની આમ પંચાયતને
પુસ્તક સંગ્રહણા બધી જાવના. સ્થાપના સ્થાપ સાર્થકા સ્ત્રી ને
સભાની ગમ્ભીરી સ્થાપ છે.


સચીવ કમ મેંત્રી
ગામ પંચાયત - નાંદરખા
તા. વાગરા, જી. ભરૂચ


સરપંચ
ગામ પંચાયત-નાંદરખા
તા. વાગરા, જી. ભરૂચ



BHARUCH ENVIRO INFRASTRUCTURE LTD.

Pad Copy

Plot No - 43, G.I.D.C Dahej - 392 130

CHALLAN CUM GATE PASS

Phone : 02641-291129

(NON - RETURNABLE)

NO. 0228

M/s. Nandeshka Gram Panchayat

Date : 03/08/2019

Village - Nandeshka

Carrier: GJ 26 W 7283

Tp - Vagra

L.R.No.: _____

Dij - Bharuch

Date : 03/08/2019

Sr. No.	Item Description	Quantity	Purpose
1	Tree Guard (CSR activity)	40 NOS	Loan Sample Party Goods Empty Carbo Drums/Cylinders Others

for Tree Plantation at Village Nandeshka Tc. Vagra
logged in padyantrigal CSR
village meeting for idea

Prepared by G. P. Requested by <u>[Signature]</u>	Authorised by <u>[Signature]</u> Rajesh Mishra	Security Dept.	1 Please return duplicate copy while receiving materials.
		Out <u>16 white</u>	
Dept. <u>CSR</u>	Permitted by	In	Received the items stated above in good condition and as per quantity
	Checked by <u>[Signature]</u>		Receiver's Signature with Stamp



ગાંધારાત

ગામ પંચાયત કડોદરા

મુ.પો. કડોદરા, તા. વાગરા, જી. ભરૂચ.

સરપંચ : અરવિંદભાઈ સી. પરમાર M. 9998821712

ક્રમાંક :

જા.નંબર :

દાખલો

તા. ૨૬ - ૧૦ - ૨૦૨૦

પ્રતિ શ્રી,

BEZL Infrastructure Ltd.
Dahel.

૧) જ્યે ભારત સર સ્થાપવાનું કે કડોદરા તા. વાગરા, જી. ભરૂચ ના ગામે સ્થાપણી કેપની બાઈ સ્કાઈ સેલિ દુકેલ રૂઝા પુસ્તો બચાવવા આદે ના પિકરા - સ્કાપેલ છે જે બદલ સ્થાપણી પંચાયત સ્થાપણ વાકુલ કરી છે વધુનો ફૂરીયા કોઈ જુરીયાત ઉભી થાય ને આપ સમને સ્થાપણ ભલામણ કરીએ છીએ

" સેલકાર બદલ સ્થાપણ "

પરમાર અરવિંદ સી
સરપંચ
ગામ પંચાયત-કડોદરા
તા. વાગરા, જી. ભરૂચ

TREE PLANTATION AT COMPOST SITE IN DAHEJ



ANNEXURE 22



The Certification Body
of
Quality Circle Forum of India
Certifies that

BEIL Infrastructure Dahej, Gujarat

*has successfully implemented
FIVE-S Workplace Management System in all departments*

*An audit was performed and it was found that
all the requirements are fulfilled.*

This certificate is valid until 31.01.2023

*subject to the continued satisfactory implementation of
workplace management system for sustenance and
improvements with a check by Surveillance audit.*



Date: 25.01.2020

D.K.Srivastava
(Executive Director)

ANNEXURE 23



← Plant Area

Garland Drain

Storm Water Channel



Plant Area →



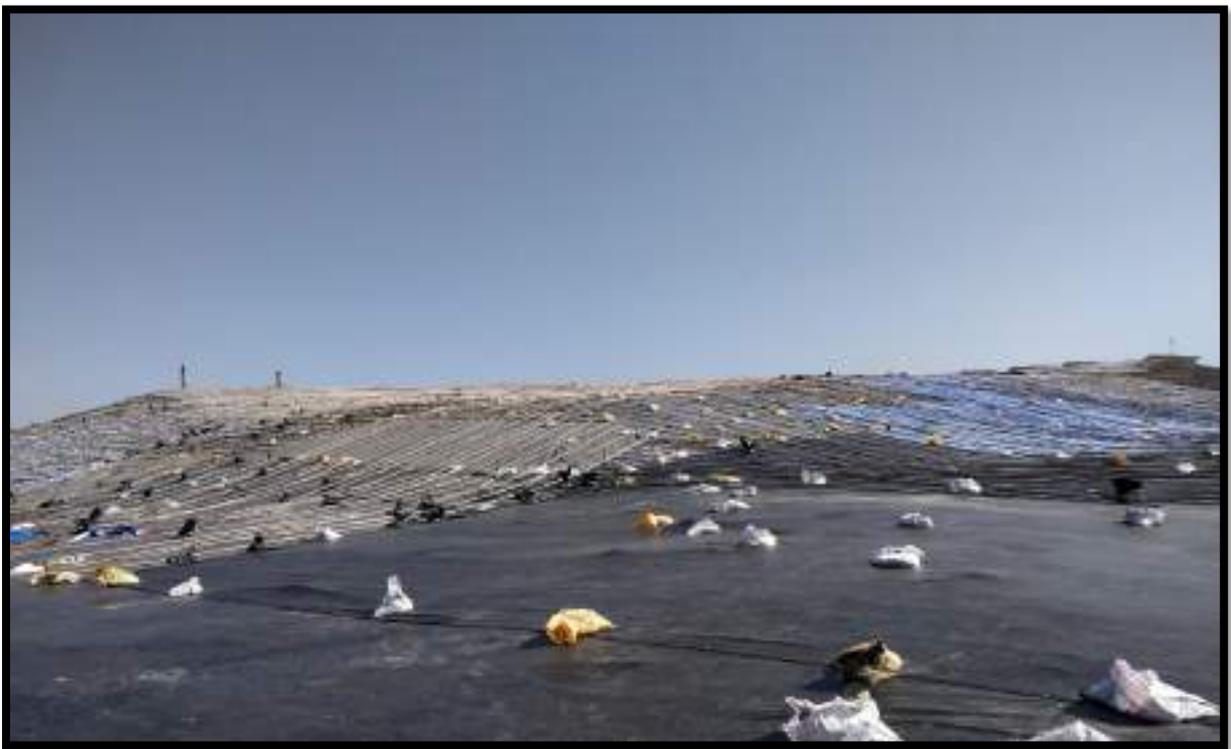
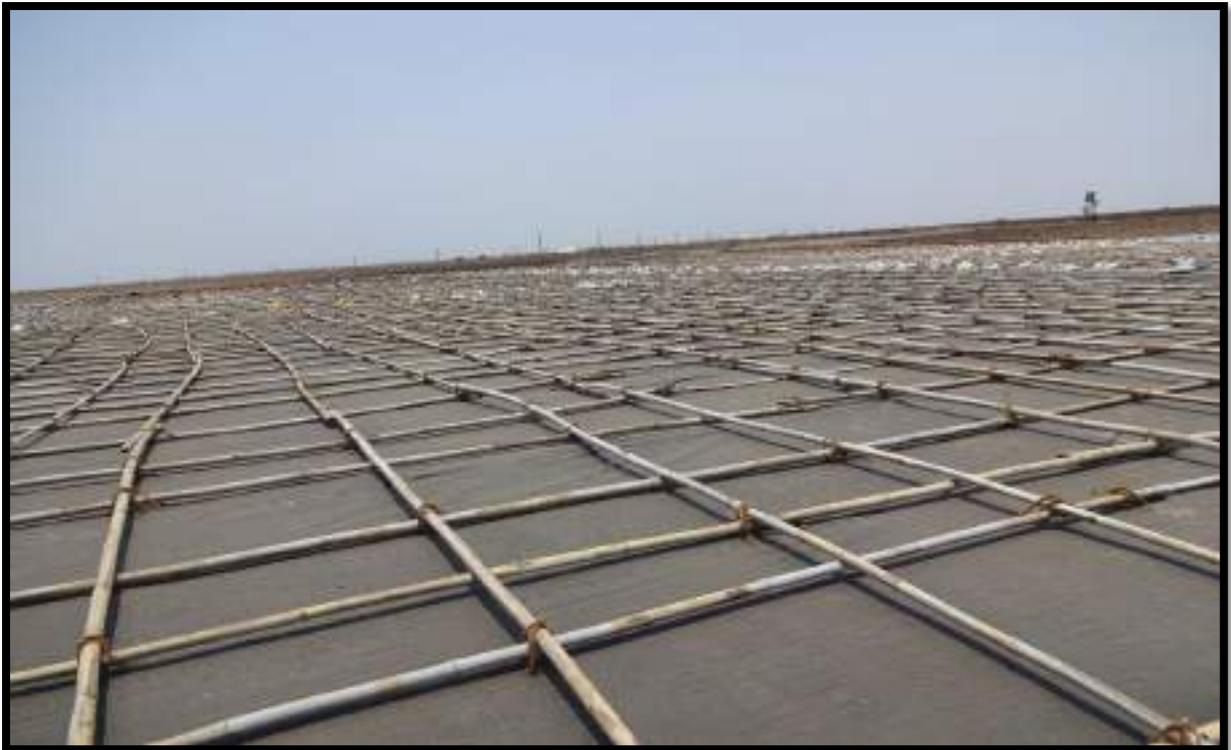
Effluent Collection Pit

Garland Drain





LANDFILL MONSOON COVER PHOTOGRAPHS




Sheet No. 01 of 01

LEACHATE COLLECTION SYSTEM

PROJECTS

CONSTRUCTION OF SECURED LANDFILL FACILITY



BHARUCH ENVIRO INFRASTRUCTURE LIMITED
PLOT NO. 41, SEC. DAMEJ

DESIGN & DRAWN BY



BHARUCH ENVIRO INFRASTRUCTURE LIMITED
PLOT NO. 41, SEC. DAMEJ



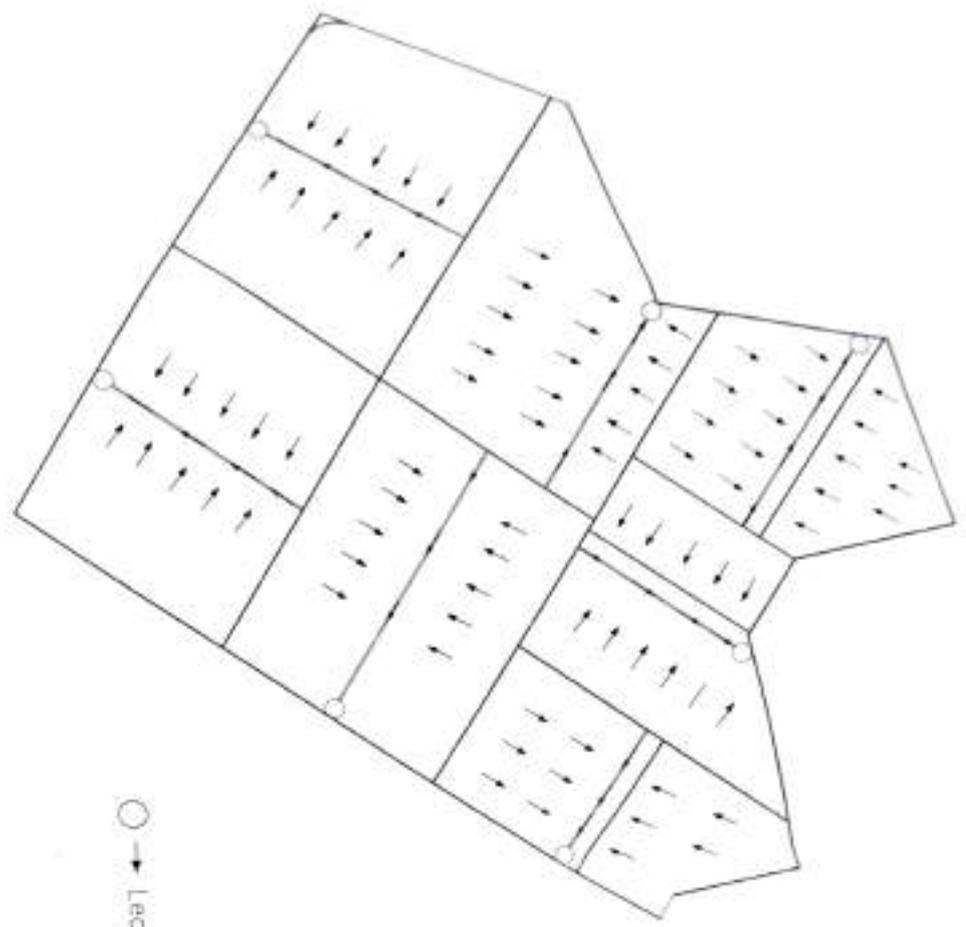
APPROVED BY

**INDIAN INSTITUTE OF TECHNOLOGY,
NEW DELHI**

[Signature]
26/09/13

Dr. Manoj Kumar
Professor
Civil Engineering Department
Indian Institute of Technology, Delhi
Hauz Khas, New Delhi - 110016

[Signature]



○ → Leachate Collection Wells

LEACHATE COLLECTION SYSTEM

DRG NO.	REV.	DATE
EEI-41-01		26.09.13

SCALE
N.T.S.

MT. DURGAMCHERU, HYDRABAD

ANNEXURE 24

**BEIL INFRA STRUCTURE LTD. – DAHEJ
PUBLIC HEARING COMPLIANCE REPORT**

The Public hearing was held on 5th April 2013 at P.J. Chheda Janta Vidyalay, Dahej, Taluka Vagra, Dist. Bharuch, Gujarat at 11:30 Hrs.

Sr. No.	Name and Address	Points represented and / or written submission	Compliance Status
1	Shri Raghuvirsinh Udaysinh Rana Village: Dahej, Taluka: Vagra, District: Bharuch	Whether GPCB is carrying out monitoring of the ambient air parameters SO _x , NO _x in Dahej Area?	Complied. The regional Officer of GPCB answered that GPCB will contact him for carrying out investigation of His complaint.
		He informed that we cannot sleep outside of our residence during night hrs. If door of house remains open, black layers get form on the utensil in morning due to Air pollution.	Complied. We are carrying out regular monitoring of ambient air & all the parameters are within the limit.
		What should be the minimum distance of the company site from village?	Complied. The minimum distance of site from village should be 0.5 Km as per guideline.
2	Shri Sureshbhai Sanabhai Village: Dahej, Taluka: Vagra,	He informed that development in Gujarat is at very fast and new industries are coming.	Noted.
		They give committeemen's during public hearings and they were given cooperation.	Noted.
		He requested industries to give employment to local people.	Complied. We have appointed 2 person as chemist and as electrician, as well as we are also sponsoring them for their skill development courses.
		He informed that they are not against the developments of industries.	Noted.
		He asked the industries representative what steps will be taken to give the employment.	Complied. We have appointed 2 person as chemist and as electrician, as well as

			we are also sponsoring them for their skill development courses.
		He further added that it should give in written by the industries.	Complied We have given employment to local people. We have appointed 2 person as chemist and as electrician, as well as we are also sponsoring them for their skill development courses.
3.	Shri Pradeep Thakar		As he is not in the definition of local people, he was advised to give his presentation or comment in writing which will be incorporated in minutes. He had not given any Written comment.
4.	Shri J. J. Rajput Member of Dahej Eco-Friendly Society, Village: Dahej, Taluka: Vagra, District: Bharuch	He asked the project proponent what the lesson they have learnt from Ankleshwar BEIL fire incident.	Complied. BEIL fire incident had occurred in 2008 in incinerable waste storage area. In this project we are not receiving any incinerable waste. Therefore there will not be possibility of fire incident. We are receiving the waste as per the acceptance criteria for disposal in TSDF site.
5.	Shri Yogesh Pandya Founder Trustee of Dahej Eco-Friendly Society, Village: Dahej, Taluka: Vagra, District: Bharuch	He informed that various problem are arising along with the development of the area.	Noted
		He added that in Gujarat solution of the problems also beings taken care therefore Gujarat develops at very fast. In connection with development of Dahej area they have develop Dahej Eco-friendly society which is also registered with government.	Noted
		He further insisted that work for the preservation of environment should be carried out site by site of development of Dahej area.	Complied. In Ankleshwar, We have HDPE single liner and here in Dahej we have double liner. We have developed a green belt (4550 Trees) along the periphery according to CPCB guidelines (Total 2, 85,343.76 sq. meters land area is available at site; out of this area about 50,500 (3300 m length * 15 m width) sq. meters (18.46 %) area is considered as greenbelt and other forms of greenery) to minimize fugitive emission. It is an ongoing activity, in this monsoon also we have planted 7532 trees to develop green belt. We have tied up with local Gram Panchayat for developing a garden in around 2200 Sq. meters.
		He further added that Dahej should not be developed like	Noted.

	Ankleshwar and Panoli GIDC.	
	He pointed out the complaints of local residence and asked the industries to take the necessary steps.	Noted.
	He added that this type of project is given subsidiary given by government under various provisions therefore people are accepting solution of their problems related to environment and other issues.	Noted.
	He said that in earlier days hazardous waste was disposed not properly which created heaps but now Gujarat is having maximum number of TSDFs, CETPs and Common Incinerators.	Noted.
	Gujarat is going toward the solution of the problems.	Noted.
	He further added that mistake made once should not be repeated again.	Noted.
	He had given incident of Vapi TSDF in which large amount of hazardous waste had washed out due to heavy rain in nearby area. In connection with the same he asked the project proponent what precaution will be taken in Dahej site?	Complied If the slope is not proper then water logging takes place. We have provided the proper slope and in monsoon, the site will be totally closed so no chance of any incidents.
	In connection with, sea is also nearby, salt pans are also nearby and site is also nearby CRZ limit. He further added that the soil of the area is also black cotton soil and water table is about 2.5 to 3 m depth, also area is having heavy rain as well as heavy wind velocity. What extra – ordinary precautions will be taken of above points?	Complied We have done analysis and survey report by government authority and report says it is 9.0 to 9.5 meter. Based on the report we have commissioned the site. We have excavated 1.8 meter black cotton soil until the yellow soil appears then TSDF commissioned.
	He informed that the site will be favorite for Dahej Eco- Friendly Society and Dahej Industrial association.	Noted
	Considering the transparency and faith representative of Dahej Eco-Friendly Society and Dahej Industrial association will be given chance to visit the construction phase of site development.	Complied We are allowing all the member of Dahej Eco-Friendly Society and Dahej Industrial Association for all activities take place in site, they don't need to take any permission.
	He further inquired that what will be disposal of condensate	Complied.

		of MEE and whether they are going to provide stripper in MEE.	MEE Plant of Capacity 200 KLD has been installed and commissioned in May, 2017. We have applied for the CC&A in May, 2017. Spray Dryer is provided and scrubber is attached.
		He advised that to think for high CV waste for co-processing in Cement Kilns.	Noted. At present it is TSDF only. It will be taken care if incinerator will come in future.
		In connection with that green belt, he advised the project proponent to develop 33% green belt in this site as well as in nearby area of Dahej.	Complied. We have developed a green belt (4550 Trees) along the periphery according to CPCB guidelines (Total 2, 85,343.76 sq. meters land area is available at site; out of this area about 50,500 (3300 m length * 15 m width) sq. meters area is considered as greenbelt and other forms of greenery). It is an ongoing activity, in this monsoon also we have planted 7532 trees to develop green belt. We have tied up with local Gram Panchayat for developing a garden in around 2200 Sq. meters. BEIL & UPL have planted the following 1800 nos near Kadodara 4000 nos in Vav village 2800 nos panyadara 2000 nos in Padariya We have also tied up with local gram panchayat and have prepared a five year plantation plan, wherein we will be providing trees and tree guards to the panchayat.
		In connection with Narmada Parikrama, he advised the industries to give necessary facilitation for this noble cause.	Complied.
		He informed that since 1995 various public hearing were conducted in this school premises but lot of work for the development of school is required to be done. He advised the project proponent to donate for school room as well as its compound wall.	Complied. We have donated Rs. 50000 to Shri P.J. Chheda Janta Vidhyalaya, Rs. 10000 to School Management Committee & Rs. 5000 to Archarya Prathmik Shala, Dahej
6	Shri Haniabhai President of Dahej Industrial Association, Village: Dahej, Taluka: Vagra, District: Bharuch	He said that Dahej Industrial estate is established in 1993. 20 years is passed for the growth.	Noted.
		He added that this project will to come before one year but due to some reason, project is	Complied We applied to GIDC for land on 06.04.2009 and got allotment &

		delayed. We welcomed the project.	possession on 28.09.2011 & 04.08.2011 subsequently. We have started the landfill site in April 2015 after getting all the required approvals.
		He further added that Dahej Eco-Friendly Society and Dahej Industrial Association will have environment cell. 77 industries is located in Dahej Industrial Estate. All members will work together and this project has to be completed at the earliest.	Complied We have started the landfill site in April 2015 and are become member of Dahej Eco-Friendly Society and Dahej Industrial Association.
		In connection with Narmada Parikrama, he advised the industries to give necessary facilitation for this noble cause. He added that Narmada Parikrama was started in 1993.	Complied.
		He asked that how fast the project will come and ask to give the completion date. Rate should competitive with other TSDFs.	Complied We have started the landfill site in April 2015
		He advised to project proponent the CETP should also come and start as you have experience of existing site.	Noted
		He also appreciated the cooperation of the surrounding villages' people.	Noted
7.	Mr. Sunil Jain Member of Dahej Eco- Friendly Society, Village: Dahej, Taluka: Vagra, District: Bharuch	What is the provision of rain water harvesting in premises?	Noted for compliance We will carry out rain water harvesting.
		What is planning or arrangement for parking the trucks-vehicles to carry the hazardous waste to project site?	Complied 1000 Sq. Mt. Parking area is provided for trucks-vehicles.
		What care is taken for the nearby existing water tanks due to transportation of vehicles?	Complied Hazardous waste is being transported in dedicated vehicles and it is completely covered. If any mishap will happen, we will collect the waste and then it will be disposed in TSDF.
8.	Shri Narendrasinh Rana Chairman of P J Chheda School & BJP Dahej Gram Panchayat, Village: Dahej, Taluka: Vagra, District: Bharuch	He said that company had given satisfied answer. They will fulfil their commitments. The development of high school should be taken care off by industries.	Complied We have donated Rs. 50000 to Shri P.J. Chheda Janta Vidhyalaya, Rs. 10000 to School Management Committee & Rs. 5000 to Archarya Prathmik Shala, Dahej
		He added that development of industries taken place without any unrest industries.	Complied. We, Dahej Industrial Association, Dahej Eco-Friendly Society and Villagers shall get together for all activities either technical or CSR.

		And all public hearing has been done here only and industrial growth without any accident with industries and villagers.	Noted
		He requested to industries that they should contribute in CSR activities as well as for education facility.	Complied We have donated Rs. 50000 to Shri P.J. Chheda Janta Vidhyalaya, Rs. 10000 to School Management Committee & Rs. 5000 to Archarya Prathmik Shala, Dahej. We are also contributing towards all CSR activities in Dahej Area.
9.	Shri Pradyumansinh Natvarsinh Rana Village: Dahej, Taluka: Vagra, istrict: Bharuch	He asked that who is the responsible to dispose the hazardous waste here and there by other industries.	Noted If any complaints registered, then necessary actions will be taken in consultation with Dahej Industrial Association and GPCB.

ANNEXURE 25

COMPOST SITE BUILT BY BEIL IN DAHEJ VILLAGE



Collection of Kitchen Waste (door to door)



Monthly average of daily collected kitchen waste comes between 100 to 150 KGs.



Kitchen waste segregation process in tumblers



Kitchen waste drying process in pits



Ready fertilizer for the use

ANNEXURE 26

Environment Clearance to BEIL-Dahej for installation of Two Incinerator and capacity enhancement of Landfill at Existing CHWTSDF

Sr. No.	Address	Sign
1.	The Sarpanch - Dahej	
1.1.	The sarpanch - vadia. }	
2.	The Sarpanch - Vav Thakorbhai M. No. 98793 86 326	સરપંચ શામલ પંચાલ - વાવ તા. વાવોરી, જિ. વડોદરા 19/01/19
3.	The Sarpanch - Vadadla શુભમી સરપંચ વાડાડા M. No. 9723 33 35 32	શ્રી. શુભમી સરપંચ 19/01/19
4.	The Sarpanch - Lakhigam	સરપંચ લાકિગમ 16/01/19
5.	The Sarpanch - Iolva Poojapati Jogalish. S.	જોગલિશ 9737457272 17/01/19
6.	The Sarpanch - Jageshwar	
7.	The Sarpanch - Rahiadi TCM	સરપંચ રાહિયાડી 17/01/19
8.	Mr. Yogesh P. Pandya Safety Health and Environment Association- Bharuch	17/01/19

Environment Clearance to BEL-Dahej for installation of Two incinerator and capacity enhancement of Landfill at Existing CHWTSDF

9.	Bharuch Nagar palika- Civil Road	<p>Despech Clerk Bharuch Nagarpalika Bharuch.</p> <p>17-1-19</p>
10.	Notified Area Office, Dahej	<p>DIA</p> <p>16/01/19</p> 
11.	Collector District Collector Office, Bharuch.	<p>19/01/19</p> <p>આવક કારકુન કલેક્ટર કચેરી</p>
12.	Dr. Naresh Ghadhvi- Dahej	<p>19/01/19</p> <p>આવક કારકુન કલેક્ટર કચેરી</p> <p>ISO 9001 : 2015 - CERTIFIED Dr. Naresh Ghadhvi M.B.B.S. A.F.I.H. Industrial Health Consultant Reg. No. G-2019-0116</p>
13.	The Sarpanch - Suraj Ganpatbhai M. NO. 9825021259	<p>19/01/19</p> <p>સરપંચ ગામ પંચાયત - સુરજ તા. વાવરા, જી. ભરૂચ</p>

14 The Sarpanch - Luvaka.

16/01/19

સરપંચ

ગામ પંચાયત - લુવાકા
તા. વાવરા, જી. ભરૂચ

15 The Sarpanch - Ambetha

16 The Sarpanch - Atali

સરપંચ



17/01/19

17 The Sarpanch - Bhesli
(P. J. Patel)

સરપંચ

ગામ પંચાયત - બેશ્લી
17/01/19

Environment Clearance to BEIL-Dahej for installation of Two Incinerator and capacity enhancement of Landfill at Existing CHWTSDF

Sr. No.	Address	Sign
18	The Sarpanch - Panyadara (Rajitkhai) M.No. 8128177527	 ગ્રામ પંચાયત-પણ્યાદરા તા.વાગરા, જી.વ.સુ. / 18/01/2019
19	The Sarpanch - Padaria (Ajitkhai Chandubhai Vasava) M No 9913694250	 ગ્રામ પંચાયત-પાદારીયા તા.વાગરા, જી.વ.સુ. / 18/01/2019
20	The Sarpanch - Kadodara (Akwindkhai) Rajitkhai Patras M No 9998821712 / 8141204301	 ગ્રામ પંચાયત-કાદોદરા તા.વાગરા, જી.વ.સુ. / 18/01/2019
	The Sarpanch -	18/01/2019
	The Sarpanch -	
	The Sarpanch -	

ANNEXURE 27

F. No. 10-43/2016-IA-III
Government of India
Ministry of Environment, Forest and Climate Change
(IA.III Section)

Indira Paryavaran Bhawan,
Jor Bagh Road, New Delhi - 3

Date: 19th December, 2018

To,

The Chief Executive Officer
M/S Bharuch Enviro Infrastructure Limited
Plot No. D-43, Dahej Industrial Estate,
Taluka Vagra, District Bharuch - 3921302 (Gujarat)
E-mail: dalwadibd@beil.co.in

Subject: Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility at existing Common Hazardous Waste Treatment, Storage and Disposal Facilities (TSDF) at plot number D-43, Dahej Industrial Estate, Taluka Vagra, District Bharuch by M/s Bharuch Enviro Infrastructure Limited - Environmental Clearance - reg.

Sir,

This has reference to your online proposal No. IA/GJ/MIS/55789/2016 dated 11th June, 2018, submitted to this Ministry for grant of Environmental Clearance (EC) in terms of the provisions of the Environment Impact Assessment (EIA) Notification, 2006 under the Environment (Protection) Act, 1986.

2. The proposal for grant of environmental clearance to the project 'Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility' at existing Common Hazardous Waste Treatment, Storage and Disposal Facilities (TSDF) at plot number D-43, Dahej Industrial Estate, Taluka Vagra, District Bharuch by M/s Bharuch Enviro Infrastructure Limited, was considered by the Expert Appraisal Committee (Infra-2) in its 32nd meeting held on 2-4 July, 2018 and 35th meeting held on 29-31 October, 2018. The details of the project, as per the documents submitted by the project proponent, and also as informed during the above meeting, are as under:-

- (i) M/s BEIL proposes to install two Incinerators and enhance the capacity of existing secured landfill facility (SLF) at Plot No. D-43, Dahej Industrial Estate, Taluka Vagra, Dist. Bharuch, Gujarat. Earlier the BEIL has obtained environment clearance for existing TSDF in July 2013 vide letter no. SEIAA/GUJ/EC/7(d)/227/2013. The proposed project is for Installation of two Incinerators I & II: having capacity of 12 Million Kcal/hour each and capacity enhancement of existing secured landfill facility from 14LMT to 19 LMT.
- (ii) The proposed project is Category "A "Common hazardous waste treatment, storage and disposal facilities (TSDFs) listed under activity 7 (d) as per EIA Notification dated 14th September 2006 as it is proposed to upgrade the facility integrated facilities having incineration & landfill.
- (iii) Due to growth of chemical industries in the Dahej industrial area, generation of hazardous waste Landfillable & incinerable waste has been increasing many folds. The existing secured landfill is likely to get exhausted much before planed period at the current rate of waste generation & disposal. Therefore, it is proposed to enhance the capacity of SLF from 14 lakhs MT to

19 lakhs MT and addition of two Incinerators. All the other facilities such as infrastructure, laboratory is already available at the existing site.

(iv) Details of existing and proposed facilities are as under:

Particulars	Existing	Proposed
Land area	2,85,343.76 m ²	Nil
Secured landfill capacity	14 LMT	19LMT
Incinerator	Nil	2 Nos.12 Million Kcal/hour each
Water consumption	466 KLD	900 KLD
Power	475 KVA	1920 KVA
D.G.	1 no. 600 KVA	2 nos. (600 KVA + 900 KVA) capacity
Employment	Employee- 23 Worker- 84	Construction phase 150 workman Operation phase: 60 workmen

- (v) Water consumption for the proposed project is 900 KLD and will be met from GIDC water supply.
- (vi) Leachate/effluent from landfill will be treated in Multiple Effect Evaporator (MEE) plant. The waste water from incinerator shall be used for quenching. Municipal spoil waste generated from the project shall be disposed as per MSW Rules, 2016.
- (vii) Hazardous solid waste generated as the residue from MEE after treatment of leachate and residue ash generated from incineration of hazardous waste shall be disposed in the landfill. Transportation of hazardous solid waste is done as per guidelines of CPCB. The TSDF have approved transporter authorization with dedicated vehicle (hydraulics) for transportation of wastes.
- (viii) The proposed project shall be an important endeavor to mitigate the degradation of environment in the region.
- (ix) ToR for the proposed project was approved by MoEF & CC on dated 26th October, 2016 vide Letter no F.No. -10-43/2016-IA-III.
- (x) Public Hearing was exempted vide amendment in ToR issued vide letter dated 14th May, 2018, as Dahej Industrial Estate of GIDC is a part of Development of Petroleum, Chemical and Petro-chemical Investment Region (PCPIR) Dahej, Dist. Bharuch. The PCPIR has already obtained Environmental Clearance on 17th September, 2017 vide letter 21-49/2010/-IA-III for the entire industrialized region. The Public hearing for the same was also conducted on 30th July, 2014.
- (xi) Investment/Cost of the project is approx. Rs. 64 Crore.
- (xii) Benefits of the project: There will be a positive environmental impact by collecting and disposing the hazardous waste in the scientific manner that will reduce the future health hazard. It is expected that additional people will get employment and hence job opportunities for the local people as well as migrants from nearby areas would increase.
- (xiii) Employment potential: About 150 persons (construction phase) & 60 persons (operational phase).

3. The project/activity is covered under category 'A' of item 7(d) Common hazardous waste Treatment, Storage and Disposal Facilities (TSDFs) of the

Schedule to the EIA Notification, 2006 and its subsequent amendments, and requires appraisal at Central Level.

4. The EAC, in its 35th meeting held on 29-31 October, 2018, deliberated on the proposal including certified compliance report letter No. 18-A-96/2013(Parya)/943 dated 28.08.2017 (inspection done on 06.06.2017) issued by the MoEF&CC's Regional Office (Western Region), Bhopal. The EAC, on being satisfied with the submissions of the project proponent, recommended the project for grant of environmental clearance to the project. As per recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the project 'Installation of Two Incinerators and Capacity Enhancement of Existing Landfill Facility at existing Common Hazardous Waste Treatment, Storage and Disposal Facilities (TSDF) at plot number D-43, Dahej Industrial Estate, Taluka Vagra, District Bharuch by M/s Bharuch Enviro Infrastructure Limited, under the provisions of the EIA Notification, 2006 and amendments/circulars issued thereon, and subject to the specific and general conditions as under:-

PART A – SPECIFIC CONDITIONS:

- (i) Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.
- (ii) The Project proponent should ensure that the TSDF fulfils all the provisions of Hazardous and other Wastes (Management and Transboundary Movement) Rules, 2016.
- (iii) Ground water abstraction shall be as prescribed by the CGWA. A clearance/permission of the CGWA shall be obtained in this regard.
- (iv) It shall be ensured that all the trees and other plantation are of the non edible varieties and do not in any way encourage the incorporation of toxic materials in the food chain.
- (v) The TSDF should only handle the waste generated from the member units.
- (vi) As proposed, air pollution control device viz. gas quencher; treatment with mixture of hydrated lime and activated powder for adsorption of partial acidity and VOCs (if any); bagfilter/ESP for removal of particulate matter; ventury scrubber followed by packed bed scrubber with caustic circulation to neutralize the acidic vapours in flue gas; and demister column for arresting water carry over will be provided to the incinerator. Online pollutant monitoring shall be provided as per CPCB guidelines for monitoring particulate matter, SO₂, NO_x and CO from the incinerator stack. The periodical monitoring of Dioxins and Furans in the Stack emissions shall be carried out.
- (vii) Analysis of Dioxins and Furans shall be done through CSIR – National Institute for Interdisciplinary Science and Technology (NIIST), Thiruvananthapuram or equivalent NABL Accredited laboratory.
- (viii) The project proponents shall adhere to all conditions as prescribed in the Protocol for 'Performance Evaluation and Monitoring of the Common Hazardous Waste Treatment, Storage and Disposal Facilities' published by the CPCB in May, 2010.
- (ix) Incinerator shall be designed as per CPCB guidelines. Energy shall be recovered from incinerator.

- (x) Sufficient number of Piezometer wells shall be installed in and around the project site to monitor the ground water quality in consultation with the State Pollution Control Board / CPCB. Trend analysis of ground water quality shall be carried out each season and information shall be submitted to the SPCB and the Regional Office of MoEF&CC.
- (xi) Ambient air quality monitoring shall be carried out in and around the landfill site at up wind and downwind locations.
- (xii) The depth of the land fill site shall be decided based on the ground water table at the site and may be such as permitted by the Pollution Control Board.
- (xiii) Environmental Monitoring Programme shall be implemented as per EIA report and guidelines prescribed by CPCB for hazardous waste facilities. Periodical ground water/soil monitoring to check the contamination in and around the site shall be carried out.
- (xiv) The Company shall ensure proper handling of all spillages by introducing spill control procedures for various chemicals.
- (xv) On line real time continuous monitoring facilities shall be provided as per the CPCB or State Board Directions.
- (xvi) No non hazardous wastes, as defined under the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016, shall be handled in the premises.
- (xvii) Gas generated in the Land fill should be properly collected, monitored and flared.
- (xviii) Project Proponent shall develop green belt with native plant species that are significant and used for the pollution abatement. At least 10 m thick greenbelt shall be developed in the periphery of hazardous waste facility.
- (xix) Project should ensure that the site is properly cordoned off from general movement and no unauthorized person or goods permitted to enter the premises. Necessary security provision should be made as a condition in the Authorization under the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016 to prevent unwanted access.
- (xx) Pre medical check-up to be carried out on workers at the time of employment and regular medical record to be maintained.
- (xxi) Emergency plan shall be drawn in consultation with SPCB/CPCB and implemented in order to minimize the hazards to human health or environment from fires, explosion or any unplanned sudden or non sudden release of hazardous waste or hazardous waste constituents to air, soil or surface water.
- (xxii) Rain water runoff from the landfill area and other hazardous waste management area shall be collected and treated in the effluent treatment plant.
- (xxiii) The Project proponent shall not store the Hazardous Wastes more than the quantity that has been permitted by the CPCB/SPCB.
- (xxiv) As per the Ministry's Office Memorandum F.No. 22-65/2017-IA.III dated 1st May 2018, and as proposed, a fund of Rs. 0.40 Crore @ 1% of project Cost, shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as sanitation, solid waste management and rain water harvesting etc. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER

shall be treated as project and shall be monitored. The monitoring report shall be submitted to the regional office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.

PART B - GENERAL CONDITIONS

- (i) A copy of the environmental clearance letter shall also be displayed on the website of the concerned State Pollution Control Board. The EC letter shall also be displayed at the Regional Office, District Industries Centre and Collector's Office/ Tehsildar's office for 30 days.
- (ii) The funds earmarked for environmental protection measures shall be kept in separate account and shall not be diverted for other purpose. Year-wise expenditure shall be reported to this Ministry and its concerned Regional Office.
- (iii) Officials from the Regional Office of MoEF&CC, Bhopal who would be monitoring the implementation of environmental safeguards should be given full cooperation, facilities and documents/data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF&CC shall be forwarded to the APCCF, Regional Office of MoEF&CC, Bhopal.
- (iv) In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.
- (v) The Ministry reserves the right to add additional safeguard measures subsequently, if found necessary, and to take action including revoking of the environment clearance under the provisions of the Environmental (Protection) Act, 1986, to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.
- (vi) All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department, the Forest Conservation Act, 1980 and the Wildlife (Protection) Act, 1972 etc. shall be obtained, as applicable by project proponents from the respective competent authorities.
- (vii) These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and Control of Pollution) Act 1981, the Environment (Protection) Act, 1986, the Public Liability (Insurance) Act, 1991 and the EIA Notification, 2006.
- (viii) The project proponent shall advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded Environmental Clearance and copies of clearance letters are available with the State Pollution Control Board and may also be seen on the website of the Ministry of Environment, Forest and Climate Change at <http://www.envfor.nic.in>. The advertisement shall be made within Seven days from the date of receipt of the Clearance letter and a copy of the same shall be forwarded to the Regional Office of this Ministry at Bhopal.
- (ix) Any appeal against this clearance shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- (x) A copy of the clearance letter shall be sent by the proponent to concerned Panchayat, Zilla Parisad/Municipal Corporation, Urban Local Body and the

Local NGO, if any, from whom suggestions/ representations, if any, were received while processing the proposal. The clearance letter shall also be put on the website of the company by the proponent.

- (xi) The proponent shall upload the status of compliance of the stipulated EC conditions, including results of monitored data on their website and shall update the same periodically. It shall simultaneously be sent to the Regional Office of MoEF&CC, the respective Zonal Office of CPCB and the SPCB. The criteria pollutant levels namely; PM_{2.5}, PM₁₀, SO₂, NO_x (ambient levels as well as stack emissions) or critical sectoral parameters, indicated for the project shall be monitored and displayed at a convenient location near the main gate of the company in the public domain.
- (xii) The environmental statement for each financial year ending 31st March in Form-V as is mandated to be submitted by the project proponent to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently, shall also be put on the website of the company along with the status of compliance of EC conditions and shall also be sent to the respective Regional Offices of MoEF&CC by e-mail.
5. This issues with the approval of the Competent Authority.


(Kushal Vashist)
Director

Copy to:

- 1) The Secretary to Government (Environment and Ecology), Forest, Forests & Environment Department, Government of Gujarat Block 14, 8th Floor, Sachivalaya, Gandhinagar - 382 010, Gujarat.
- 2) The Addl. Principal Chief Conservator of Forests (Central) Ministry of Environment, Forest and Climate Change, Regional Office (WZ) E-5, Kendriya Paryavaran Bhawan, E-5 Arera Colony, Link Road-3 Ravishankar Nagar, Bhopal - 462016.
- 3) The Chairman, Central Pollution Control Board Parivesh Bhavan, CBD-cum-Office Complex, East Arjun Nagar, New Delhi - 110 032.
- 4) The Member Secretary, Gujarat Pollution Control Board, Paryavaran Bhavan, Sector-10A, Gandhinagar-382010, Gujarat.
- 5) Monitoring Cell, MoEF&CC, Indira Paryavaran Bhavan, New Delhi.
- 6) Guard File/ Record File/ Notice Board.
- 7) MoEF&CC website.


(Kushal Vashist)
Director

ଓଡ଼ିଶାର ସମସ୍ତ ଅଞ୍ଚଳରେ ଉପଲବ୍ଧ ଡିଜିଟାଲ ଡିଲିଭରୀ

ଓଡ଼ିଶାର ସମସ୍ତ ଅଞ୍ଚଳରେ ଉପଲବ୍ଧ ଡିଜିଟାଲ ଡିଲିଭରୀ

ଓଡ଼ିଶାର ସମସ୍ତ ଅଞ୍ଚଳରେ ଉପଲବ୍ଧ ଡିଜିଟାଲ ଡିଲିଭରୀ



ଓଡ଼ିଶାର ସମସ୍ତ ଅଞ୍ଚଳରେ ଉପଲବ୍ଧ ଡିଜିଟାଲ ଡିଲିଭରୀ

SANDESH

FRIDAY, 21•12•2018

ପଦା ସୂଚ୍ୟା

ନର୍ମଦା ଜିଲ୍ଲା-୧୧୦୩, ଶାଠଲୀଖୋଲା ଶିକ୍ଷାଧିକାରୀ ଓ ଅଧିକାରୀ

ଶାଠଲୀଖୋଳା ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ



ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

Table with columns for movie title, genre, and showtimes. Includes 'INNOX' logo.

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

ଝଙ୍କରକୁମ୍ଭୀର ନିର୍ଦ୍ଦେଶକାଳୟ ଓ ଅଧିକାରୀ

